

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Roso Cost Num	% Complet	Gantt Chart											
									Task 1, 2019	Task 1, 2020	Task 1, 2020	Task 1, 2021	Task 1, 2021	Task 1, 2022	Task 1, 2022	Task 1, 2023	Task 1, 2023	Task 1, 2024	Task 1, 2024	
1		Construcción de Depósitos Reguladores, Estación de Bombeo y Línea de Impulsión en Aterredado Cambita	1852.3 days?	Mon 09/12/19	Wed 13/12/23		\$31,985,411.87	92%	[Gantt Chart for Task 1: 09/12 to 13/12/23]											
2		Obra Cambita Pucelcoito	0 days	Mon 09/12/19	Mon 09/12/19		\$0.00	0%	[Gantt Chart for Task 2: 09/12/19 to 09/12/19]											
3		Tramo Línea Matriz desde Depósito Regulador 08"	33 days?	Mon 09/12/19	Thu 23/01/20	E	\$2,975,545.67	99%	[Gantt Chart for Task 3: 09/12/19 to 23/01/20]											
4		Compasento	10 days	Mon 09/12/19	Fri 20/12/19		\$0.00	100%	[Gantt Chart for Task 4: 09/12/19 to 20/12/19]											
5		Replanteo y Control Topográfico	30 days	Thu 12/12/19	Thu 23/01/20	455+3 days	\$5,504.85	100%	[Gantt Chart for Task 5: 12/12/19 to 23/01/20]											
6		Movimiento de tierra	15 days	Sat 14/12/19	Thu 09/01/20	555+3 days	\$1,180,105.17	100%	[Gantt Chart for Task 6: 14/12/19 to 09/01/20]											
7		Suministro de tubería y piezas	24 days	Thu 19/12/19	Thu 23/01/20	555+4 days	\$1,009,214.64	100%	[Gantt Chart for Task 7: 19/12/19 to 23/01/20]											
8		Colocación de tubería y piezas	15 days	Tue 21/12/19	Thu 23/01/20	755+5 days	\$564,944.18	100%	[Gantt Chart for Task 8: 21/12/19 to 23/01/20]											
9		Incremento	1 day?	Thu 23/01/20	Thu 23/01/20	SFF	\$399,312.28	100%	[Gantt Chart for Task 9: 23/01/20 to 23/01/20]											
10		Limpieza Continua y final	3 days	Mon 20/01/20	Thu 23/01/20	SFF	\$16,514.55	95%	[Gantt Chart for Task 10: 20/01/20 to 23/01/20]											
11		Depósito Regulador de 700 M3	609.5 days?	Sat 14/12/19	Fri 08/04/22	D2	\$8,256,103.06	99%	[Gantt Chart for Task 11: 14/12/19 to 08/04/22]											
12		Replanteo y Control Topográfico	3 days	Sat 14/12/19	Tue 17/12/19	555+3 days	\$20,000.00	100%	[Gantt Chart for Task 12: 14/12/19 to 17/12/19]											
13		Inicio Estudio de Suelo	4 days	Tue 17/12/19	Sat 21/12/19	1255+3 days	\$0.00	100%	[Gantt Chart for Task 13: 17/12/19 to 21/12/19]											
14		Movimiento de tierra	20 days	Mon 23/12/19	Mon 20/01/20	13	\$507,947.22	100%	[Gantt Chart for Task 14: 23/12/19 to 20/01/20]											
15		Acondicionamiento de Camino	1 day?	Mon 23/12/19	Mon 23/12/19	G	\$49,601.20	100%	[Gantt Chart for Task 15: 23/12/19 to 23/12/19]											
16		Hormigones Armados FC=280 kg/cm2	419.5 days	Tue 14/01/20	Mon 16/08/21	1455+15 days	\$5,725,223.15	100%	[Gantt Chart for Task 16: 14/01/20 to 16/08/21]											
17		Terminaciones de Superficie	55.5 days	Wed 19/02/20	Thu 31/03/22	1555+27 days	\$55,450.81	100%	[Gantt Chart for Task 17: 19/02/20 to 31/03/22]											
18		Aplicaciones de banda impermeabilizante	59.5 days	Tue 21/12/19	Fri 05/04/22	1455+6 days	\$17,210.34	100%	[Gantt Chart for Task 18: 21/12/19 to 05/04/22]											
19		Construcción entubada y rebosa y by pass	5 days	Wed 29/01/20	Mon 17/02/20	1555+11 days	\$99,311.34	100%	[Gantt Chart for Task 19: 29/01/20 to 17/02/20]											
20		Movimiento de tierra	4 days	Thu 13/02/20	Tue 18/02/20	1555+23 days	\$20,374.33	100%	[Gantt Chart for Task 20: 13/02/20 to 18/02/20]											
21		Suministro y colocación de escalera y tarax	55.5 days	Sat 22/02/20	Fri 01/04/22	1755+3 days	\$55,000.00	100%	[Gantt Chart for Task 21: 22/02/20 to 01/04/22]											
22		Verja de Malla Cíclica	57.5 days	Wed 23/01/20	Fri 01/04/22	1555+5 days	\$47,432.67	100%	[Gantt Chart for Task 22: 23/01/20 to 01/04/22]											
23		Caseta de Materiales	3 days	Sat 14/12/19	Tue 17/12/19	1255	\$30,000.00	100%	[Gantt Chart for Task 23: 14/12/19 to 17/12/19]											
24		Embelladamiento con Gravel	3 days	Tue 17/03/20	Tue 05/04/22	17	\$27,170.00	100%	[Gantt Chart for Task 24: 17/03/20 to 05/04/22]											
25		Limpieza final	3 days	Fri 20/03/20	Thu 07/04/22	24	\$15,000.00	100%	[Gantt Chart for Task 25: 20/03/20 to 07/04/22]											
26		Caseta de Cloración	45 days	Tue 01/03/22	Mon 02/04/22	J	\$1,861,080.29	10%	[Gantt Chart for Task 26: 01/03/22 to 02/04/22]											
27		Caseta de Closo	45 days	Tue 01/03/22	Mon 02/04/22		\$1,861,080.39	10%	[Gantt Chart for Task 27: 01/03/22 to 02/04/22]											
28		Red de Distribución G1" y G4"	625.65 days?	Fri 20/03/20	Tue 10/05/22	F	\$3,679,281.96	90%	[Gantt Chart for Task 28: 20/03/20 to 10/05/22]											
29		Replanteo y Control Topográfico	3 days	Fri 20/12/19	Fri 08/04/22	25	\$5,677.75	100%	[Gantt Chart for Task 29: 20/12/19 to 08/04/22]											
30		Movimiento de tierra	15 days	Thu 26/12/19	Mon 23/04/22	29	\$1,116,916.87	95%	[Gantt Chart for Task 30: 26/12/19 to 23/04/22]											
31		Suministro de tubería y piezas	15 days	Sat 28/12/19	Wed 27/04/22	3077+3 days	\$48,594.68	95%	[Gantt Chart for Task 31: 28/12/19 to 27/04/22]											

Robina E. Pedrono

Project: CONSTRUCCION DPO
 Date: Mon 02/04/23


Task Summary: [Blue bar] Inactive Milestone: [Grey bar] Duration only: [Light blue bar] Start-only: [Light blue bar] External Milestone: [Light blue bar] Critical Spd: [Red dotted bar]

Task Summary: [Blue bar] Inactive Milestone: [Grey bar] Manual Summary (Full): [Light blue bar] End-only: [Light blue bar] Define: [Light blue bar] Progress: [Blue bar]

Milestone: [Blue diamond] Inactive Task: [Grey bar] Manual Task: [Light blue bar] External Links: [Light blue bar] Critical: [Red bar] Manual Progress: [Blue bar]

Page 1

Robina E Pedrono

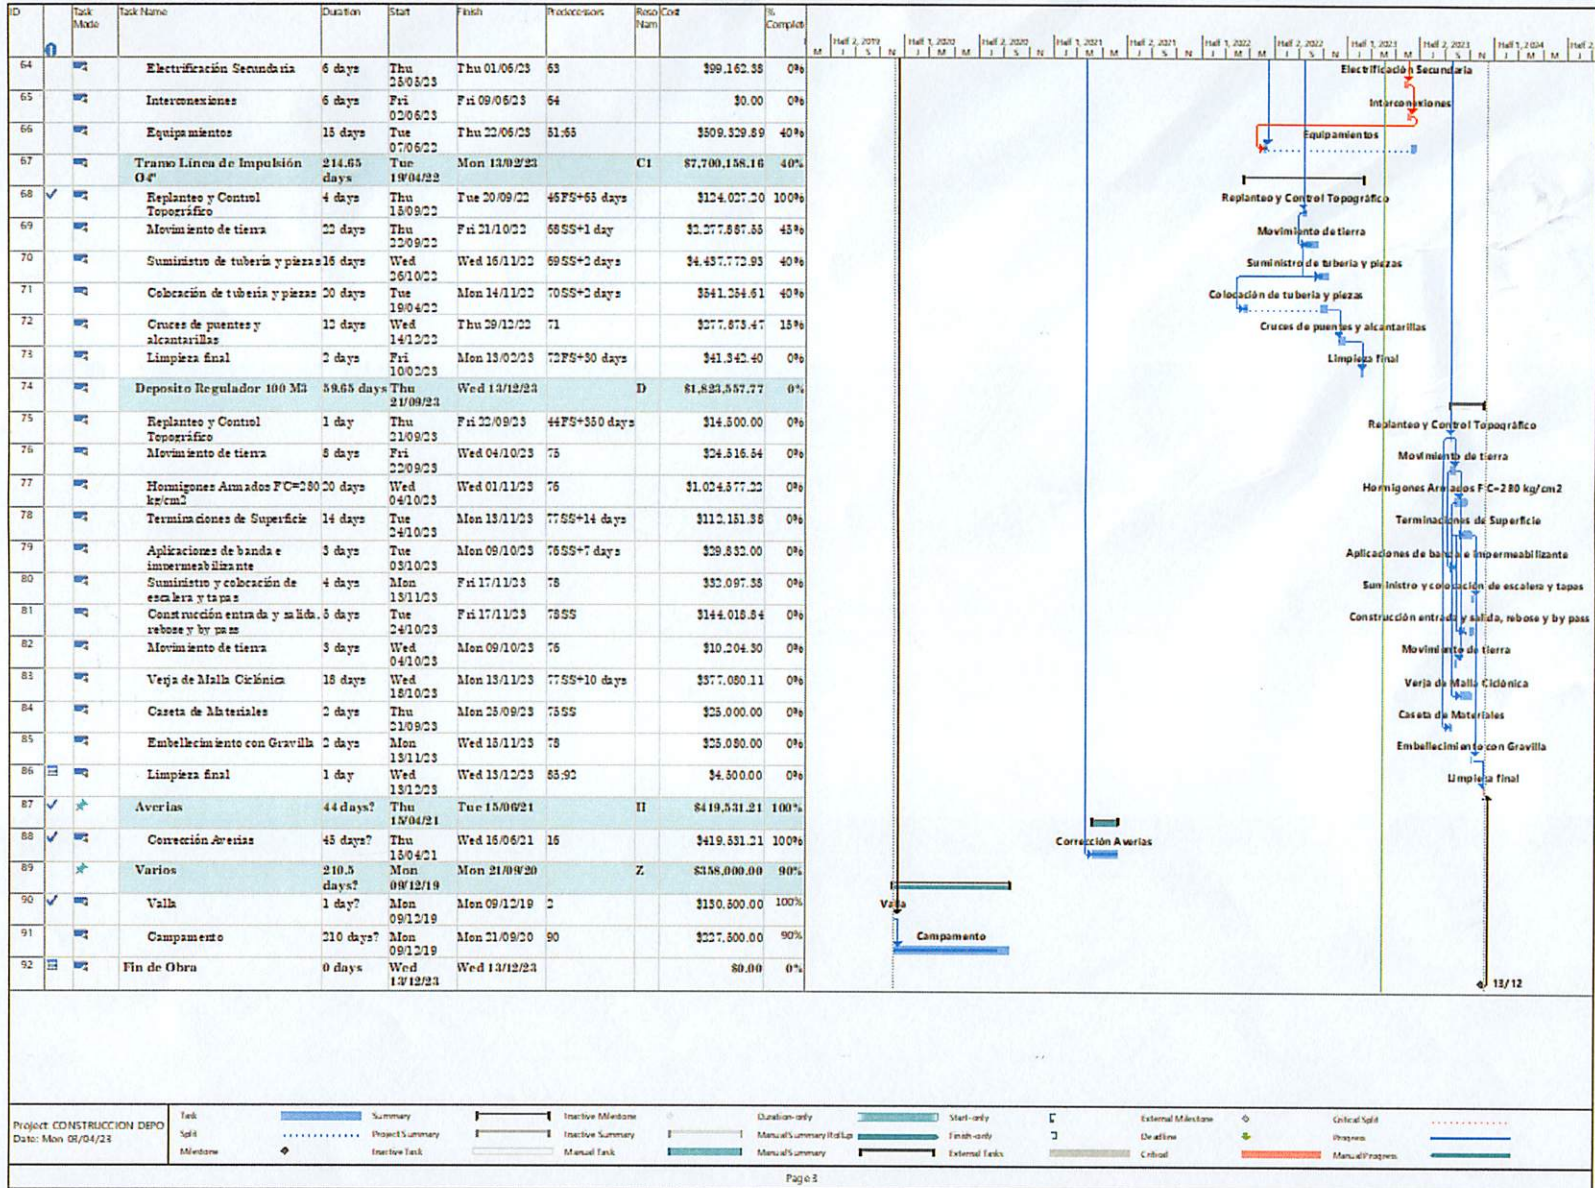

Project CONSTRUCCION DEPO
Date: Mon 05/04/23



