

0	Task Mode	Task Name	Duration	Start	Finish	Feb 4, '18	Feb 11, '18	Feb 18, '18
1	Task Mode	Task Name	Duration	Start	Finish	S S M T W T F S	S S M T W T F S	S S M T W T F S
	Task	Inicio del Proyecto	54 days	M 2/5/18	S 4/7/18			
2	Task	CAJUELA EXISTENTE UBICADA EN ARROYO CANADA	3 days	M 2/5/18	W 2/7/18			
3	Task	LIMPIEZA DE CAJUELA	3 days	M 2/5/18	W 2/7/18			
4	Task	TRAMO LINEA DE ADUCCION ARROYO CANADA HONDA	41 days	M 2/5/18	S 3/24/18			
5	Task	REPLANTEO	2 days	M 2/5/18	T 2/6/18			
6	Task	MOVIMIENTO DE TIERRA	33 days	W 2/7/18	S 3/17/18			
7	Task	SUMINISTRO Y COLOCACION DE TUBERIAS	18 days	T 3/1/18	T 3/22/18			
8	Task	CONFESION DE ANCLAJES	10 days	T 3/1/18	T 3/13/18			
9	Task	SUMINISTRO Y COLOCACION DE TUB. ESPECIALES	3 days	M 3/19/18	T 3/22/18			
10	Task	SUMINISTRO Y COLOCACION DE VALVULAS	3 days	M 3/19/18	T 3/22/18			
11	Task	CONFESION DE REGISTROS	5 days	M 3/12/18	S 3/17/18			



Project: Cronograma 038  
Date: W 1/3/18

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone →	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

D	Task Mode	Task Name	Duration	Start	Finish	Feb 4, '18					Feb 11, '18					Feb 18, '18				
						S	S	M	T	W	T	F	S	S	S	M	T	W	T	F
12		PRUEBAS HIDROESTATICAS	2 days	T 3/22/18	S 3/24/18															
13		CAJUELA EXISTENTE UBICADA EN NORIA EN UN LATERAL RIO SITO	2 days	T 2/8/18	F 2/9/18															
14		LIMPIEZA DE CAJUELA	2 days	T 2/8/18	F 2/9/18															
15		TRAMO LINEA DE ADUCCION D/CAJUELA EN NORIA A RIO SITO	15 days	S 3/17/18	T 4/3/18															
16		REPLANTEO	2 days	S 3/17/18	T 3/20/18															
17		MOVIMIENTO DE TIERRA	9 days	T 3/20/18	F 3/30/18															
18		SUMINISTRO Y COLOCACION DE TUBERIAS	11 days	T 3/20/18	S 3/31/18															
19		CONFESION DE ANCLAJES	11 days	T 3/20/18	S 3/31/18															
20		SUMINISTRO Y COLOCACION DE TUB. ESPECIALES	10 days	T 3/20/18	S 3/31/18															
21		SUMINISTRO Y COLOCACION DE VALVULAS	10 days	T 3/20/18	S 3/31/18															
22		CONFESION DE REGISTROS	10 days	T 3/20/18	S 3/31/18															

*Handwritten signature*

Project: Cronograma 038  
Date: W 1/3/18

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

D	Task Mode	Task Name	Duration	Start	Finish	Feb 4, '18							Feb 11, '18							Feb 18, '18																						
						S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T																	
23		PRUEBAS HIDROESTATICAS	3 days	S 3/31/18	T 4/3/18																																					
24		LINEA DE ADUCCION D/ ARROYO PLATON	6 days	S 3/31/18	F 4/6/18																																					
25		REPLANTEO	1 day	W 4/4/18	W 4/4/18																																					
26		SUMINISTRO Y COLOCACION DE TUBERIAS	4 days	S 3/31/18	W 4/4/18																																					
27		CONFESION DE ANCLAJES	4 days	S 3/31/18	W 4/4/18																																					
28		PRUEBA HIDROESTATICA	2 days	T 4/5/18	F 4/6/18																																					
29		LIMPIEZA FINAL	1 day	S 4/7/18	S 4/7/18																																					
30		LIMPIEZA FINAL Y CONTINUA	1 day	S 4/7/18	S 4/7/18																																					

*Handwritten signature*

Project: Cronograma 038 Date: W 1/3/18	Task		Inactive Summary		External Tasks
	Split		Manual Task		External Milestone
	Milestone		Duration-only		Deadline
	Summary		Manual Summary Rollup		Progress
	Project Summary		Manual Summary		Manual Progress
	Inactive Task		Start-only		
	Inactive Milestone		Finish-only		

Feb 25, '18							Mar 4, '18							Mar 11, '18							Mar 18, '18							Mar 25, '18							Apr 1, '18							Apr 8, '18								
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S

Project: Cronograma 038 Date: W 1/3/18	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

*(Handwritten signature)*




- ▶ [Faint text]
- ▶ [Faint text]
- ▶ [Faint text]
- ▶ [Faint text]
- ▶ [Faint text]
- ▶ [Faint text]

*Handwritten signature*

Project: Cronograma 038 Date: W 1/3/18	Task	Inactive Summary	External Tasks
	Split	Manual Task	External Milestone
	Milestone	Duration-only	Deadline
	Summary	Manual Summary Rollup	Progress
	Project Summary	Manual Summary	Manual Progress
	Inactive Task	Start-only	
	Inactive Milestone	Finish-only	

Feb 25, '18      Mar 4, '18      Mar 11, '18      Mar 18, '18      Mar 25, '18      Apr 1, '18      Apr 8, '18

F S S M T W T F S    S M T W T F S    S M T W T F S    S M T W T F S    S M T W T F S    S M T W T F S    S M T W T F S

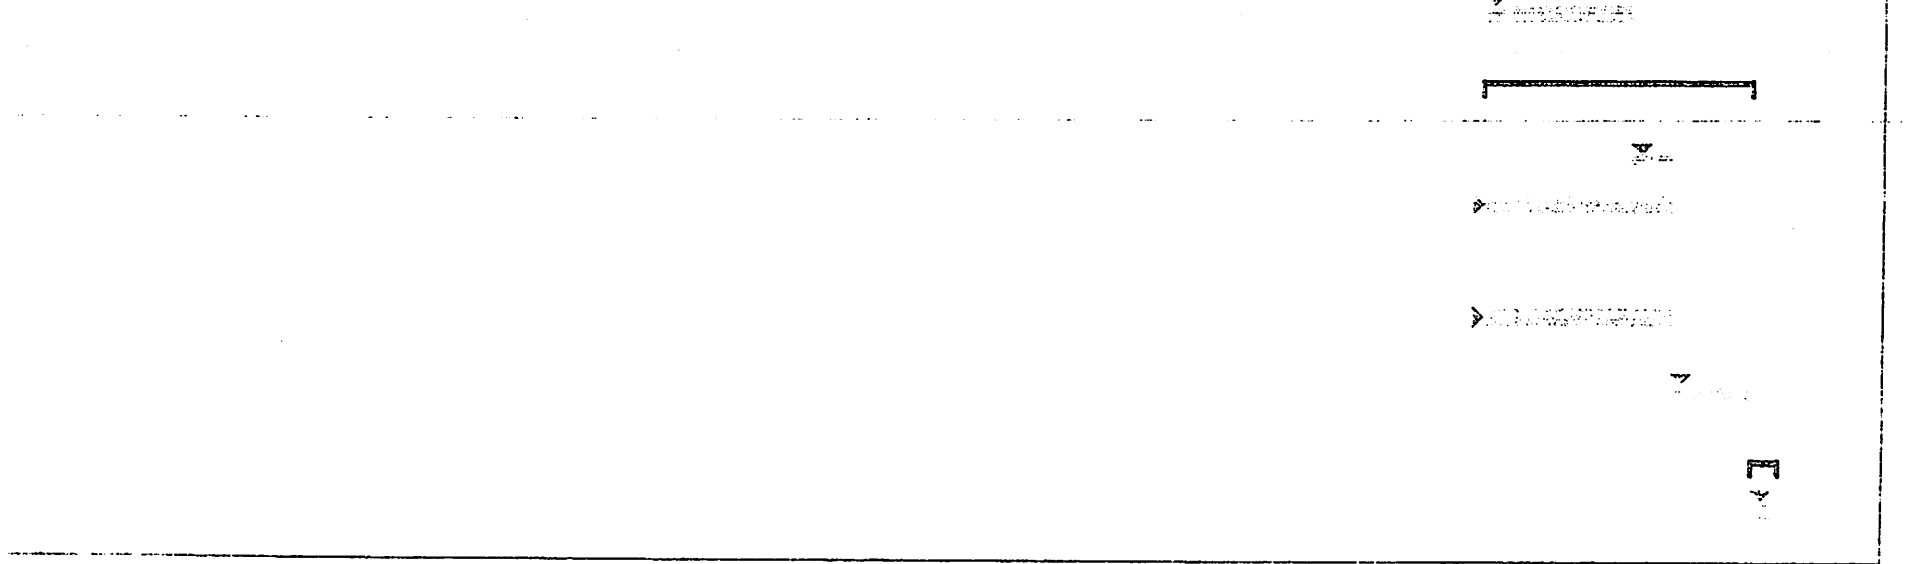

*Handwritten signature*

Project: Cronograma 038 Date: W 1/3/18	Task	Inactive Summary	External Tasks
	Split	Manual Task	External Milestone
	Milestone	Duration-only	Deadline
	Summary	Manual Summary Rollup	Progress
	Project Summary	Manual Summary	Manual Progress
	Inactive Task	Start-only	
	Inactive Milestone	Finish-only	
