


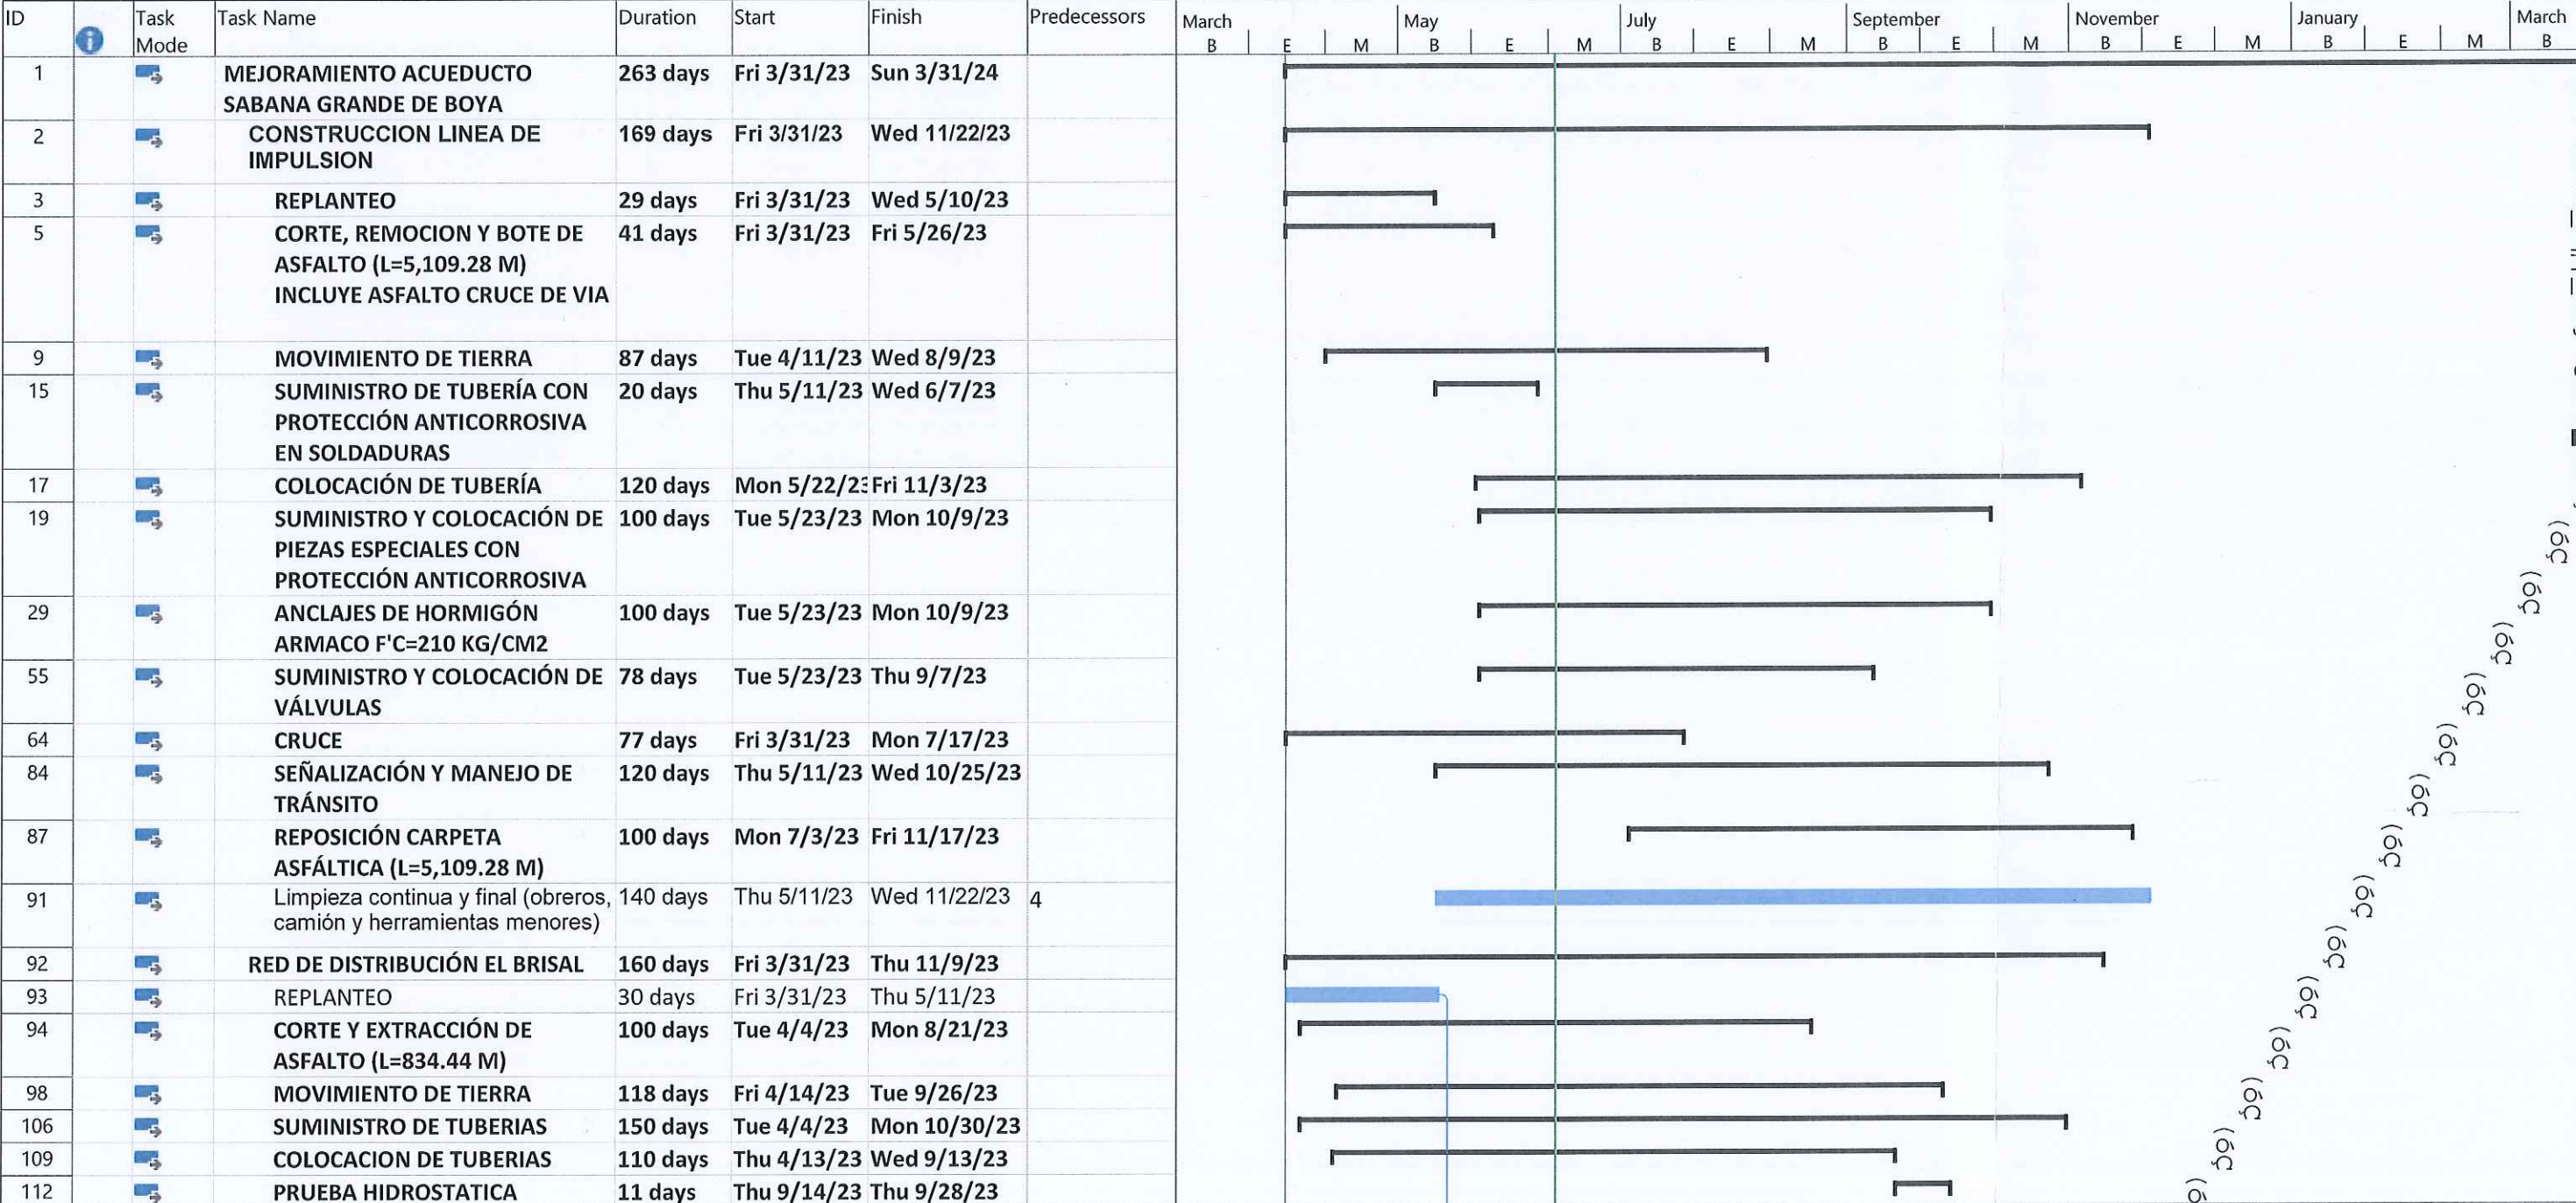

Project: INAPA SABANA GRANDE
Date: Tue 6/13/23

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split


Progress

Manual Progress

CONSTRUCTORA ALFAU, S.R.L.

Santo Domingo, D.D.N.

República Dominicana

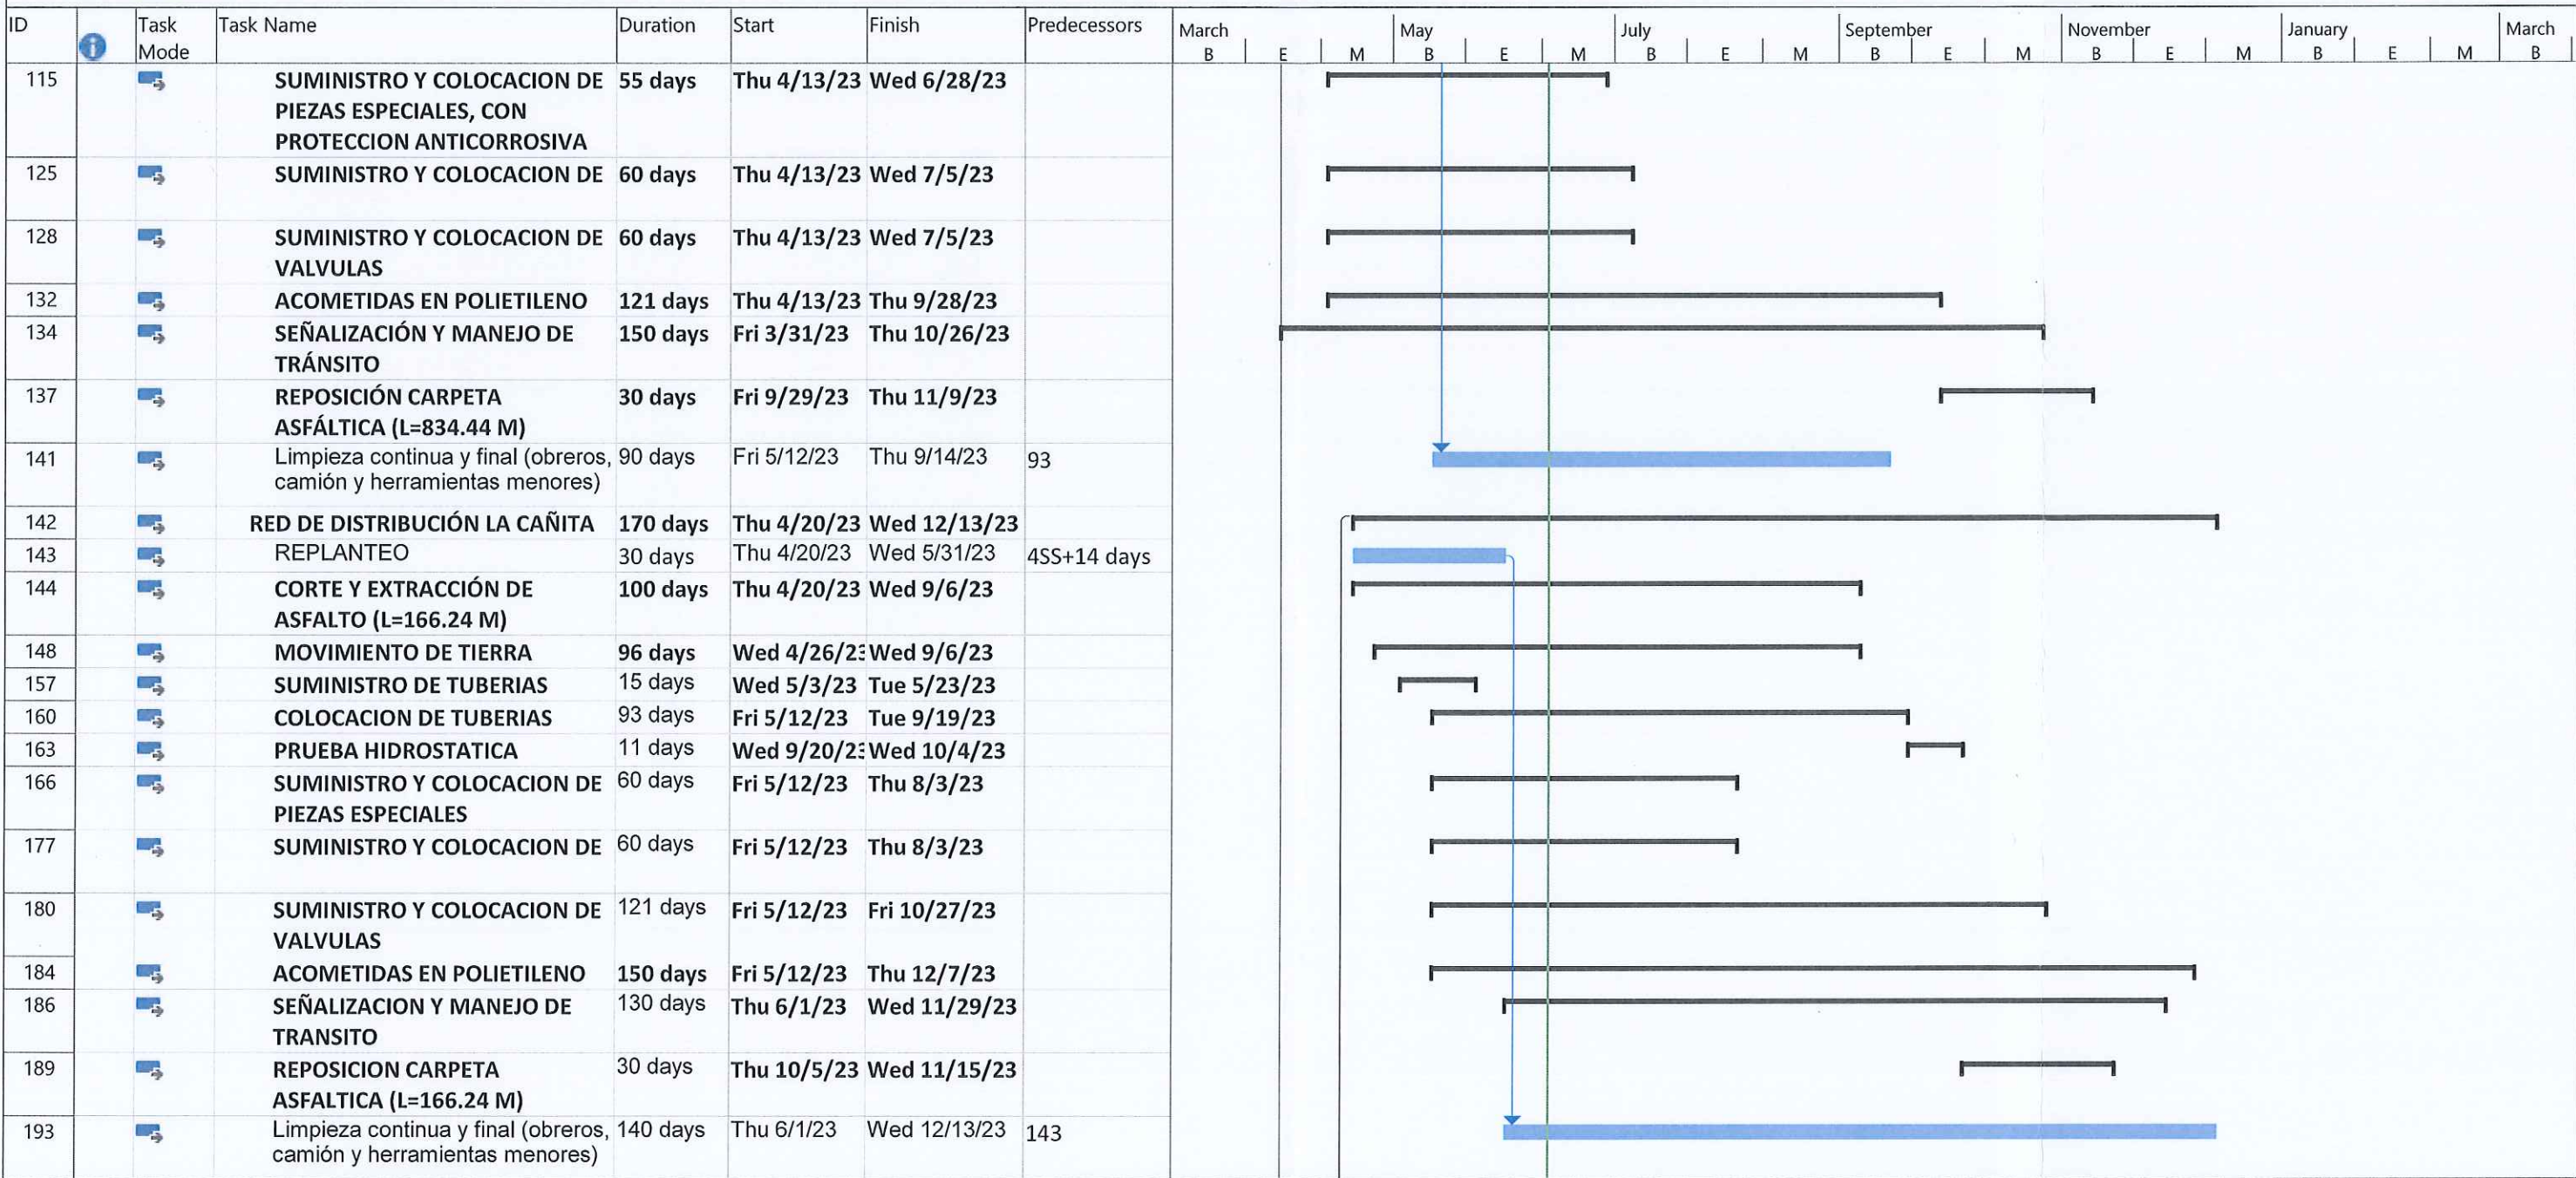

Project: INAPA SABANA GRANDE
Date: Tue 6/13/23

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress


Manual Progress

CONSTRUCTORA ALFAU, S.R.L.

Santo Domingo, D.N.

República Dominicana

Page 2

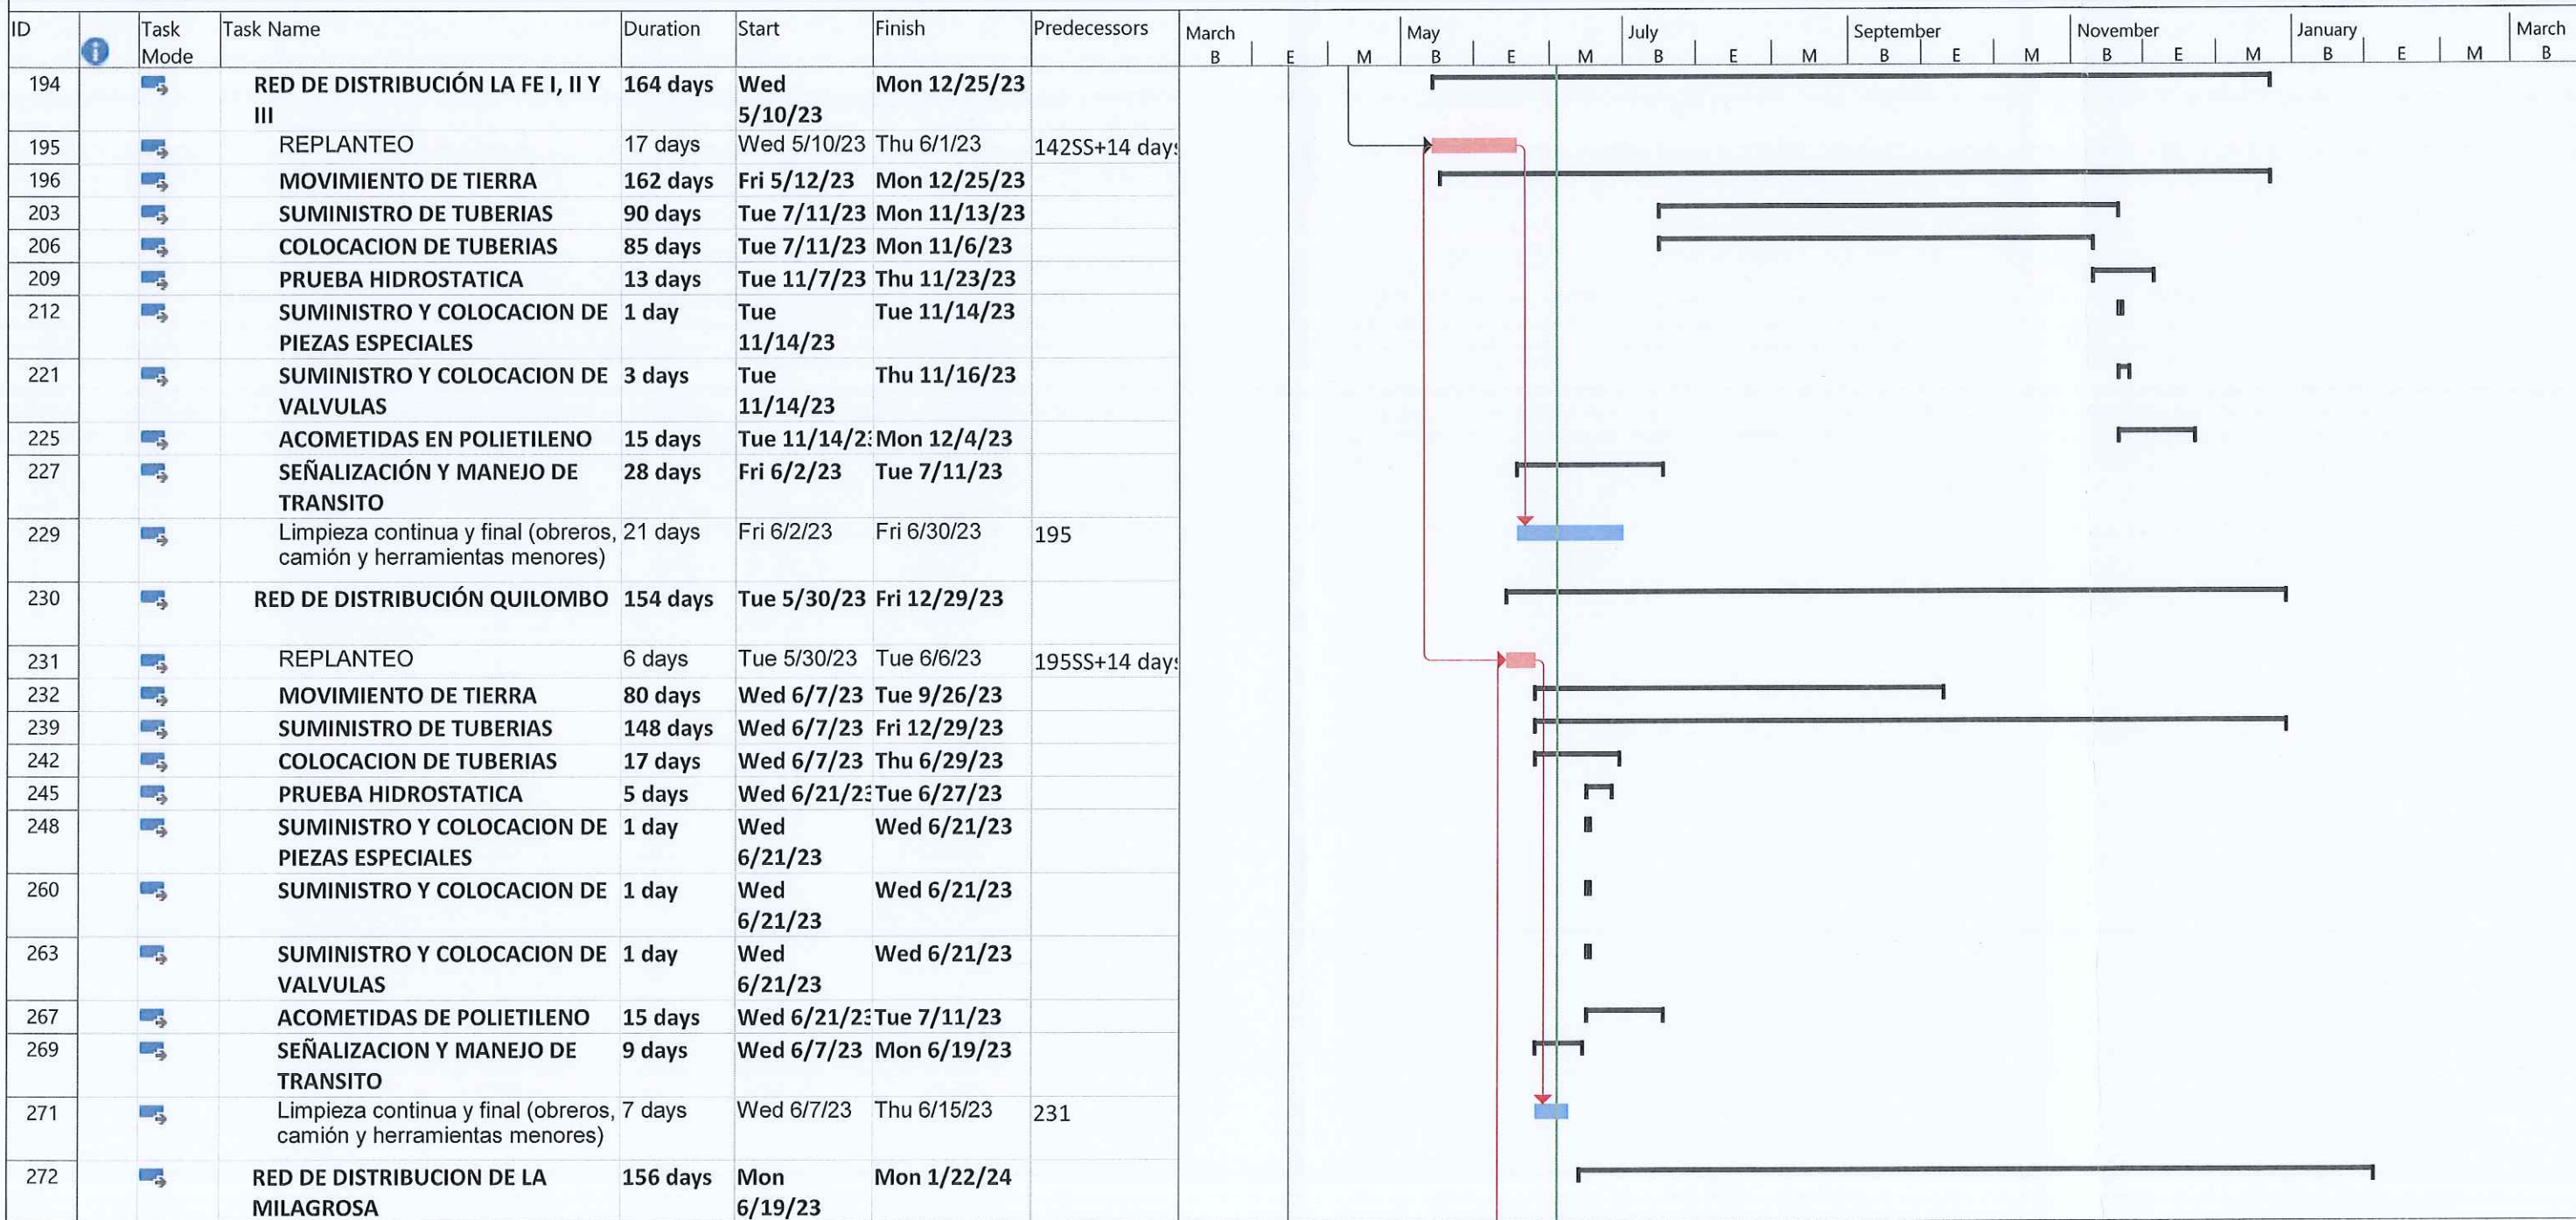

Project: INAPA SABANA GRANDE
Date: Tue 6/13/23

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone


Deadline

Critical

Critical Split

Progress

Manual Progress

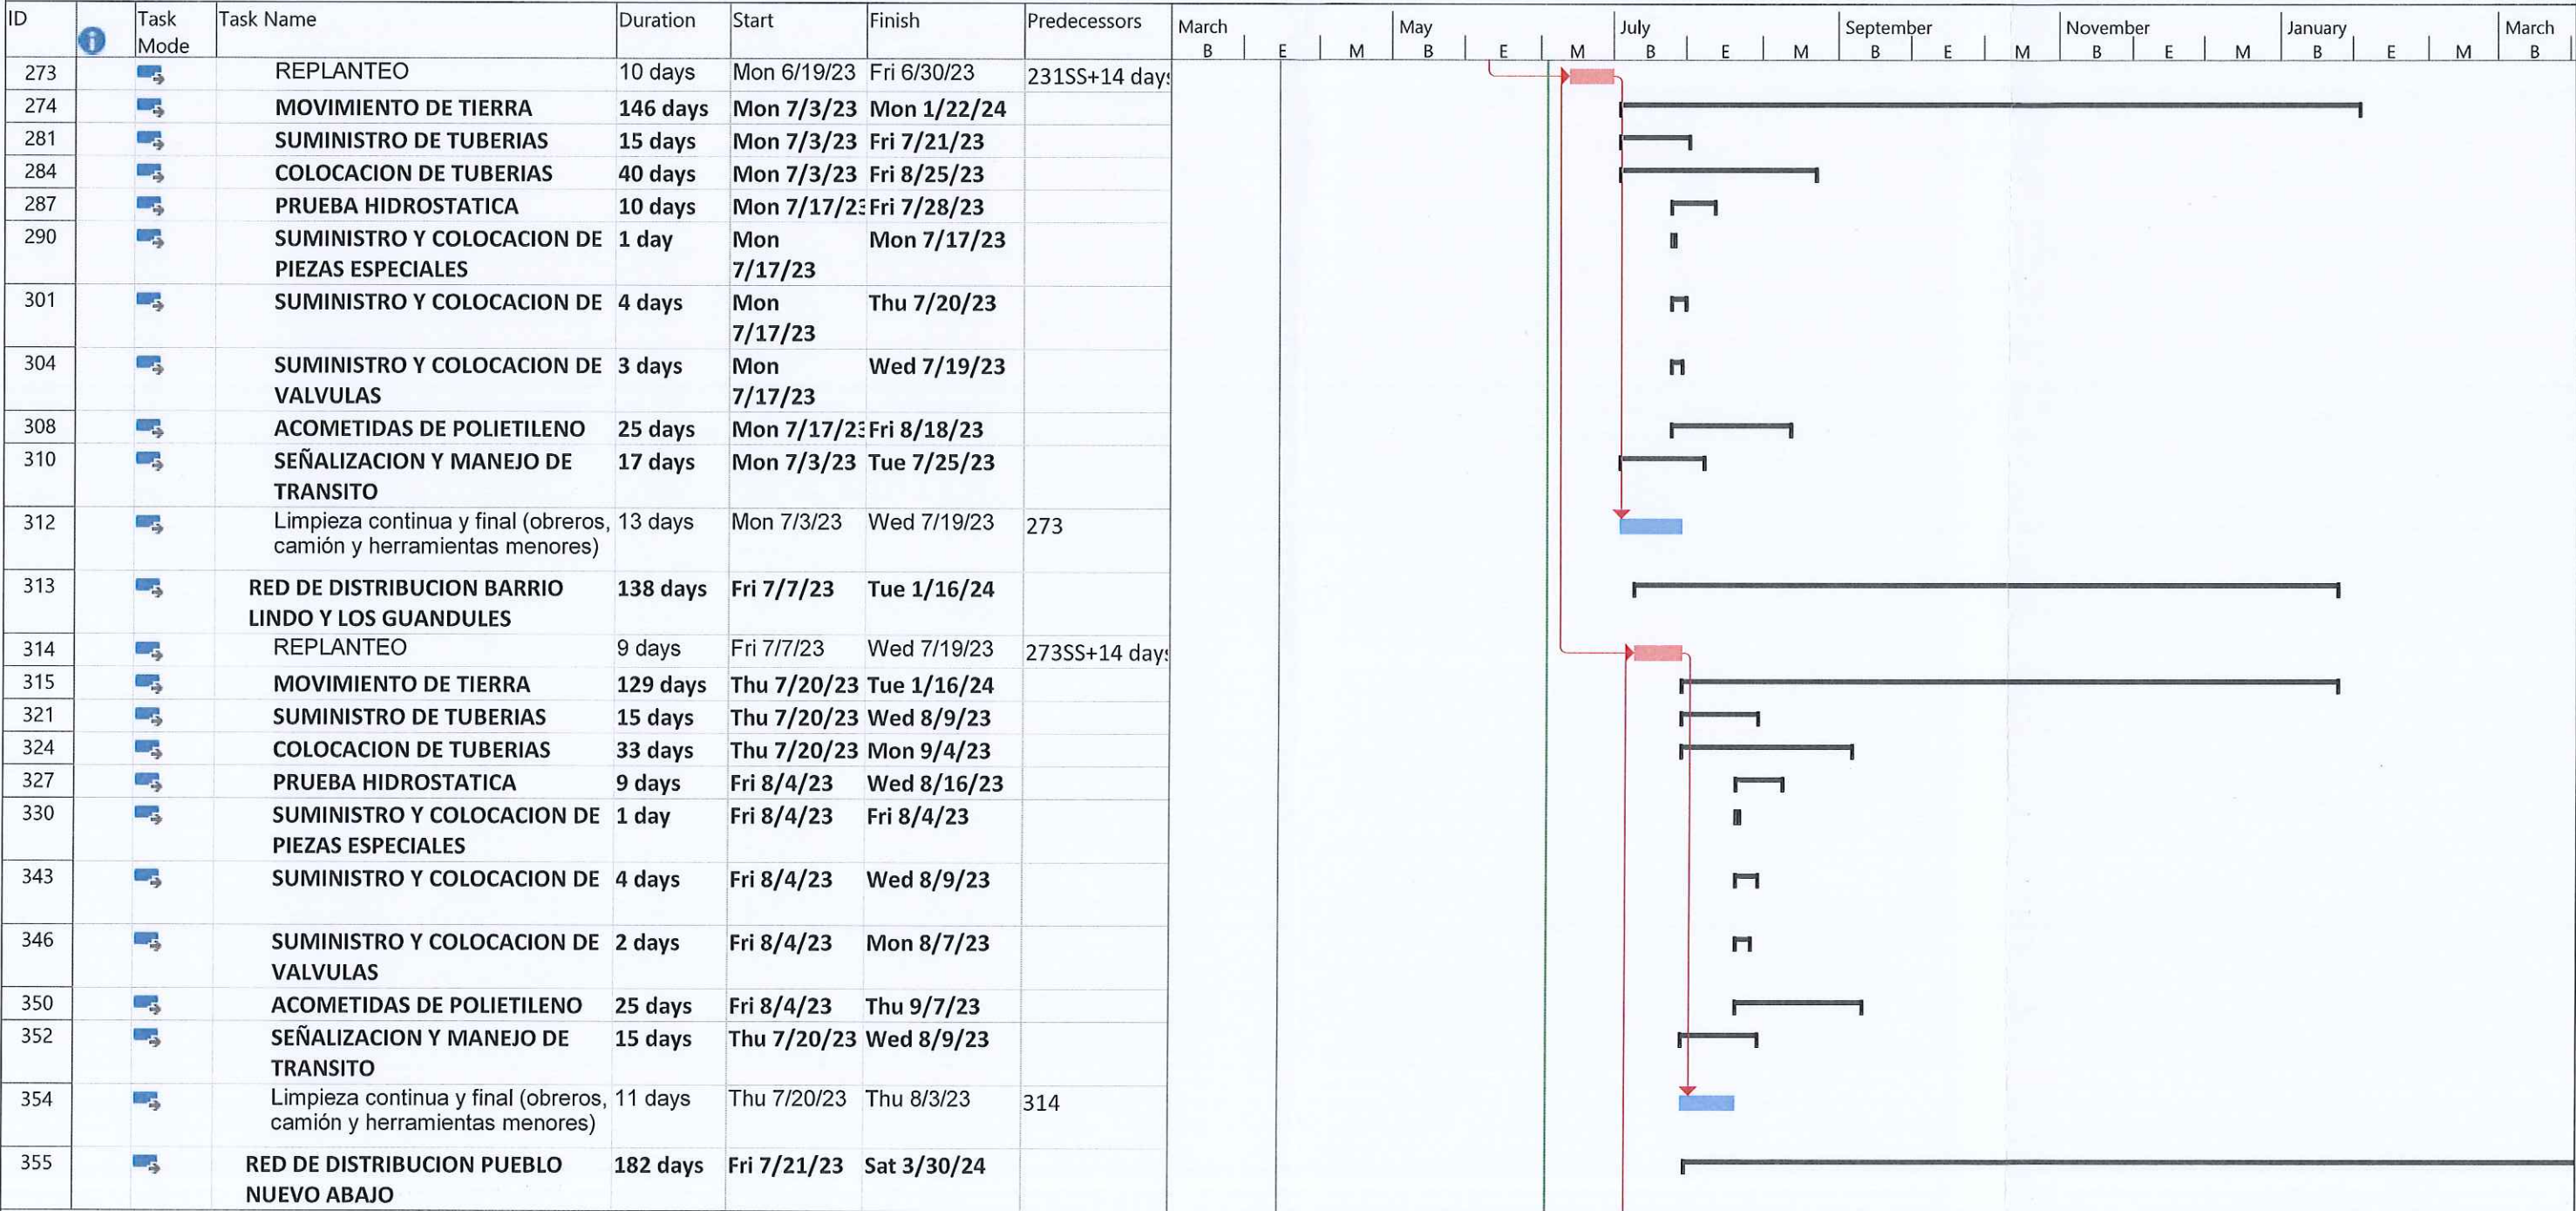

Project: INAPA SABANA GRANDE
Date: Tue 6/13/23

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

CONSTRUCTORA ALFAU, S.R.L.

Santo Domingo, D.N.

República Dominicana

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	March			May			July			September			November			January			March
							B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B
356		REPLANTEO	30 days	Fri 7/21/23	Thu 8/31/23	314SS+10 days																			
357		CORTE Y EXTRACCION DE ASFALTO (L=111.60M)	5 days	Fri 9/1/23	Thu 9/7/23																				
361		MOVIMIENTO DE TIERRA	149 days	Wed 9/6/23	Sat 3/30/24																				
368		SUMINISTRO DE TUBERIAS	15 days	Wed 9/6/23	Tue 9/26/23																				
371		COLOCACION DE TUBERIAS	80 days	Wed 9/6/23	Tue 12/26/23																				
374		PRUEBA HIDROSTATICA	27 days	Wed 12/27/23	Thu 2/1/24																				
377		SUMINISTRO Y COLOCACION DE PIEZAS ESPECIALES	1 day	Wed 12/27/23	Wed 12/27/23																				
389		SUMINISTRO Y COLOCACION DE	4 days	Wed 12/27/23	Mon 1/1/24																				
394		SUMINISTRO Y COLOCACION DE VALVULAS	6 days	Wed 12/27/23	Wed 1/3/24																				
398		ACOMETIDAS DE POLIETILENO	65 days	Wed 12/27/23	Tue 3/26/24																				
400		SEÑALIZACION Y MANEJO DE TRANSITO	50 days	Fri 9/1/23	Thu 11/9/23																				
402		REPOSICION CARPETA ASFALTICA (L=111.60 M)	3 days	Wed 12/27/23	Fri 12/29/23																				
406		Limpieza continua y final (obreros, camión y herramientas menores)	50 days	Mon 1/1/24	Fri 3/8/24	405																			
407		RED DE DISTRIBUCION VISTA HERMOSA Y BARRIO DEPORTIVO	176 days	Tue 8/1/23	Sun 3/31/24																				
408		REPLANTEO	45 days	Tue 8/1/23	Mon 10/2/23	356SS+7 days																			
409		CORTE Y EXTRACCION DE ASFALTO (L=867.71 M)	26 days	Tue 10/3/23	Tue 11/7/23																				
413		MOVIMIENTO DE TIERRA	80 days	Tue 10/3/23	Mon 1/22/24																				
421		SUMINISTRO DE TUBERIAS	15 days	Tue 10/3/23	Mon 10/23/23																				
424		COLOCACION DE TUBERIAS	80 days	Tue 10/3/23	Mon 1/22/24																				
427		PRUEBA HIDROSTATICA	45 days	Tue 1/23/24	Mon 3/25/24																				
430		SUMINISTRO Y COLOCACION DE PIEZAS ESPECIALES	80 days	Thu 10/12/23	Wed 1/31/24																				
445		SUMINISTRO Y COLOCACION DE	80 days	Thu 10/12/23	Wed 1/31/24																				
449		SUMINISTRO Y COLOCACION DE VALVULAS	80 days	Thu 10/12/23	Wed 1/31/24																				
453		ACOMETIDA DE POLIETILENO	63 days	Thu 10/12/23	Mon 1/8/24																				

Project: INAPA SABANA GRANDE
Date: Tue 6/13/23

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

CONSTRUCTORA ALFAU, S.R.L.

Santo Domingo, D.N.

República Dominicana

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	March			May			July			September			November			January			March
							B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B	E	M	B
455		SEÑALIZACION Y CONTROL DE TRANSITO	176 days	Tue 8/1/23	Sun 3/31/24																				
458		REPOSICION CARPETA ASFALTICA (L=867.71 M)	11 days	Tue 1/23/24	Tue 2/6/24																				
462		Limpieza continua y final (obreros, camión y herramientas menores)	176 days	Tue 8/1/23	Sun 3/31/24	408SS																			
463		VARIOS	263 days	Fri 3/31/23	Sun 3/31/24																				
464		FABRICACION E INSTALACION DE VALLA (20' X 10') IMPRESIÓN FULL COLOR EN BANNER BLANCO Y NEGRO CON LOGO DE INAPA, NOMBRE DEL CONTRATISTA Y PROYECTO. ESTRUCTURA EN TUBOS GALVANIZADOS 1.5"x 1.5" Y SOPORTES EN TUBO CUADRADO DE 4" X 4"	14 days	Fri 3/31/23	Wed 4/19/23																				
465		CAMPAMENTO (INCLUYE ALQUILER DEL SOLAR CON O SIN CASA, BANOS MOVILES, CASETA DE MATERIALES	263 days	Fri 3/31/23	Sun 3/31/24																				

Project: INAPA SABANA GRANDE
Date: Tue 6/13/23

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline

Critical

Critical Split

Progress

Manual Progress

