


Constructora Montebianco, S.R.L.
RNC: 131-47453-5
Santo Domingo

ID	WBS	Task Name	Duration	Start	Finish	Predecessors	Cost
80	B	ESTACION DE BOMBEO (FASE B)	357 days?	Mon 8/8/22	Tue 19/12/23		\$136,866,173.66
831	C	LINEA DE IMPULSION (FASE C)	500 days?	Tue 1/2/22	Mon 1/1/24		\$188,857,310.91
840	1	Replanteo y control topográfico	5 days	Mon 1/10/22	Fri 7/10/22	81	\$1,410,844.68
841	2	MOVIMIENTO DE TIERRAS	242 days?	Tue 1/2/22	Wed 4/3/23		\$49,586,040.88
842	2.1	Excavación material compactado con equipo zarzán 15 days	15 days	Wed 26/10/22	Tue 15/11/22	866	\$3,809,026.33
843	2.2	Excavación en roca c/ equipo	10 days	Wed 16/11/22	Tue 29/11/22	842	\$7,494,939.18
844	2.3	Asiento de arena	5 days	Fri 9/12/22	Thu 15/12/22	845	\$1,838,501.45
845	2.4	Regularización de zanjas	7 days	Wed 30/11/22	Thu 8/12/22	843	\$350,567.89
846	2.5	Suministro de material de minas dist.+20km	2 days	Mon 28/11/22	Tue 29/11/22	850	\$927,513.23
847	2.6	Relleño compactado c/mat. De excavación	15 days	Thu 15/12/22	Wed 4/1/23	846,860,861,862	\$7,961,268.45
848	2.7	Bote de material c/camión dist.+5km	7 days	Wed 30/11/22	Thu 8/12/22	842,843	\$756,354.79
849	2.8	EXCAVACIÓN EN ROCA DURA C/TRENCHER PARA CONFORMAR EXPLANADA	1 day?	Tue 1/2/22	Tue 1/2/22		\$26,387,879.56
850	4	SUMINISTRO DE TUBERIAS	214 days?	Tue 1/2/22	Fri 25/11/22		\$106,931,211.21
851	4.1	DE Ø 12" PVC SDR 26 C/JG + 4% Perdida por campo 3 days	3 days	Wed 24/11/22	Fri 16/11/22	842	\$16,462,481.09
852	4.2	DE Ø 16" PVC SDR 26 C/JG + 4% Perdida por campo 3 days	3 days	Mon 21/11/22	Wed 23/11/22	851	\$71,119,174.85
853	4.3	DE Ø 20" PVC SDR 26 C/JG + 6% Perdida por campana	2 days	Thu 24/11/22	Fri 25/11/22	852	\$12,715,101.14
854	4.4	DE Ø 8" PVC SDR 26 C/JG + 3 % PERDIDA POR CAMPANA	1 day?	Tue 1/2/22	Tue 1/2/22		\$6,634,454.13
855	5	COLOCACION DE TUBERIAS	13 days	Mon 21/11/22	Wed 7/12/22		\$1,630,160.67
856	5.1	DE Ø 12" PVC SDR 26 C/JG	7 days	Mon 21/11/22	Tue 29/11/22	851	\$327,761.04
857	5.2	DE Ø 16" PVC SDR 26 C/JG	10 days	Thu 24/11/22	Wed 7/12/22	852	\$1,085,058.38
858	5.3	DE Ø 20" PVC SDR 26 C/JG	5 days	Mon 28/11/22	Fri 2/12/22	853	\$217,341.25
859	6	PRUEBA HIDROSTATICA	2 days	Tue 13/12/22	Wed 14/12/22	868	\$1,523,106.40
860	6.1	DE Ø 12" PVC SDR 26 C/JG	2 days	Tue 13/12/22	Wed 14/12/22	856	\$332,141.15
861	6.2	DE Ø 16" PVC SDR 26 C/JG	2 days	Tue 13/12/22	Wed 14/12/22	857	\$1,030,046.60
862	6.3	DE Ø 20" PVC SDR 26 C/JG	2 days	Tue 13/12/22	Wed 14/12/22	858	\$158,918.65
863	7	SUMINISTRO Y COLOCACION DE PIEZAS ESPECIALES	3 days	Thu 8/12/22	Mon 12/12/22	855	\$132,176.42
864	8	ASFALTO 90 % DE LAS LONGITUDES	341 days?	Mon 12/9/22	Mon 1/1/24		\$24,645,770.45
865	8.1	Corte carpeta asfáltica	7 days	Mon 10/10/22	Tue 18/10/22	840	\$8,844,563.86
866	8.2	Extracción carpeta asfáltica	5 days	Wed 19/10/22	Tue 25/10/22	865	\$3,618,718.04
867	8.3	Bote de material c/camión dist.+5km	2 days	Wed 26/10/22	Thu 27/10/22	866	\$156,519.13
868	8.4	Suministro y colocación de asfalto 2"	3 days	Thu 5/1/23	Mon 9/1/23	869,847	\$5,688,858.31
869	8.5	Transporte de asfalto distancia aprox.+57km	2 days	Fri 28/10/22	Mon 31/10/22	867	\$321,837.69
870	9	Control y manejo de tránsito	3 days	Tue 10/1/23	Thu 12/1/23	868	\$412,855.74
871	10	Limpieza final y continua	5 days	Fri 13/1/23	Thu 19/1/23	870	\$356,768.76
872	12	DEMOLICION DE SUELO CEMENTO CON RETRO MARTILLO	1 day?	Fri 20/1/23	Fri 20/1/23		\$1,049,938.34
873	12.1	DEMOLICION DE SUELO CEMENTO CON RETRO MARTILLO	1 day?	Fri 20/1/23	Fri 20/1/23	871	\$1,049,938.34
874	12	EXCAVACION, SUMINISTRO Y COLOCACION DE TUBERIAS Ø20" PVC SDR-26 CAMINO A LA	27 days?	Mon 23/1/23	Tue 28/2/23		\$8,190,710.78
875	12.1	REPLANTEO Y CONTROL TOPOGRAFICO	1 day?	Mon 23/1/23	Mon 24/1/23		\$204,027.69
876	12.1.1	MOVIMIENTO DE TIERRA:	16 days?	Mon 23/1/23	Mon 23/1/23	873	\$204,027.69
877	12.2	EXCAVACIÓN EN ROCA CON TRENCHER	5 days	Tue 24/1/23	Mon 30/1/23	876	\$4,899,646.98
878	12.2.1	REGULARIZACION DE ZANJAS	5 days	Tue 24/1/23	Mon 30/1/23	876	\$3,562,020.40
879	12.2.2	SUMINISTRO Y COLOCACION ASIENTO ARENA	3 days	Tue 24/1/23	Thu 26/1/23	878	\$26,797.48
880	12.2.3	SUMINISTRO Y COLOCACION ASIENTO ARENA	3 days	Tue 24/1/23	Thu 26/1/23	878	\$213,824.79
881	12.2.4	SUMINISTRO DE CAUCHO PARA RELLENO	3 days	Tue 24/1/23	Thu 26/1/23	880	\$398,212.94
882	12.2.5	RELLENO COMPACTADO CON MACO (2 CAPAS)	8 days	Fri 3/2/23	Tue 14/2/23	892	\$524,781.40
883	12.2.6	NOTE DE MATERIAL SOBRIANTE (A 15 KMS)	8 days	Fri 3/2/23	Tue 14/2/23	882	\$164,039.97
884	12.3	SUMINISTRO DE TUBERIAS Y PIEZAS:	14 days	Mon 23/1/23	Thu 9/2/23		\$1,406,823.34
885	12.3.1	TUBERIA:	14 days	Mon 23/1/23	Thu 9/2/23		\$1,355,400.73
886	12.3.1.1	TUBERIA DE Ø20" PVC SDR-26 CON JUNTA DE GOMA	4 days	Mon 23/1/23	Thu 26/1/23	876	\$1,028,472.28
887	12.3.1.2	REUTILIZACION DE 30 TUBOS DE Ø20" PVC SDR 26 CON JUNTA DE GOMA QUE YA ESTABAN INSTALADOS EN TRAMO (INCLUYE EXCAVACION Y MOVILIZACION A NUEVO TRAMO)	3 days	Tue 7/2/23	Thu 9/2/23	879	\$326,928.45
888	12.3.2	SUMINISTRO DE PIEZAS ESPECIALES:	3 days	Mon 23/1/23	Wed 25/1/23		\$51,423.61
889	12.3.2.1	SUMINISTRO DE PIEZAS ESPECIALES 5N	3 days	Mon 23/1/23	Wed 25/1/23	885	\$51,423.61
890	12.4	COLOCACION DE TUBERIAS Y PIEZAS	7 days	Fri 27/1/23	Mon 6/2/23		\$297,862.97
891	12.4.1	TUBERIA:	5 days	Fri 27/1/23	Thu 2/2/23		\$229,125.36
892	12.4.1.1	TUBERIA DE Ø20" PVC SDR-26 CON JUNTA DE GOMA	5 days	Fri 27/1/23	Thu 2/2/23	880	\$229,125.36
893	12.4.2	PIEZAS ESPECIALES:	2 days	Fri 3/2/23	Mon 6/2/23		\$68,737.61
894	12.4.2.1	COLOCACION DE PIEZAS ESPECIALES 30N	2 days	Fri 3/2/23	Mon 6/2/23	892	\$68,737.61
895	12.5	REPARACION DE SERVICIO EXISTENTE	2 days	Tue 7/2/23	Wed 8/2/23	894	\$1,000,000.00
896	2.6	PRUEBA HIDROSTATICA	10 days?	Wed 15/2/23	Tue 28/2/23		\$207,048.12
898	2.7	CONTROL Y MANEJO DE TRANSITO	5 days	Wed 15/2/23	Tue 21/2/23	882	\$88,480.32
899	2.8	LIMPIEZA FINAL Y CONTINUA	5 days	Wed 22/2/23	Tue 28/2/23	898	\$86,820.36

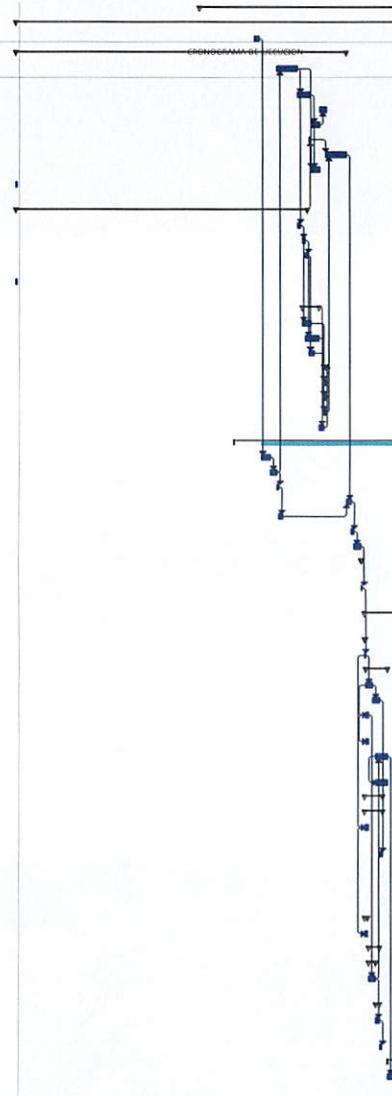

Constructora Montebianco, S.R.L.
RNC: 131-47453-5
Santo Domingo

Task Summary Milestone Project Task Task Summary Milestone External Task Task Summary Milestone Critical Critical Task Progress Manual Progress

fw

[illegible]

Constructora Montebianco, S.R.L.
RNC: 131-47453-5
Santo Domingo
