

Id.	Nombre de tarea	Duración	ene '21																											
			L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	
1	LOTE XVIII - CONTRATISTA EMMANUEL RIVERA GUEVARA																													
2	DURACION TOTAL	132,75 días	[Barra horizontal azul que cubre todo el periodo]																											
3																														
4	RED DE DISTRIBICION COMUNIDADES LA PALMITA, LA JAVILLA Y LA FELICITA																													
5	REPLANTEO	54,88 días	[Barra azul que comienza el 07 feb '21 y termina el 14 feb '21]																											
6																														
7	MOVIMIENTO DE TIERRA:																													
8	EXCAVACION MATERIAL COMPACTO C/EQUIPO	68,75 días	[Barra azul que comienza el 14 feb '21 y termina el 14 feb '21]																											
9	ASIENTO DE ARENA	81,75 días	[Barra azul que comienza el 14 feb '21 y termina el 14 feb '21]																											
10	RELLENO COMPACTADO C/COMPACTADOR MECANICO EN CAPAS 0.30	81,75 días	[Barra azul que comienza el 14 feb '21 y termina el 14 feb '21]																											
11	BOTE DE MATERIAL C/CAMON D= 5 KM (SUJETO A CUANTIFICACION DEL SUPERVISOR)	69,75 días	[Barra azul que comienza el 14 feb '21 y termina el 14 feb '21]																											
12																														
13	SUMINISTRO DE TUBERIA:																													

Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea	[Barra azul]	Resumen inactivo	[Barra gris]	Tareas externas
	División	[Puntos azules]	Tarea manual	[Barra azul]	Hito externo
	Hito	[Diamante azul]	solo duración	[Barra azul]	Fecha límite
	Resumen	[Barra azul]	Informe de resumen manual	[Barra azul]	Progreso
	Resumen del proyecto	[Barra gris]	Resumen manual	[Barra azul]	Progreso manual
	Tarea inactiva	[Barra azul]	solo el comienzo	[Barra azul]	
	Hito inactivo	[Barra azul]	solo fin	[Barra azul]	

Id.	Nombre de tarea	Duración	ene '21																											
			L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	
26	★ TEE DE Ø4" X Ø3" ACERO SCH-80 CON PROTECCION ANTICORROSIVA	3,75 días																												
27	★ JUNTAS MECANICAS TIPO DRESSER DE Ø4"	3,75 días																												
28	★ JUNTAS MECANICAS TIPO DRESSER DE Ø3"	48,75 días																												
29	★ JUNTAS MECANICAS TIPO DRESSER DE Ø6"	5,75 días																												
30	★ ANCLAJE H.S.	79,75 días																												
31	■																													
32	★ SUMINISTRO Y COLOCACION DE VALVULAS																													
33	★ VALVULA DE COMPUERTA DE Ø6" PLATILLADA (INC. 2 JUNTAS DE GOMA, 2 NIPLA PLATILLADOS, 2 JUNTAS MECANICAS TIPO DRESSER Y 2 PARES DE TORNILLOS)	5,75 días																												
34	★ VALVULA DE COMPUERTA DE Ø3" PLATILLADA (INC. 2 JUNTAS DE GOMA, 2 NIPLA PLATILLADOS, 2 JUNTAS MECANICAS TIPO DRESSER Y 2 PARES DE TORNILLOS)	2 días																												
35	★ CAJA TELESCOPICA	1 día																												
36	■																													

Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

Id.	Nombre de tarea	Duración	ene '21																											
			L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	
37	ACOMETIDAS RURALES (300 U)																													
38	COLLARIN EN POLIETILENO Ø3" (ABRAZADERA)	79,75 días																												
39	TUBERIA DE POLIETILENO DE ALTA DENSIDAD Ø1/2" INTERNO L=12.00M (PROMEDIO)	79,75 días																												
40	ADAPTADOR MACHO Ø1/2" ROSCADO A MANGUERA	79,88 días																												
41	CODO 1/2" X 90° HG	79,88 días																												
42	TUBERIA DE HIERRO GALVANIZADO Ø1/2" (BASTONES)	79,88 días																												
43	NIPLE Ø1/2" H.G.	79,75 días																												
44	COUPLING 1/2 H.G	79,75 días																												
45	LLAVE DE CHORRO Ø1/2" BRONCE	79,75 días																												
46	CHECK 1/2" HG	79,75 días																												
47	CEMENTO SOLVENTE Y TEFLON	79,75 días																												
48	PEDESTAL H.S (0.80 X 0.15)	79,75 días																												
49	EXCAVACION Y TAPADO	79,75 días																												
50	MANO DE OBRA PLOMERO	79,75 días																												
51																														
52	ACOMETIDAS URBANAS (56 U)																													
53	COLLARIN EN POLIETILENO Ø3" (ABRAZADERA)	74,75 días																												
54	TUBERIA DE POLIETILENO DE ALTA DENSIDAD Ø1/2" INTERNO L=6.00M (PROMEDIO)	74,75 días																												

Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

Id	M de tar	Nombre de tarea	Duración	ene '21																											
				L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	
55		ADAPTADOR MACHO Ø1/2" ROSCADO A MANGUERA	74,75 días																												
56		ADAPTADOR HEMBRA Ø1/2" ROSCADO A MANGUERA	74,75 días																												
57		LLAVE DE PASO DE Ø1/2"	74,75 días																												
58		CAJA DE ACOMETIDA PLASTICA EN POLIETILENO 10"	74,75 días																												
59		TUBERIA Ø1/2" SCH-40 PVC LONGITUD PROMEDIO	74,75 días																												
60		VALVULA CHECK 1/2" DE BRONCE	74,75 días																												
61		ANCLAJE DE H.S.	74,75 días																												
62		CEMENTO SOLVENTE Y TEFLON	74,75 días																												
63		TAPON HEMBRA Ø1/2"	74,75 días																												
64		EXCAVACION Y TAPADO	74,75 días																												
65		MANO DE OBRA PLOMERO	74,75 días																												
66																															
67		PRUEBA HIDROSTATICA																													
68		TUBERIA Ø3" PVC (SDR-26 C/J.G.) + 2% DE PERDIDA POR CAMPANA	75,75 días																												
69		TUBERIA Ø4" PVC (SDR-26 C/J.G.) + 2% DE PERDIDA POR CAMPANA	75,75 días																												
70		TUBERIA Ø6" PVC (SDR-26 C/J.G.) + 3% DE PERDIDA POR CAMPANA	75,75 días																												
71																															
72		ACERA PERIMETRAL 0.80 M	68,75 días																												

Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			


Id.	Nombre de tarea	Duración	ene '21																											
			L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	
73	★ CONTEN	70,75 días																												
74																														
75	★ PAVIMENTO (1000 M)																													
76	★ CORTE DE ASFALTO E= 2"	27,88 días																												
77	★ REMOCION DE CARPETA ASFALTICA 2"	27,75 días																												
78	★ SUMINISTRO Y COLOCACION MATERIAL DE BASE	90,75 días																												
79	★ COMPACTACION MATERIAL DE BASE EN CAPA DE 0.20	90,75 días																												
80	★ BOTE DE MATERIAL RELLENO Y ASFALTICO C/CAMION D = 5 KM	27,75 días																												
81	★ REPOSICION CARPETA ASFALTICA (E = 0.05 M)	80,75 días																												
82	★ TRANSPORTE DE ASFALTO (DIST. APROX. = 50 KM)	80,75 días																												
83																														
84	★ SEÑALIZACION, MANEJO DE TRANSITO Y SEGURIDAD VIAL (INC. OBREROS, MECHONES, CONOC, CINTA, AVISO DE PELIGRO Y LETREROS)	100,88 días																												

Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
	Hito inactivo		solo fin			

Id	Nombre de tarea	Duración	ene '21																											
			L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	
85	★ LIMPIEZA FINAL	7 días																												
86																														
87	★ VARIOS																													
88	★ CAMPAMENTO (INC ALQUILER DE CASA O SOLAR, CON CASETA DE MATERIALES CON (U) BAÑO MOVIL)	100,88 días																												

Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin				


21 feb '21 28 feb '21 07 mar '21 14 mar '21 21 mar '21 28 mar '21 04 abr '21 11 abr '21
D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S

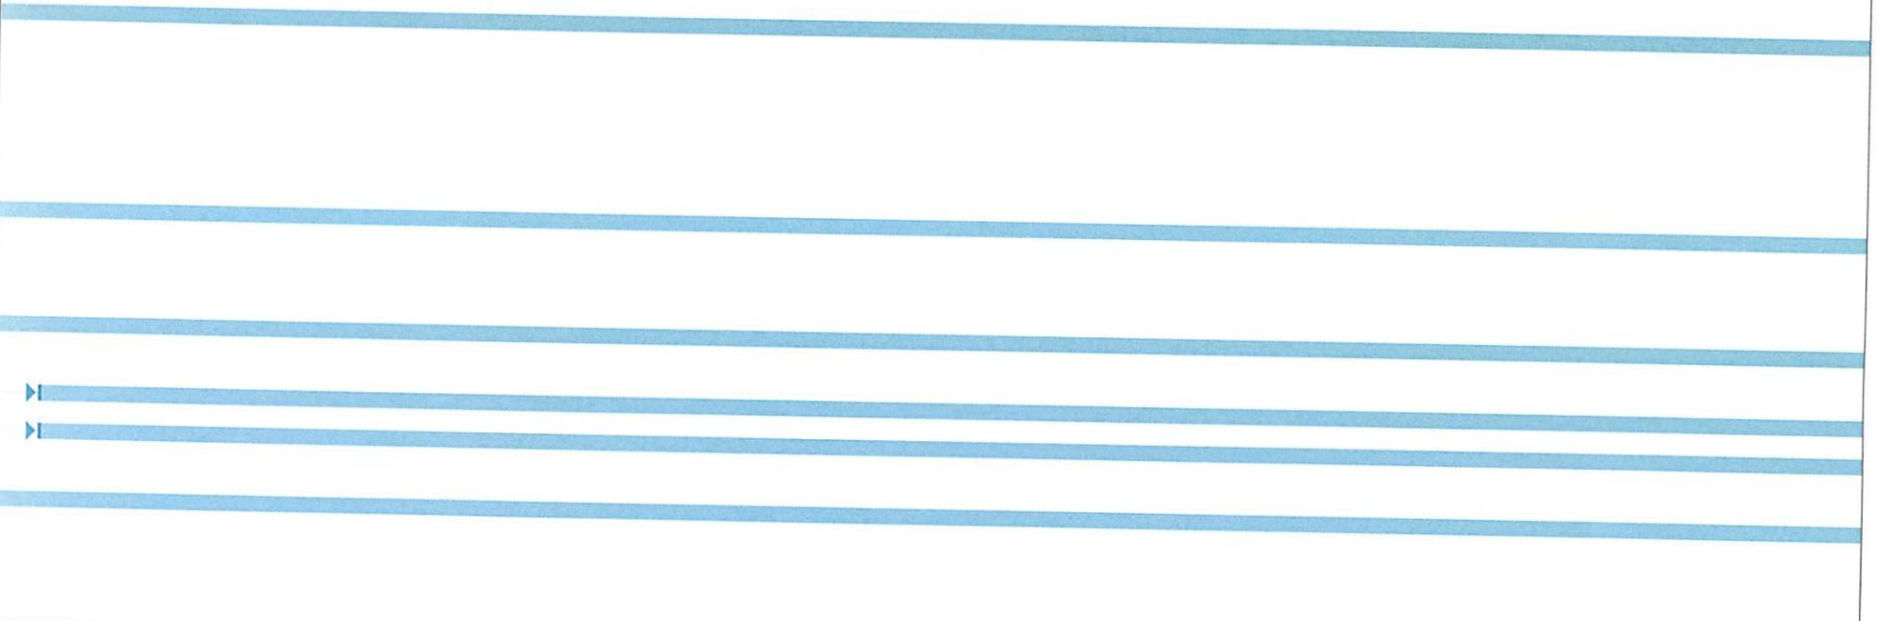


Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

21 feb '21 | 28 feb '21 | 07 mar '21 | 14 mar '21 | 21 mar '21 | 28 mar '21 | 04 abr '21 | 11 abr '21
 D L M X J V S | D L M X J V S | D L M X J V S | D L M X J V S | D L M X J V S | D L M X J V S | D L M X J V S | D L M X J V S

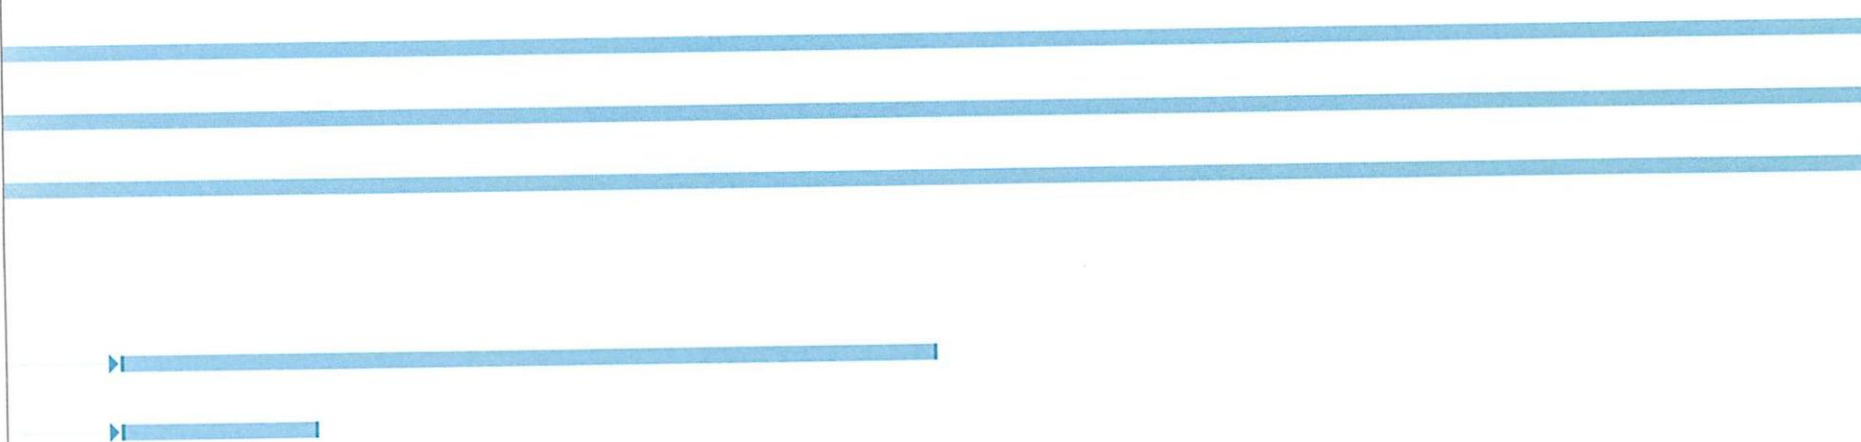


Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
	Hito inactivo		solo fin			

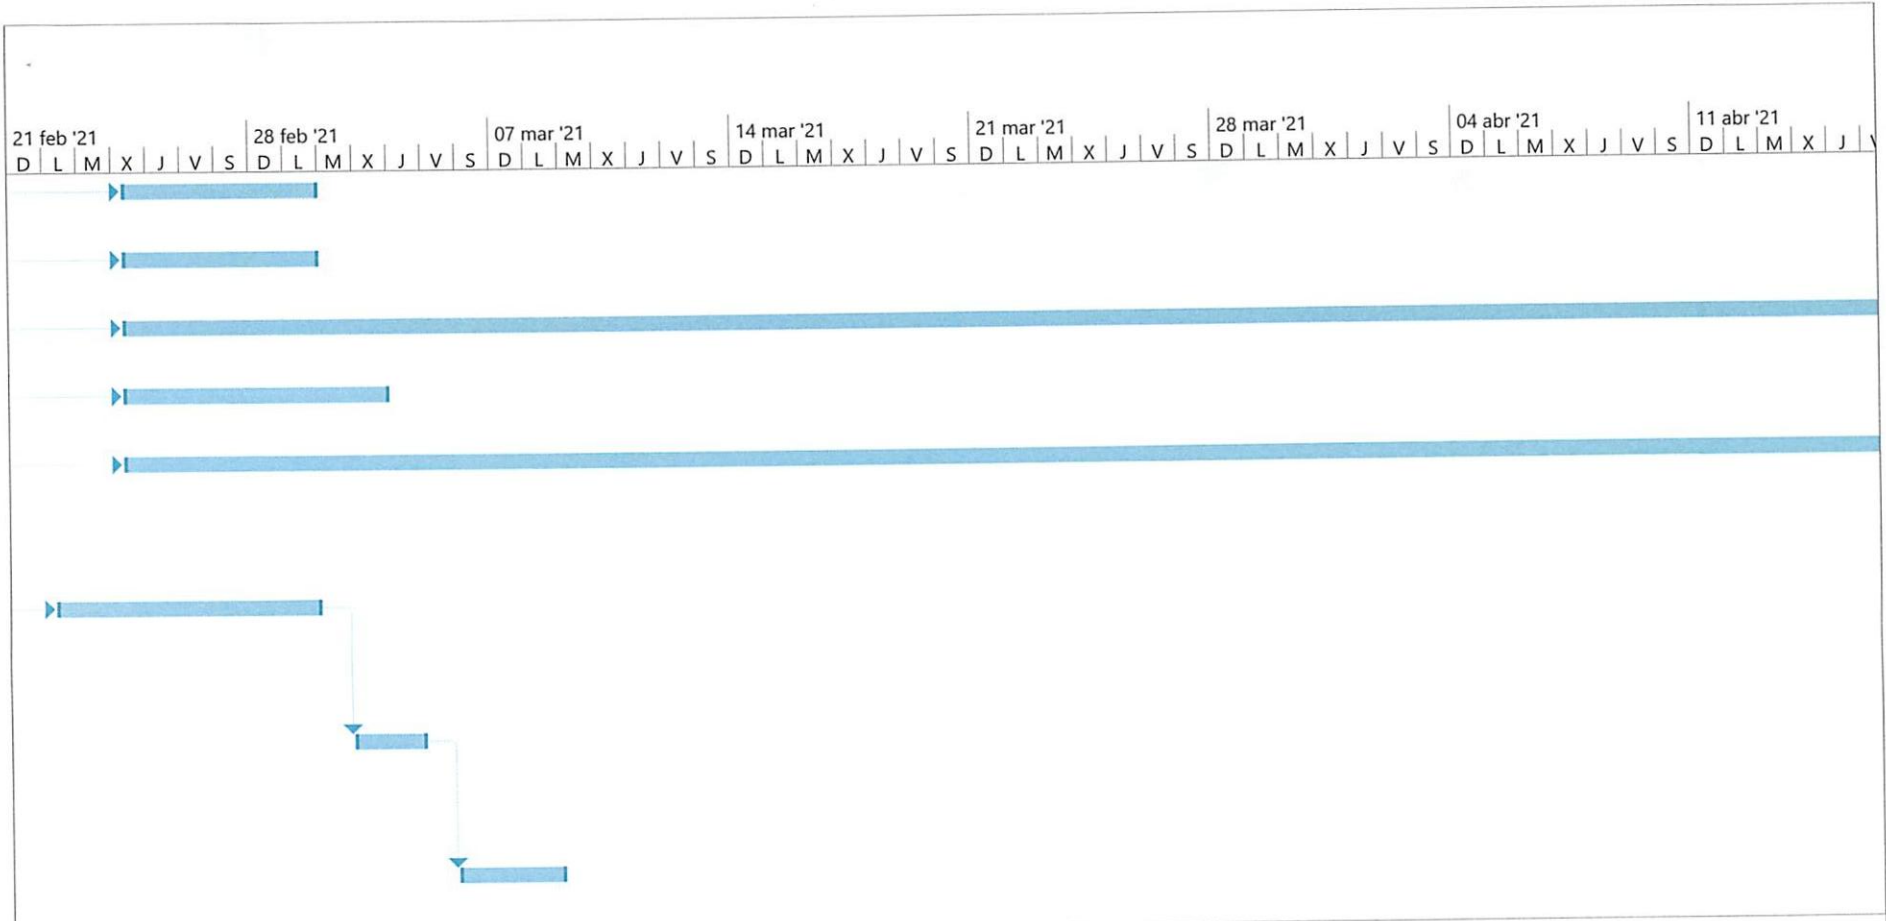


Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
	Hito inactivo		solo fin			

21 feb '21 28 feb '21 07 mar '21 14 mar '21 21 mar '21 28 mar '21 04 abr '21 11 abr '21
D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S

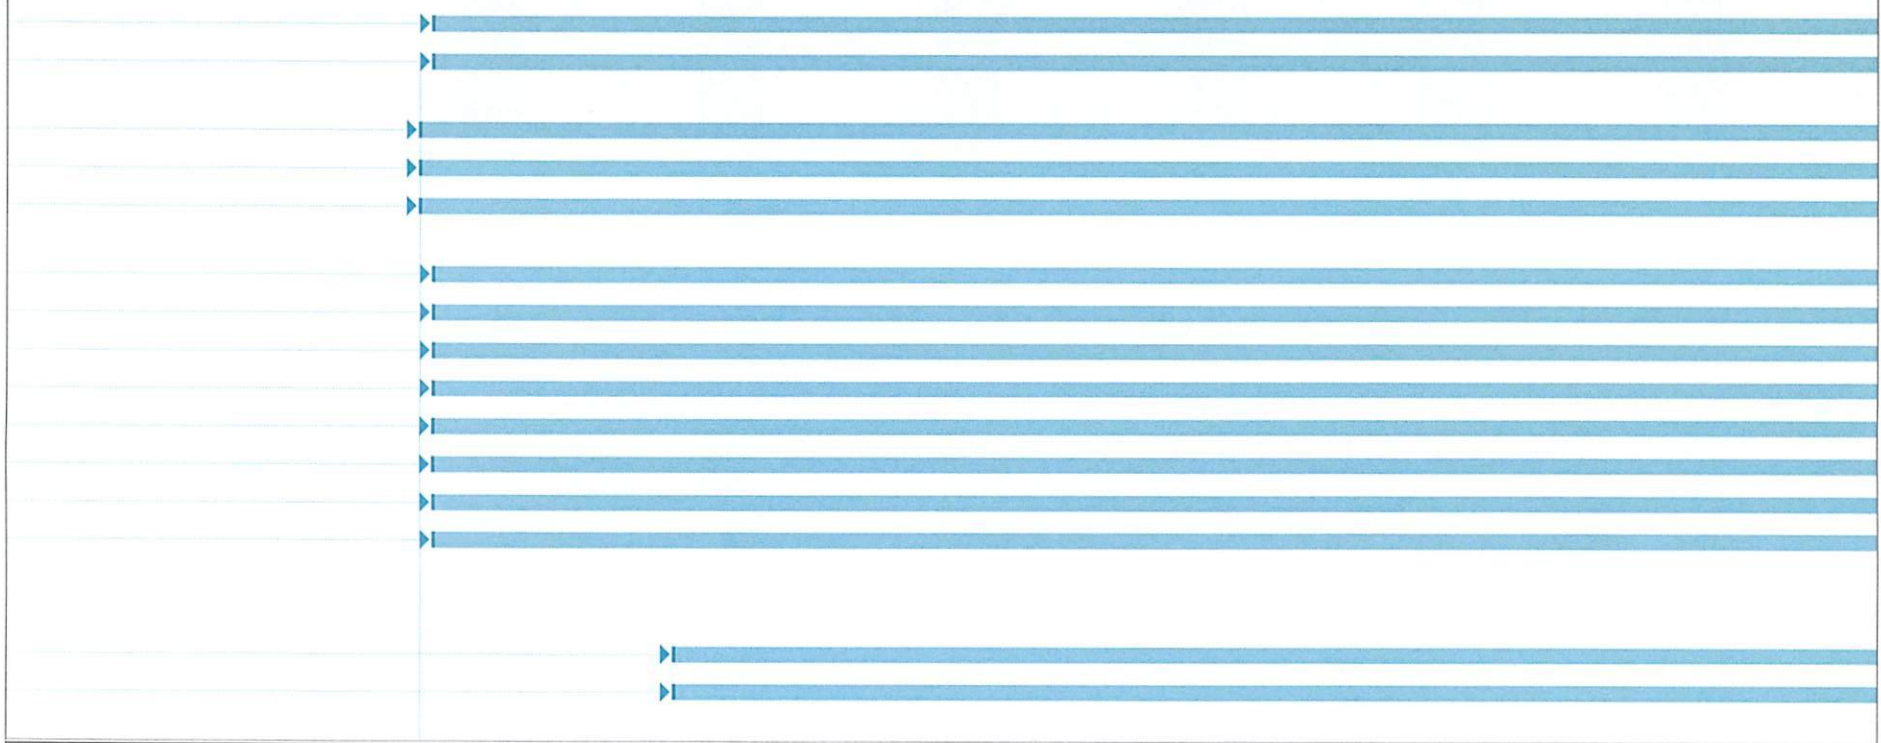

Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin				


21 feb '21 | 28 feb '21 | 07 mar '21 | 14 mar '21 | 21 mar '21 | 28 mar '21 | 04 abr '21 | 11 abr '21

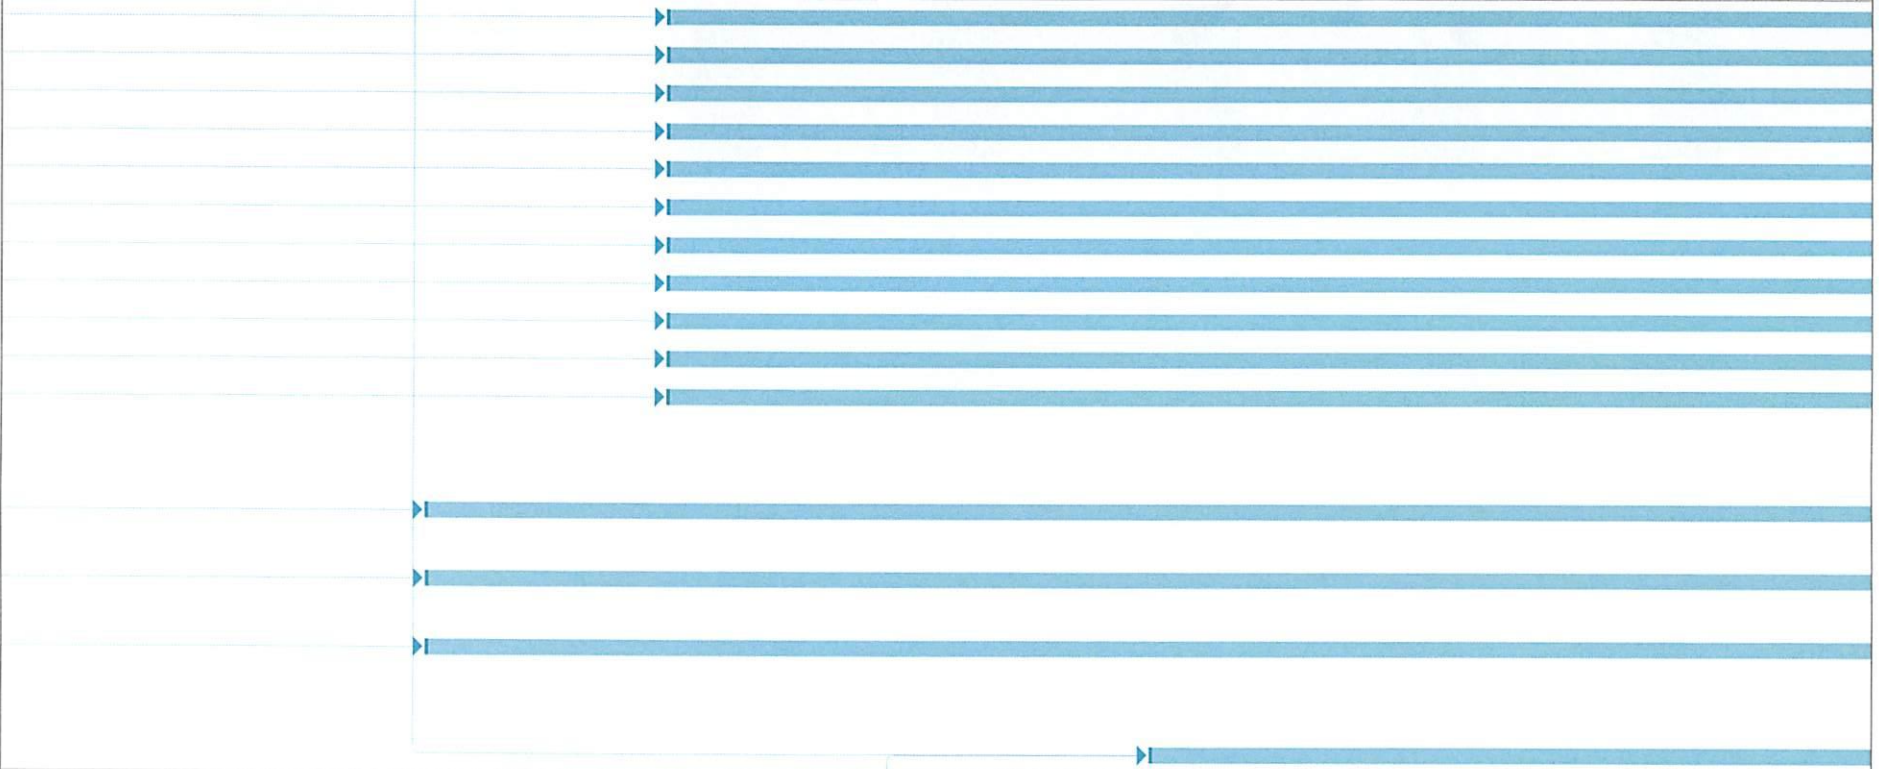

Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

21 feb '21 28 feb '21 07 mar '21 14 mar '21 21 mar '21 28 mar '21 04 abr '21 11 abr '21
 D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S

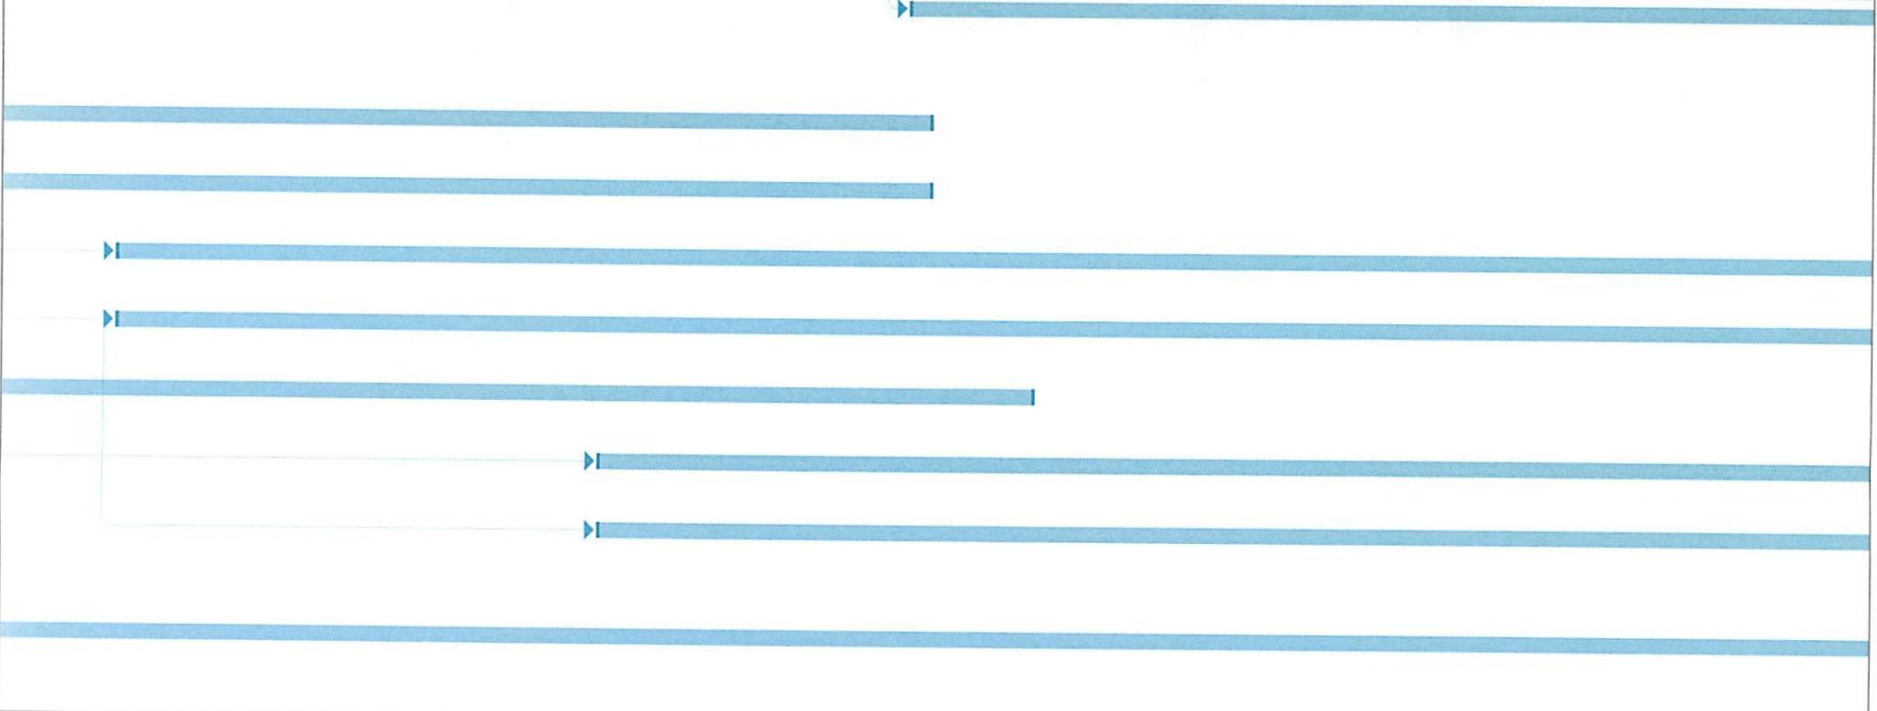

Proyecto: LOTE XVIII - INAPA -
 Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			


21 feb '21 | 28 feb '21 | 07 mar '21 | 14 mar '21 | 21 mar '21 | 28 mar '21 | 04 abr '21 | 11 abr '21
 D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S D L M X J V S



Proyecto: LOTE XVIII - INAPA -
 Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			


V S 18 abr '21 25 abr '21 02 may '21 09 may '21 16 may '21 23 may '21 30 may '21 06 jun '21

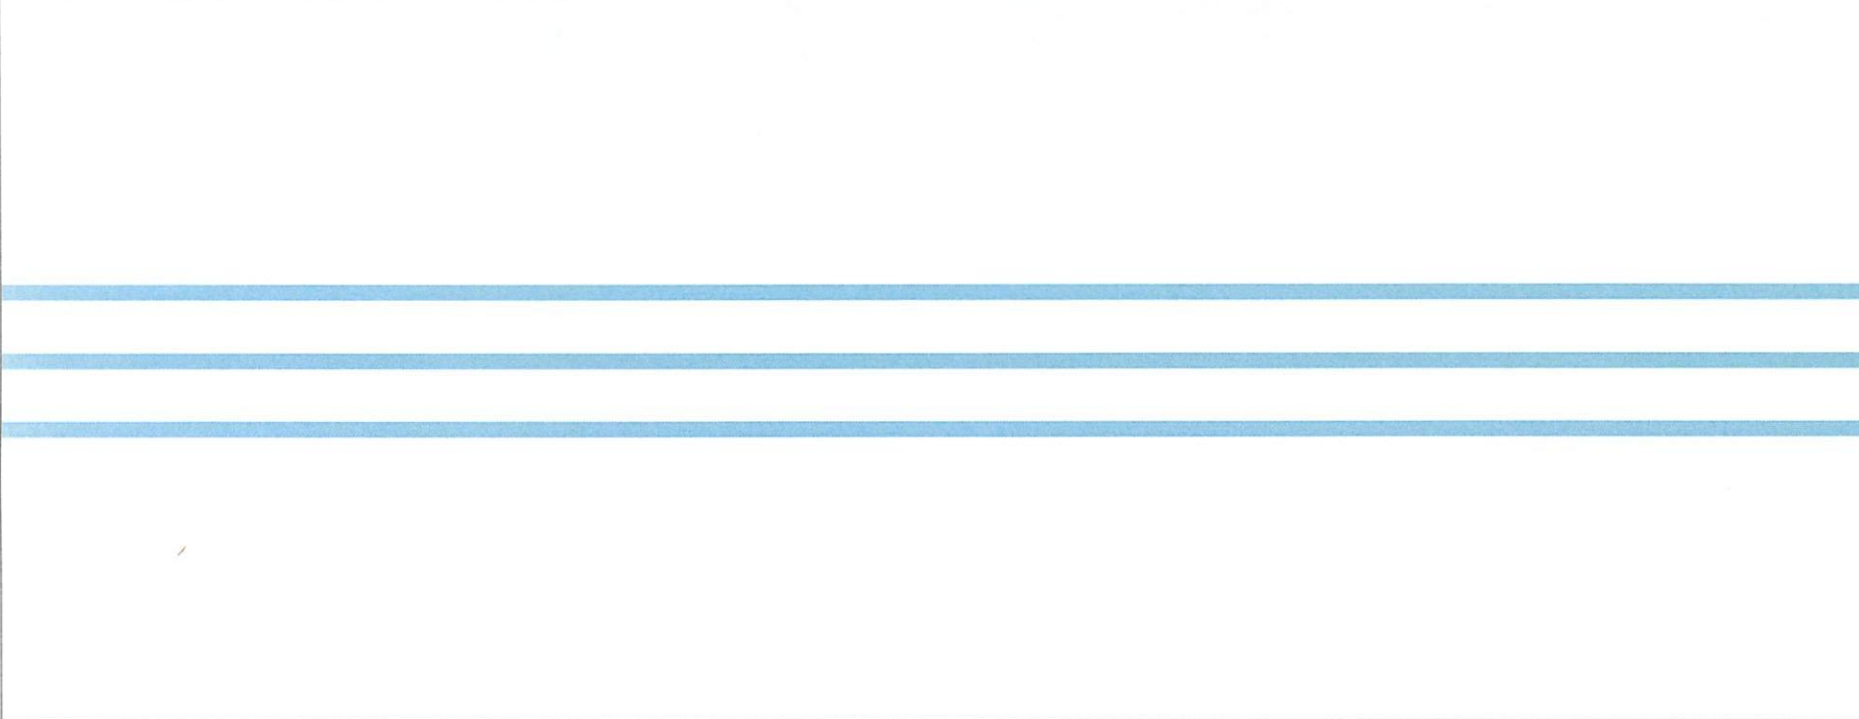

Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			


V S | 18 abr '21 | D L M X J V S | 25 abr '21 | D L M X J V S | 02 may '21 | D L M X J V S | 09 may '21 | D L M X J V S | 16 may '21 | D L M X J V S | 23 may '21 | D L M X J V S | 30 may '21 | D L M X J V S | 06 jun '21 | D L M X

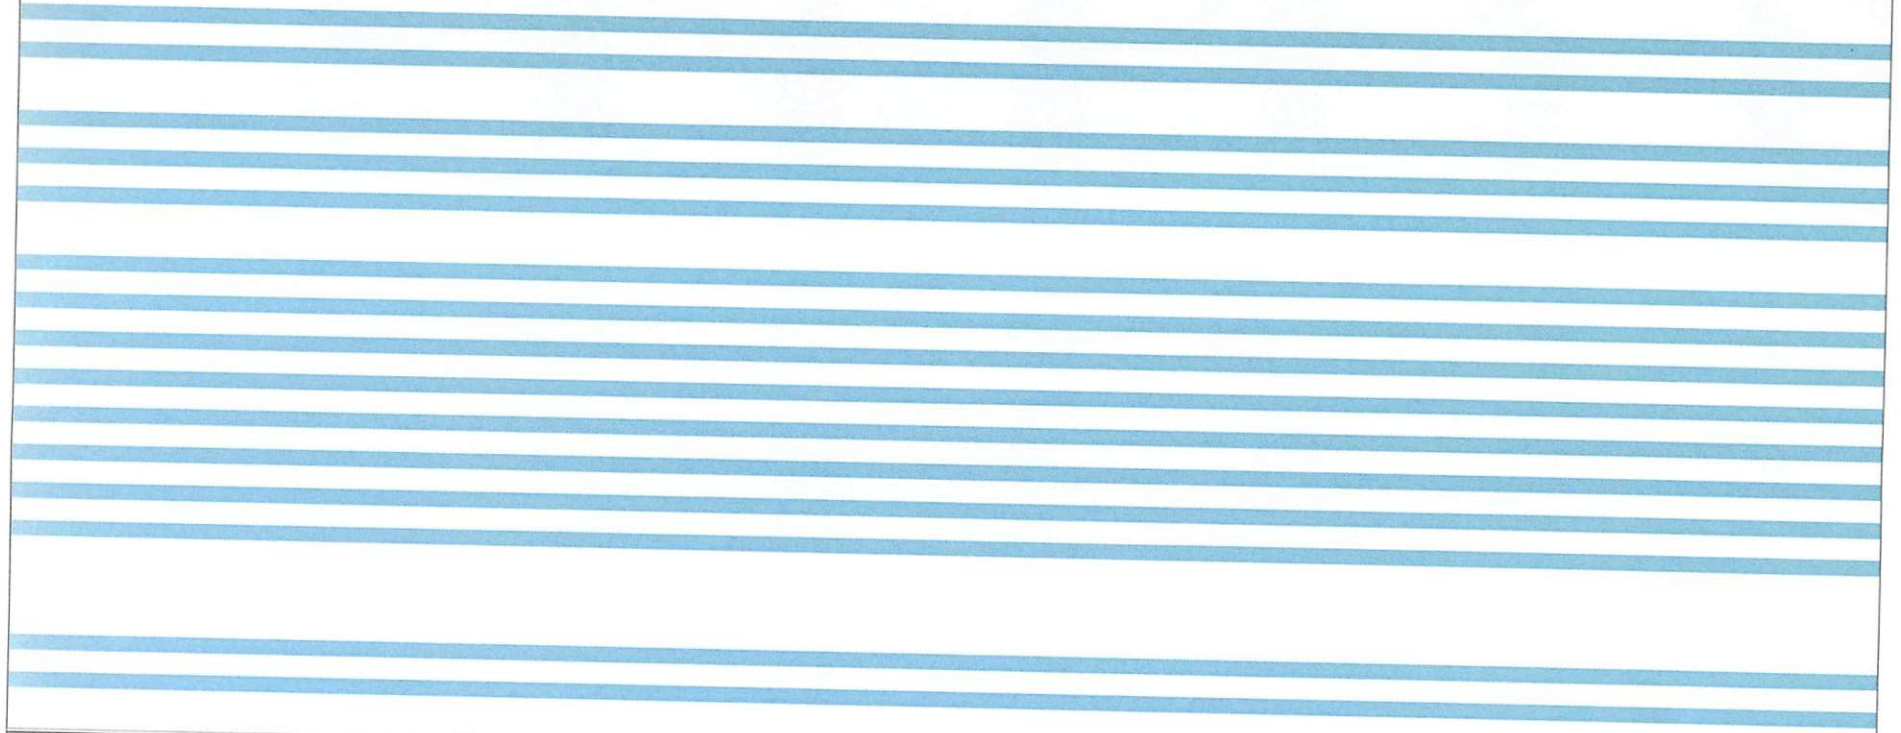

Proyecto: LOTE XVIII - INAPA -
 Fecha: mar 09/02/21


Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

V | S | 18 abr '21 | 25 abr '21 | 02 may '21 | 09 may '21 | 16 may '21 | 23 may '21 | 30 may '21 | 06 jun '21 |

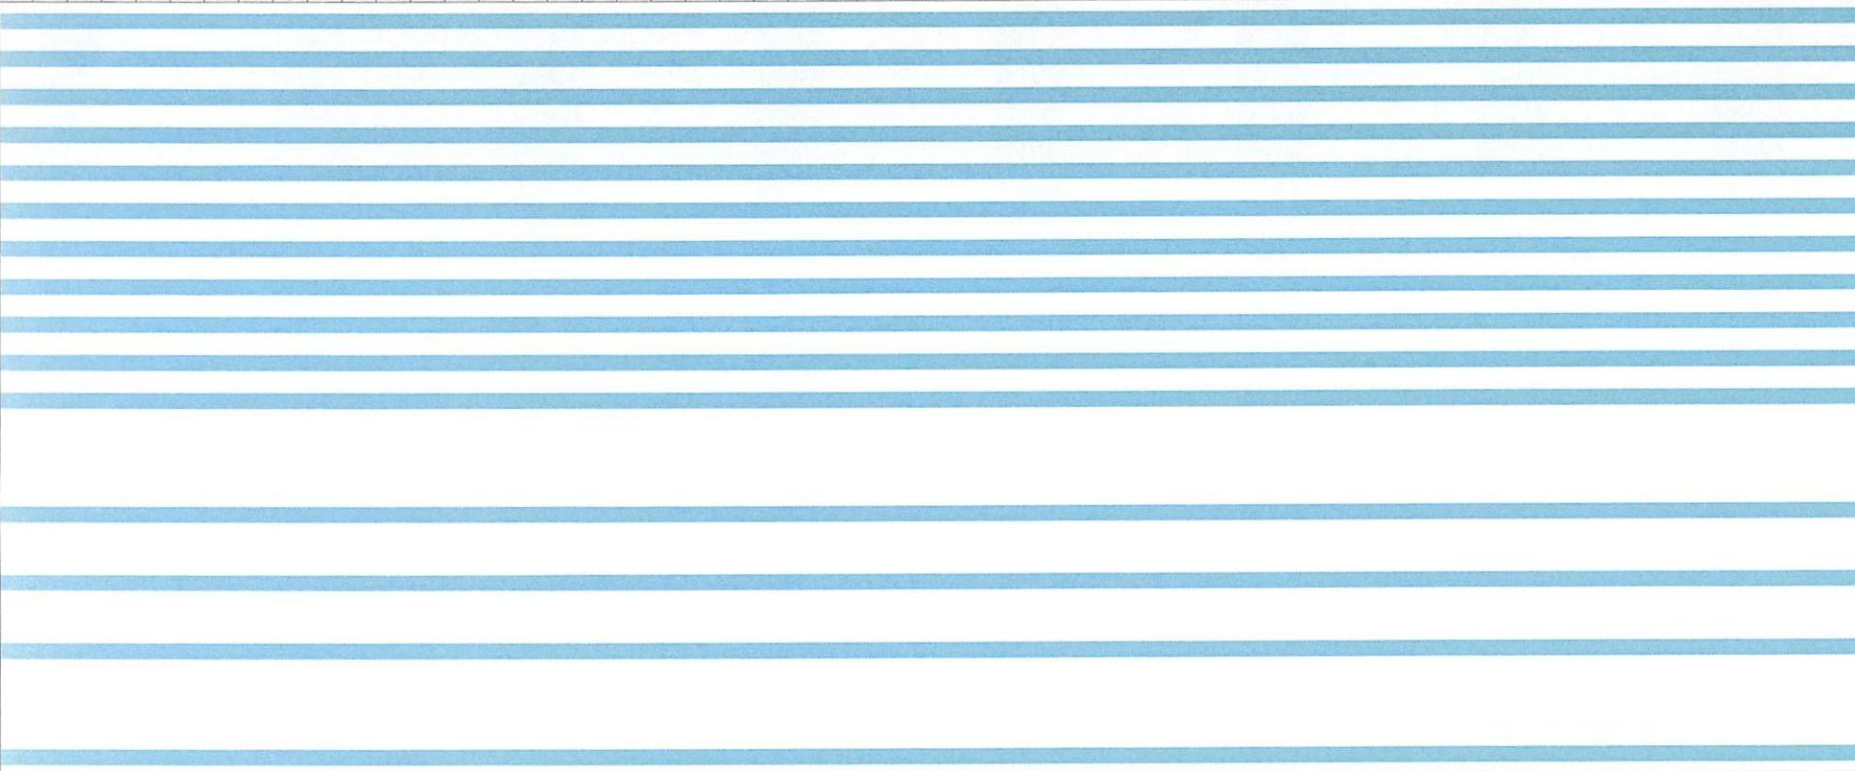

Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
	Hito inactivo		solo fin			

V | S | 18 abr '21 | 25 abr '21 | 02 may '21 | 09 may '21 | 16 may '21 | 23 may '21 | 30 may '21 | 06 jun '21 | X

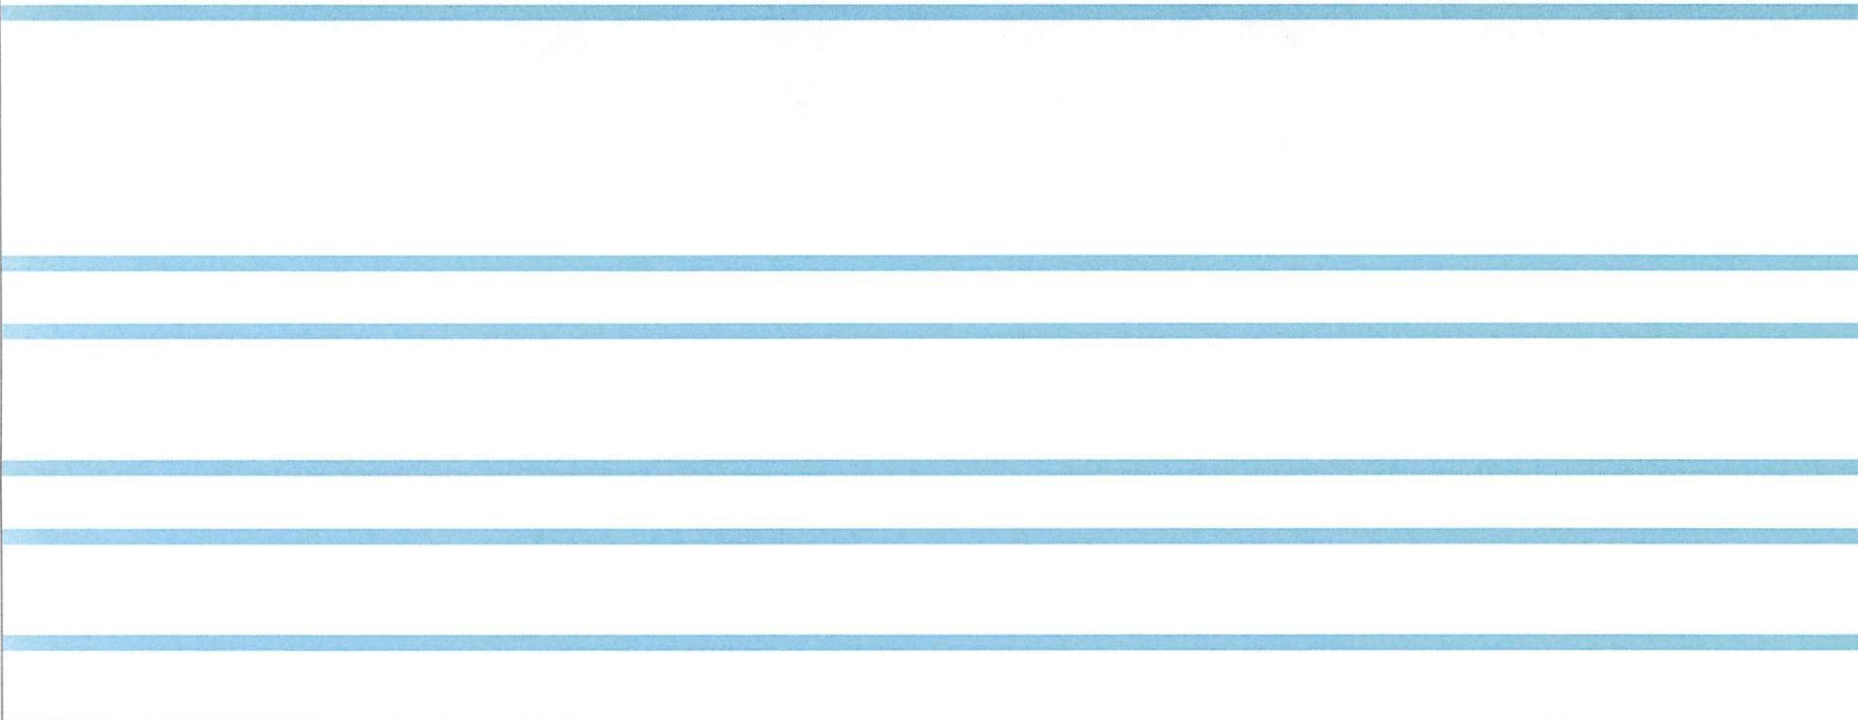

Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21


Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

V S D L M X J V S | 18 abr '21 | D L M X J V S | 25 abr '21 | D L M X J V S | 02 may '21 | D L M X J V S | 09 may '21 | D L M X J V S | 16 may '21 | D L M X J V S | 23 may '21 | D L M X J V S | 30 may '21 | D L M X J V S | 06 jun '21



Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
	Hito inactivo		solo fin			

X J V S 13 jun '21 X J V S 20 jun '21 X J V S 27 jun '21 X J V S 04 jul '21 X J V S 11 jul '21 X J V S 18 jul '21 X J V S 25 jul '21 X J V S 01 ag

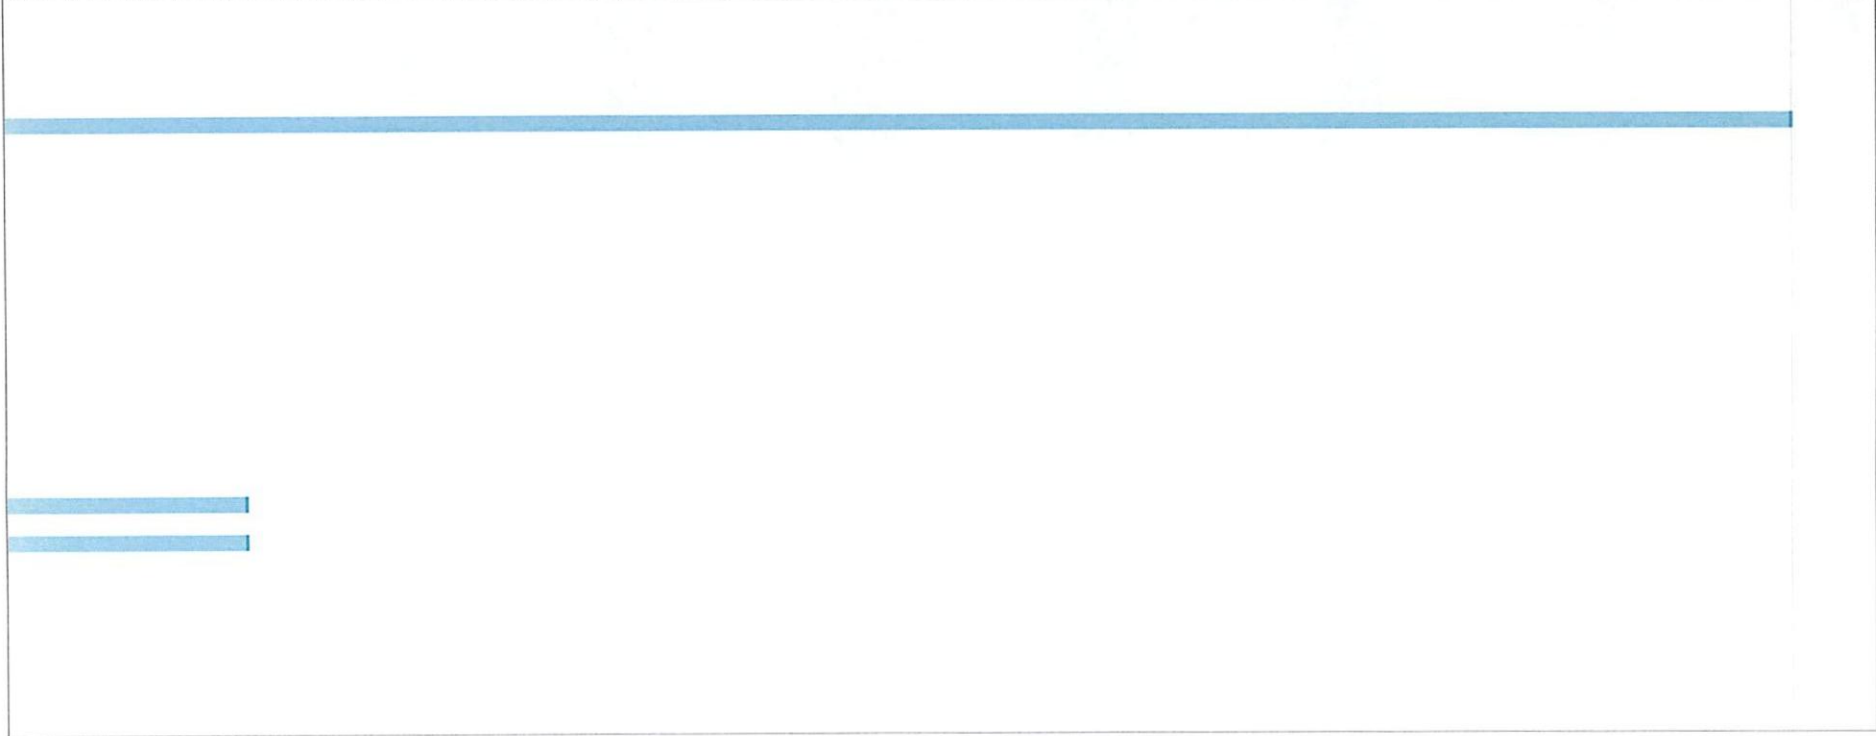

Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

X J V S | 13 jun '21 | D L M X J V S | 20 jun '21 | D L M X J V S | 27 jun '21 | D L M X J V S | 04 jul '21 | D L M X J V S | 11 jul '21 | D L M X J V S | 18 jul '21 | D L M X J V S | 25 jul '21 | D L M X J V S | 01 ag




Proyecto: LOTE XVIII - INAPA - Fecha: mar 09/02/21	Tarea		Resumen inactivo		Tareas externas	
	División		Tarea manual		Hito externo	
	Hito		solo duración		Fecha límite	
	Resumen		Informe de resumen manual		Progreso	
	Resumen del proyecto		Resumen manual		Progreso manual	
	Tarea inactiva		solo el comienzo			
	Hito inactivo		solo fin			

X J V S | 13 jun '21 | 20 jun '21 | 27 jun '21 | 04 jul '21 | 11 jul '21 | 18 jul '21 | 25 jul '21 | 01 ago '21



Proyecto: LOTE XVIII - INAPA -
Fecha: mar 09/02/21

Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

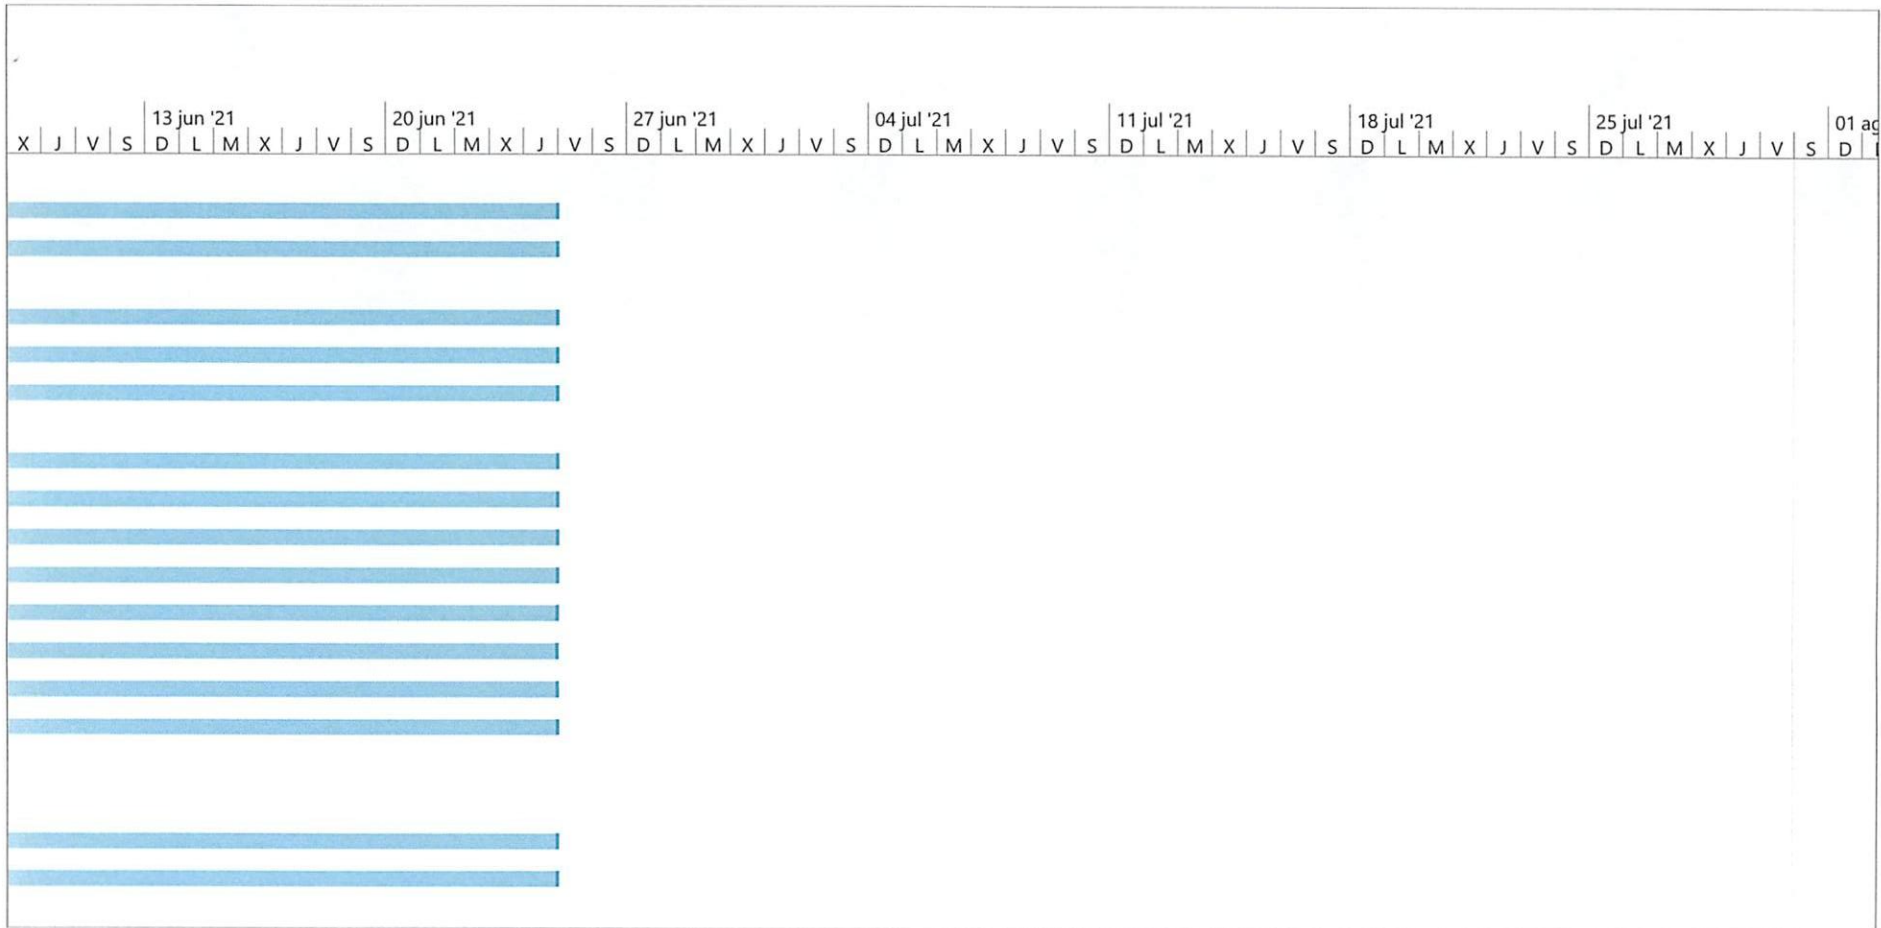


Proyecto: LOTE XVIII - INAPA -
 Fecha: mar 09/02/21


Tarea		Resumen inactivo		Tareas externas	
División		Tarea manual		Hito externo	
Hito		solo duración		Fecha límite	
Resumen		Informe de resumen manual		Progreso	
Resumen del proyecto		Resumen manual		Progreso manual	
Tarea inactiva		solo el comienzo			
Hito inactivo		solo fin			

CRONOGRAMA ACUEDUCTO ZONA 4
 LINEA DE IMPULSION 12"
 SANTO DOMINGO-MONTE PLATA


3/28	abril 1	4/4	abril 11	4/11	abril 21	4/18	4/25	mayo 1	5/2	mayo 11	5/9	5/16	mayo 21	5/23	junio 1	5/30	6/6	junio 11	6/13	junio 21	6/20	6/27	julio 1	7/4	julio 11	7/11	julio 21	7/18
------	---------	-----	----------	------	----------	------	------	--------	-----	---------	-----	------	---------	------	---------	------	-----	----------	------	----------	------	------	---------	-----	----------	------	----------	------

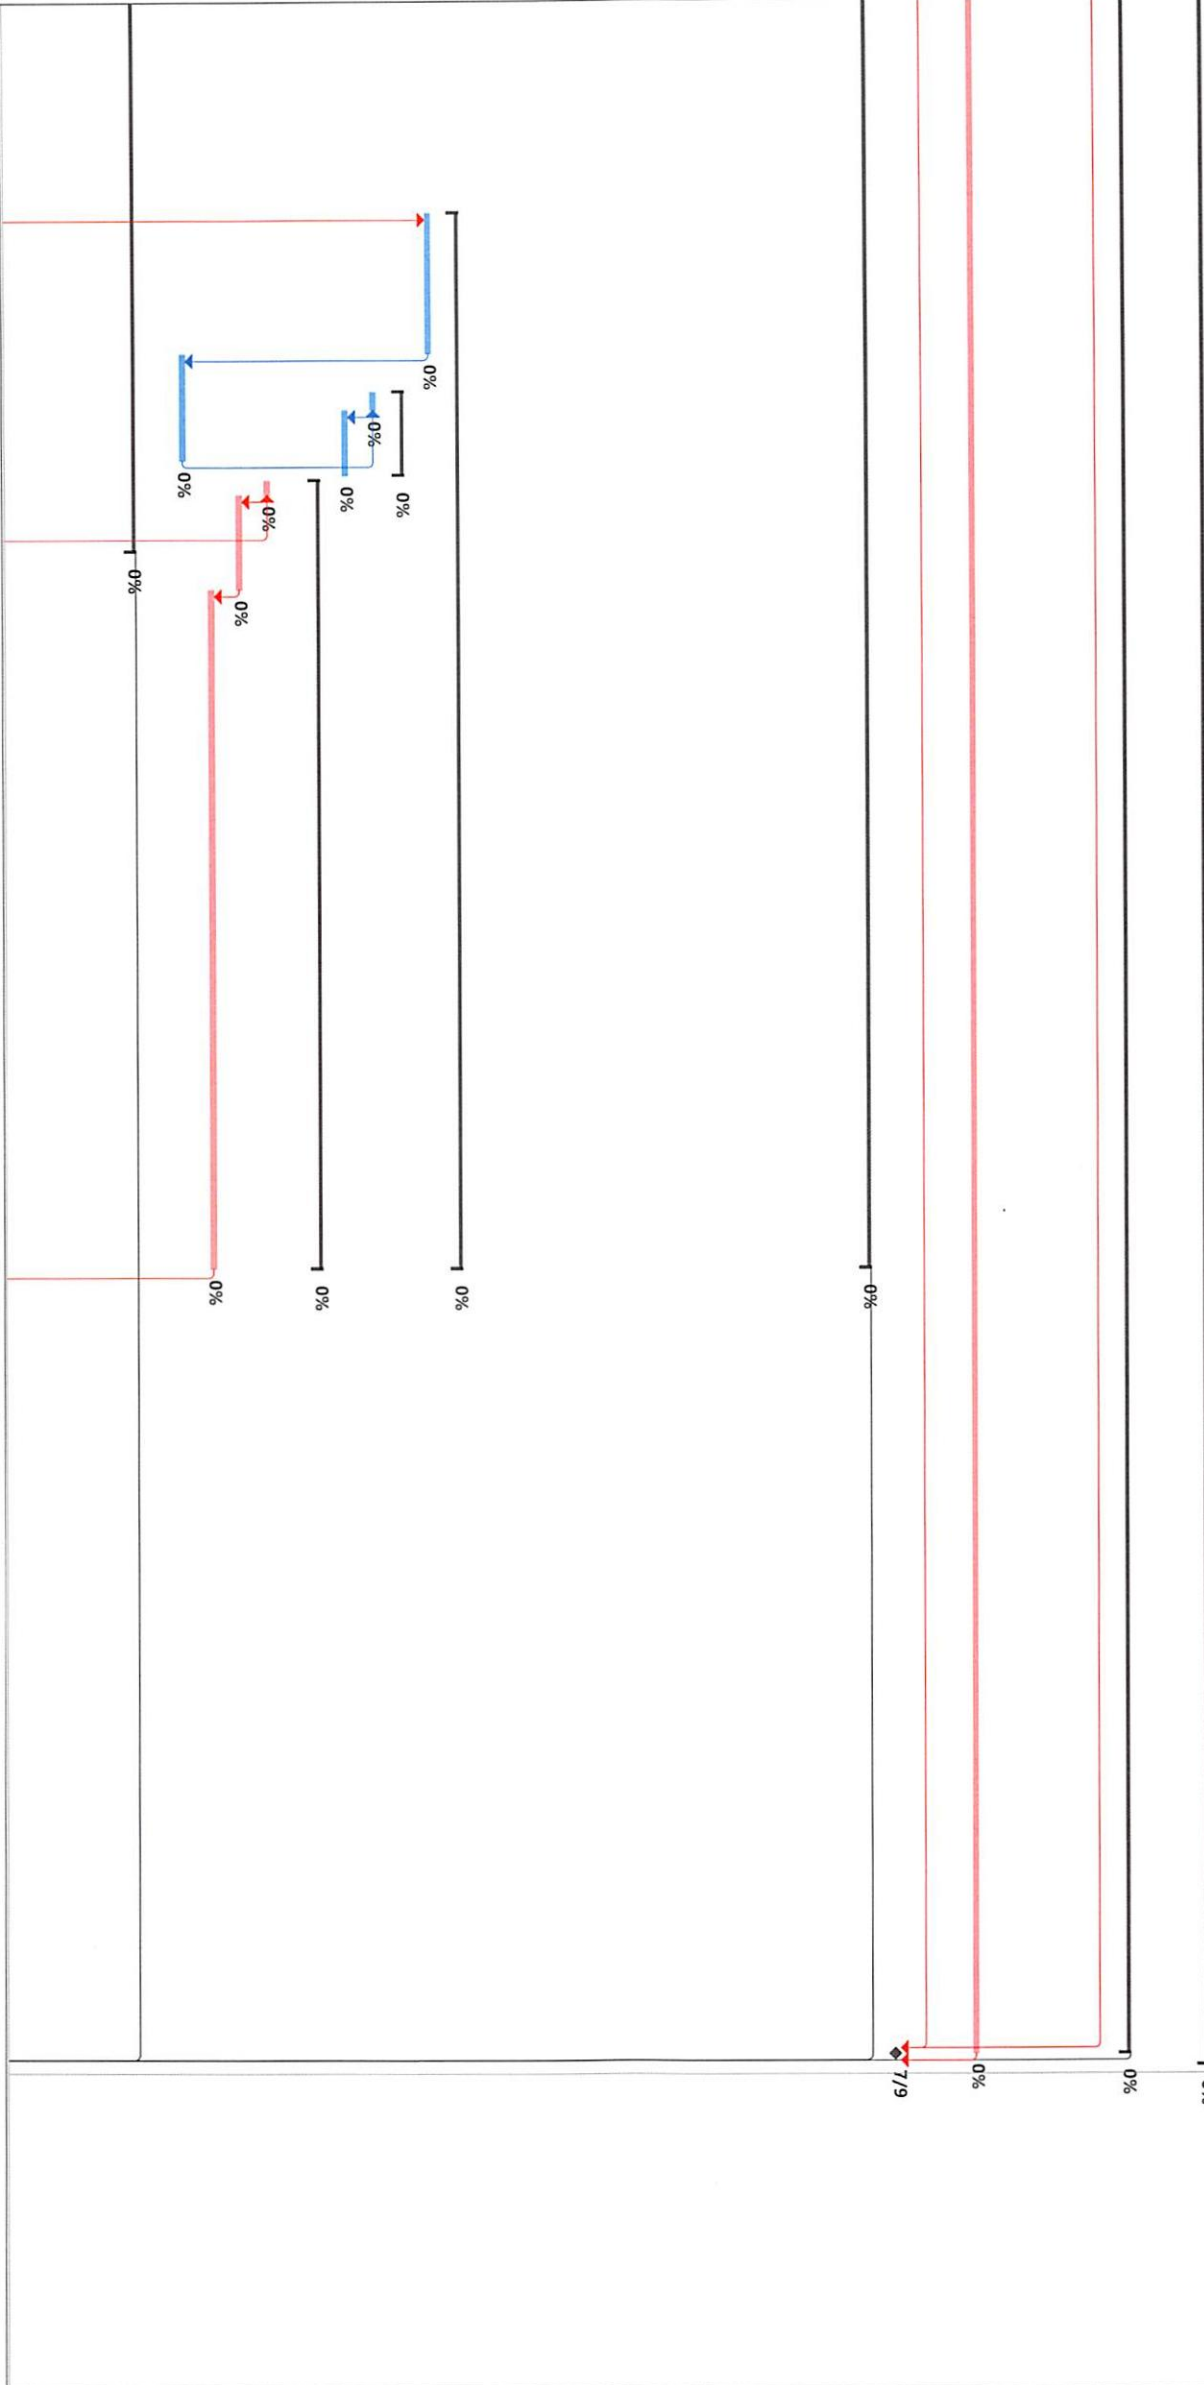

CRONOGRAMA ACUEDUCTO ZONA 4
 LINEA DE IMPULSION 12"
 SANTO DOMINGO-MONTE PLATA

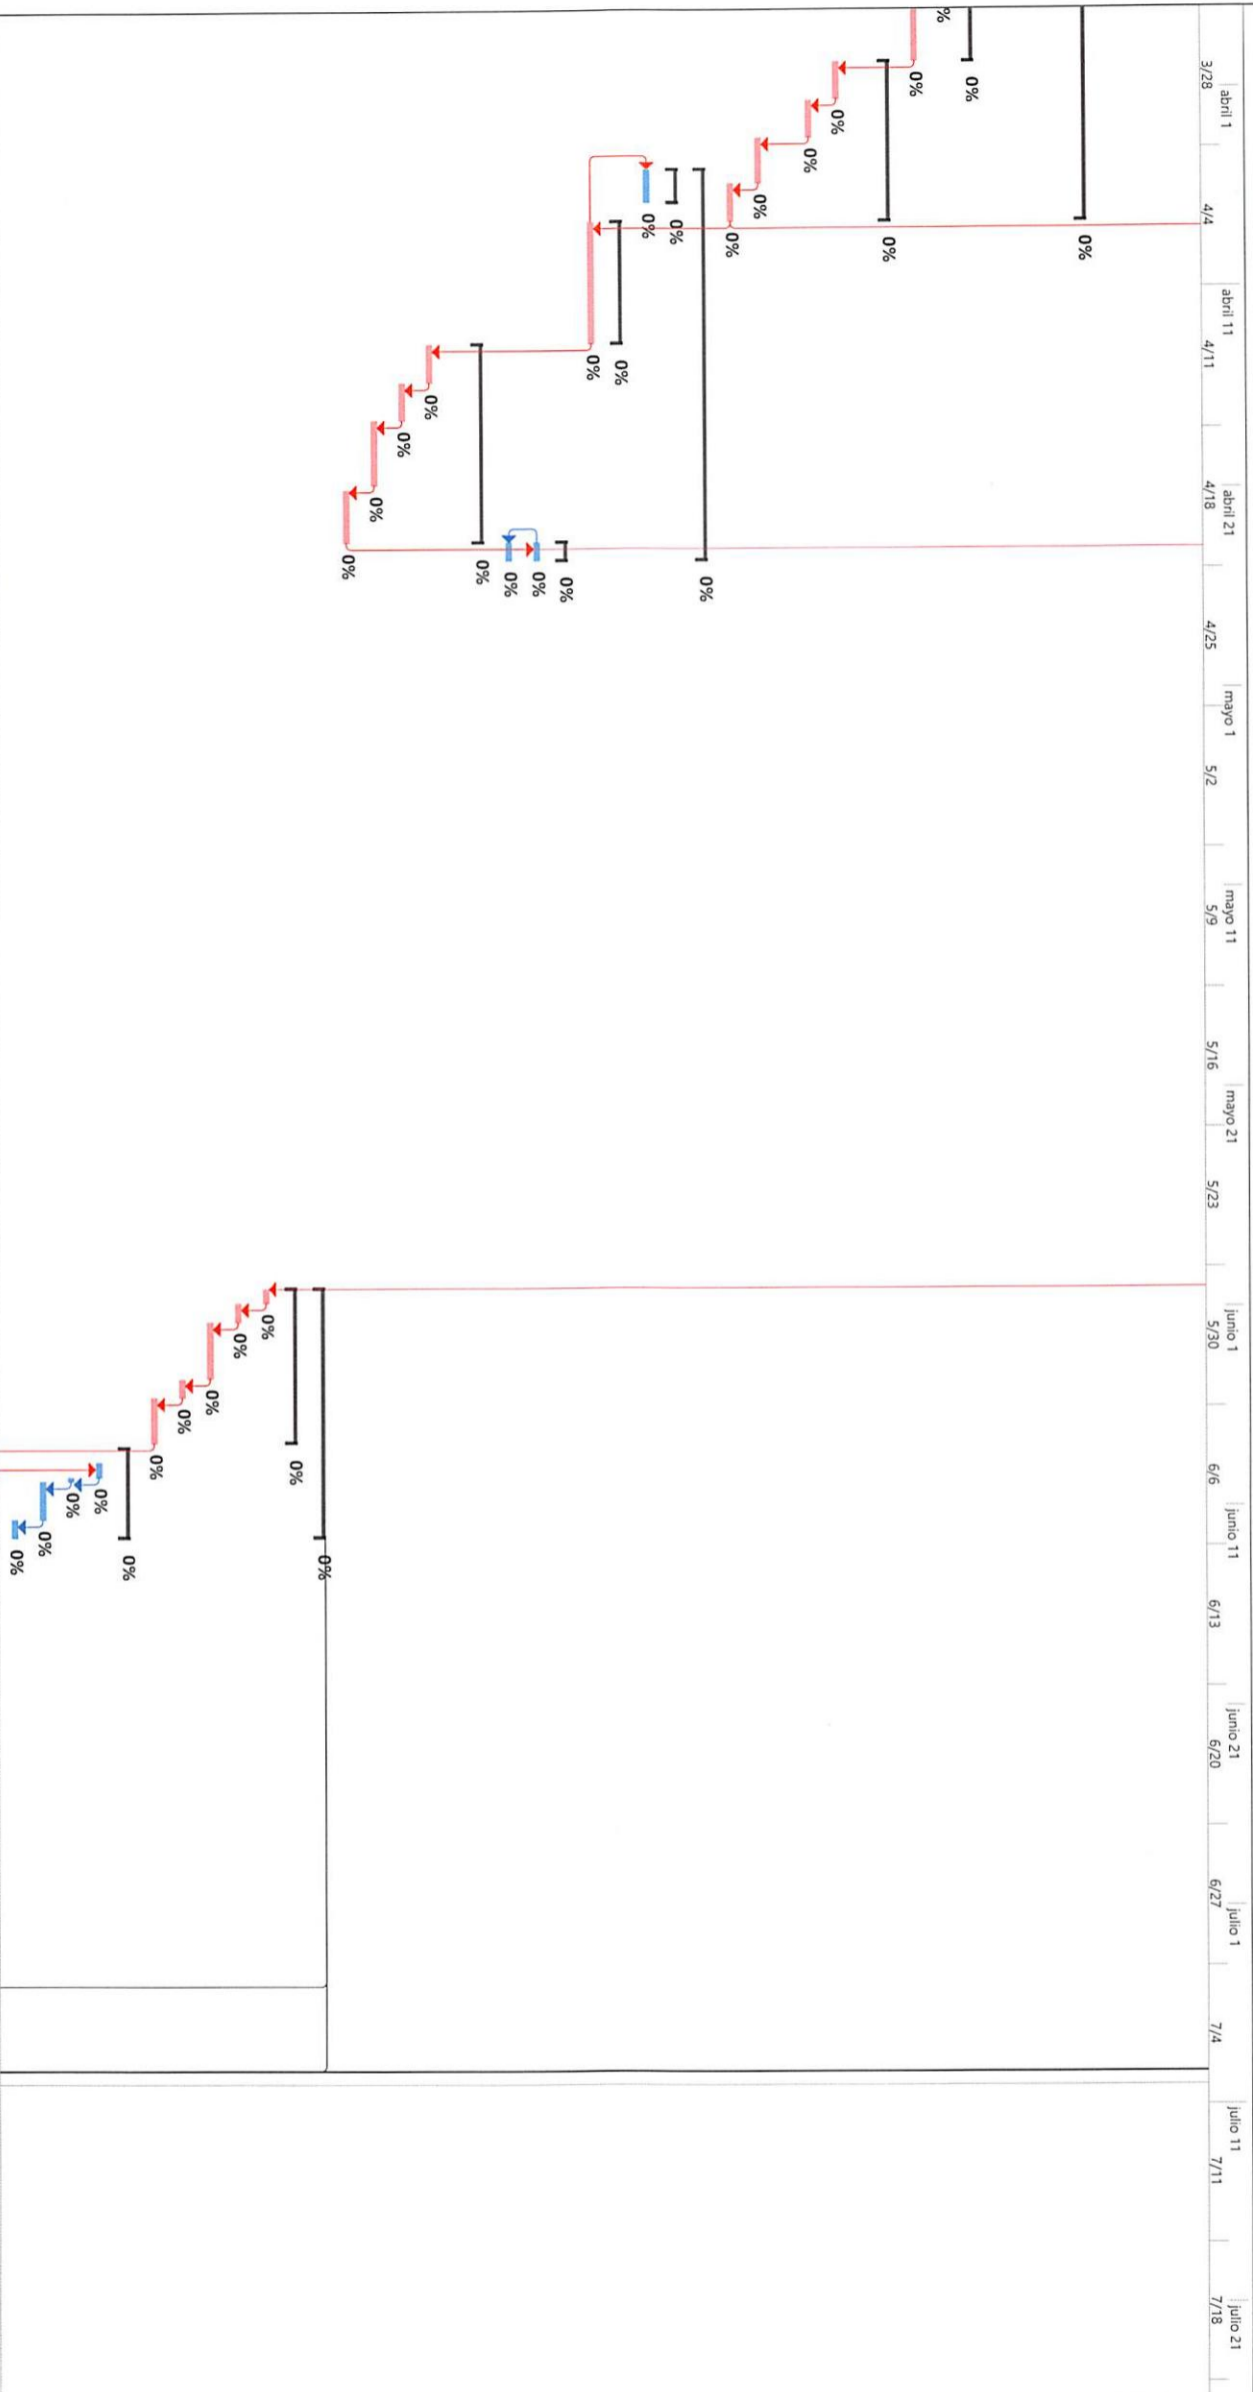

CRONOGRAMA ACUEDUCTO ZONA 4
 LINEA DE IMPULSION 12"
 SANTO DOMINGO-MONTE PLATA

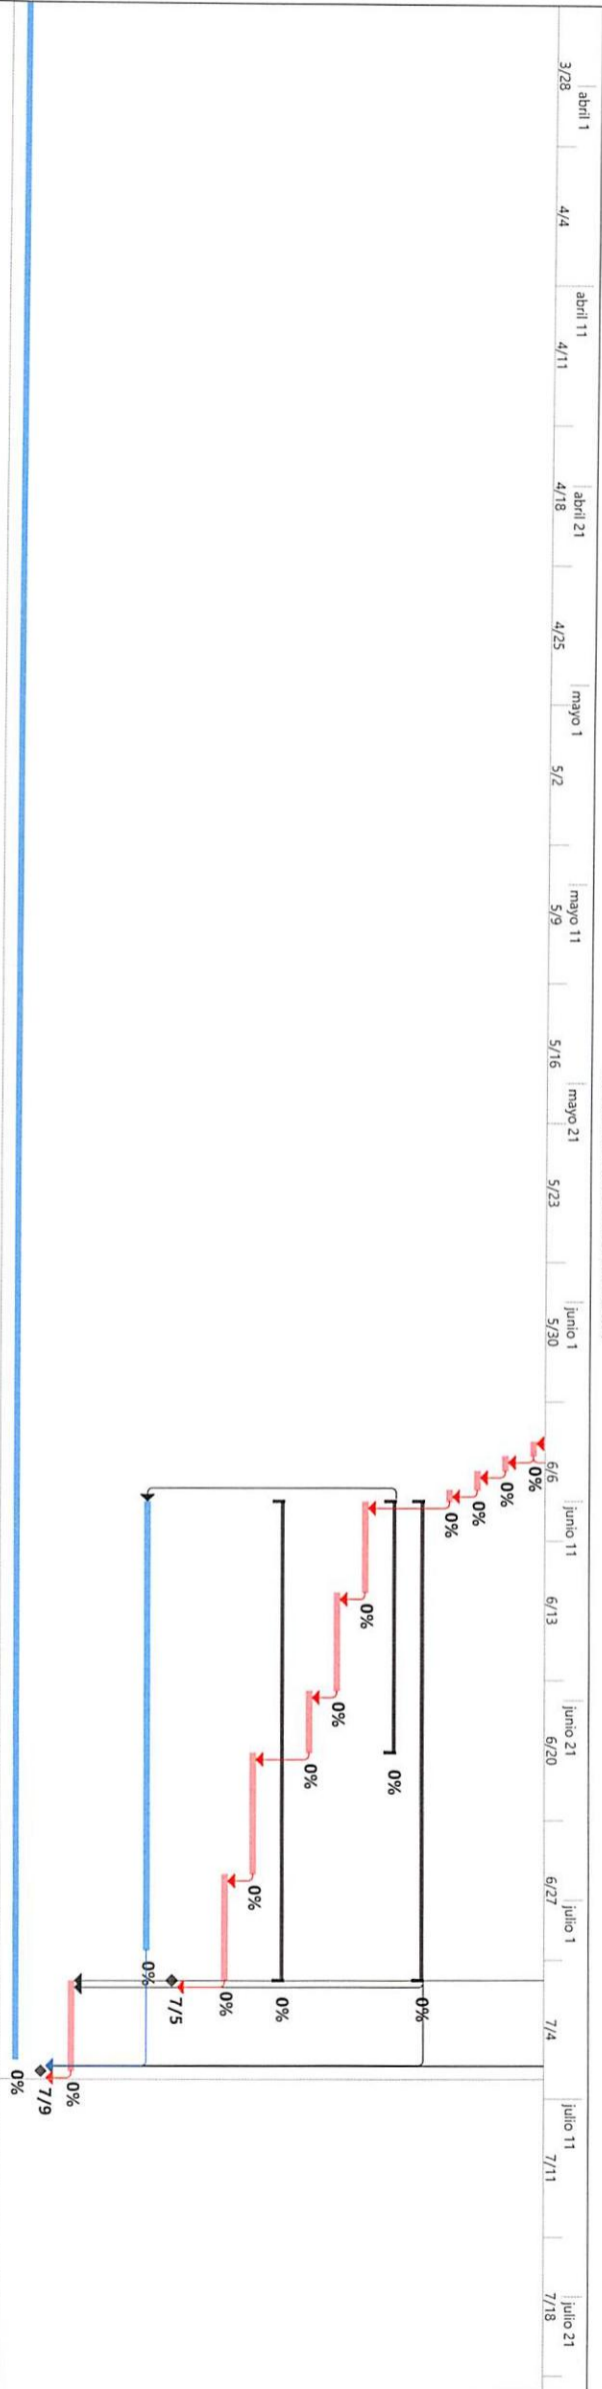

ID	Task Mode	Task Name	Duration	Start	Finish	24 Jan '21								
						W	T	F	S	S	M	T	W	T
0		CRONOGRAMA LINEA DE CONDUCCION TRAMO DESDE EST. 2+356.60 HASTA EST. 3+372.40	365 days	Tue 19/1/21	Mon 17/1/22									
1														
2														
3		LINEA DE CONDUCCION LOS BOTADOS (DESDE ESTACION 2+359.60 HASTA ESTACION 3+372.40)	365 days	Tue 19/1/21	Mon 17/1/22									
4														
5		REPLANTEO	45 days	Tue 19/1/21	Thu 4/3/21									
6														
7		MOVIMIENTO DE TIERRA	212 days	Thu 10/6/21	Fri 7/1/22									
8		EXCAVACION MATERIAL COMPACTO C/EQUIPO (DENTRO DEL VOLUMEN TOTAL, PARA LONG. 120.00M LA ZANJA TENDRA UN ANCHO =1.45M, DONDE SE COLOCARA UN TRAMO DE LA RED DISTRIBUCION Ø3" JUNTO A LA DE 12" DE CONDUCCION)	62 days	Thu 10/6/21	Wed 11/8/21									
9		ASIENTO DE ARENA	13 days	Wed 11/8/21	Tue 24/8/21									
10		RELLENO COMPACTADO C/COMPACTADOR MECANICO EN CAPAS DE 0.20M	10 days	Thu 23/12/21	Mon 3/1/22									

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

ID	Task Mode	Task Name	Duration	Start	Finish	24 Jan '21								
						W	T	F	S	S	M	T	W	T
11		BOTE DE MATERIAL CON CAMION, INCLUYE CARGIO Y ESPARCIMIENTO EN BOTADERO (DIST.=5.0 KM)	5 days	Mon 3/1/22	Fri 7/1/22									
12														
13		SUMINISTRO DE TUBERIAS	5 days	Wed 9/6/21	Mon 14/6/21									
14		Ø12" PVC (SDR-26) C/JUNTA DE GOMA + 4 % PERD. P/CAMPANA (LINEA CONDUCCION)	2 days	Wed 9/6/21	Thu 10/6/21									
15		Ø6" PVC (SDR-26) C/JUNTA DE GOMA + 3 % PERD. P/CAMPANA (RED DE DISTRIBUCION)	1 day	Thu 10/6/21	Fri 11/6/21									
16		Ø4" PVC (SDR-26) C/JUNTA DE GOMA + 2 % PERD. P/CAMPANA (RED DE DISTRIBUCION)	1 day	Fri 11/6/21	Sat 12/6/21									
17		Ø3" PVC (SDR-26) C/JUNTA DE GOMA + 2 % PERD. P/CAMPANA (RED DE DISTRIBUCION)	1 day	Sat 12/6/21	Mon 14/6/21									
18														
19		COLOCACION DE TUBERIAS (SE COLOCARAN EN LA MISMA ZANJA)	107.5 days	Tue 24/8/21	Thu 9/12/21									

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

ID	Task Mode	Task Name	Duration	Start	Finish	24 Jan '21								
						W	T	F	S	S	M	T	W	T
20		Ø12" PVC (SDR-26) C/JUNTA DE GOMA + 4 % PERD. P/CAMPANA (LINEA CONDUCCION)	50 days	Tue 24/8/21	Wed 13/10/21									
21		Ø6" PVC (SDR-26) C/JUNTA DE GOMA + 3 % PERD. P/CAMPANA (RED DE DISTRIBUCION)	23 days	Thu 14/10/21	Fri 5/11/21									
22		Ø4" PVC (SDR-26) C/JUNTA DE GOMA + 2 % PERD. P/CAMPANA (RED DE DISTRIBUCION)	32 days	Mon 8/11/21	Thu 9/12/21									
23		Ø3" PVC (SDR-26) C/JUNTA DE GOMA + 2 % PERD. P/CAMPANA (RED DE DISTRIBUCION)	18 days	Thu 14/10/21	Tue 2/11/21									
24		SUMINISTRO Y COLOCACION DE PIEZAS C/PROTECCION ANTICORROSIVA	62 days	Wed 13/10/21	Tue 14/12/21									
25														
26		TEE 12"X 6" ACERO (SCH-30)	1 day	Wed 13/10/21	Thu 14/10/21									
27		TEE 12"X 4" ACERO (SCH-30)	1 day	Thu 14/10/21	Fri 15/10/21									
28		TEE 12"X 3" ACERO (SCH-30)	1 day	Fri 15/10/21	Fri 15/10/21									
29		TEE 6"X 4" ACERO (SCH-40)	1 day	Fri 5/11/21	Sat 6/11/21									
30		TEE 6"X 3" ACERO (SCH-40)	1 day	Sat 6/11/21	Mon 8/11/21									
31		TEE 4"X 4" ACERO (SCH-80)	1 day	Thu 9/12/21	Fri 10/12/21									

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

ID	Task Mode	Task Name	Duration	Start	Finish	24 Jan '21								
						W	T	F	S	S	M	T	W	T
32		TEE 4"X 3" ACERO (SCH-80)	1 day	Fri 10/12/21	Sat 11/12/21									
33		TEE 3"X 3" ACERO (SCH-80)	1 day	Tue 2/11/21	Tue 2/11/21									
34		CODO 12"X 22.5" ACERO (SCH-30)	1 day	Wed 13/10/21	Thu 14/10/21									
35		CODO 6"X 90" ACERO (SCH-40)	1 day	Fri 5/11/21	Sat 6/11/21									
36		CODO 3"X 45" ACERO (SCH-80)	1 day	Tue 2/11/21	Tue 2/11/21									
37		CODO 3"X 22.5" ACERO (SCH-80)	1 day	Tue 2/11/21	Wed 3/11/21									
38		CODO 3"X 90" ACERO (SCH-30) C/PROTECCION ANTICORROSIVA	1 day	Wed 3/11/21	Thu 4/11/21									
39		CRUZ 6"X 6" ACERO (SCH-40)	1.5 days	Fri 5/11/21	Mon 8/11/21									
40		CRUZ 4"X 3" ACERO (SCH-80)	1.5 days	Thu 9/12/21	Fri 10/12/21									
41		CRUZ 4"X 3" ACERO (SCH-80)	1.5 days	Fri 10/12/21	Mon 13/12/21									
42		YEE 4"X 3" ACERO (SCH-40) C/PROTECCION ANTICORROSIVA	1.5 days	Mon 13/12/21	Tue 14/12/21									
43		REDUCCION 12"X 3" ACERO (SCH-30)	1.5 days	Wed 13/10/21	Thu 14/10/21									
44		REDUCCION 6"X 4" ACERO (SCH-40)	1.5 days	Fri 5/11/21	Mon 8/11/21									
45		REDUCCION 6"X 3" ACERO (SCH-40)	1.5 days	Mon 8/11/21	Tue 9/11/21									
46		REDUCCION 4"X 3" ACERO (SCH-80)	1.5 days	Tue 9/11/21	Wed 10/11/21									
47		NIPLE 12" X 1.00 M ACERO (SCH-30) C/PROTECCION ANTICORROSIVA	1.5 days	Wed 13/10/21	Thu 14/10/21									
48		NIPLE 6" X 1.00 M ACERO (SCH-40)	1.5 days	Fri 5/11/21	Mon 8/11/21									
49		NIPLE 4" X 1.00 M ACERO (SCH-80)	2.5 days	Thu 9/12/21	Sat 11/12/21									

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

ID	Task Mode	Task Name	Duration	Start	Finish	24 Jan '21								
						W	T	F	S	S	M	T	W	T
50		NIPLE 3" X 1.00 M ACERO (SCH-80)	2.5 days	Tue 2/11/21	Thu 4/11/21									
51		JUNTA MECANICA TIPO DRESSER DE Ø 12" HF	4 days	Wed 13/10/21	Mon 18/10/21									
52		JUNTA MECANICA TIPO DRESSER DE Ø 6" HF	4 days	Fri 5/11/21	Wed 10/11/21									
53		JUNTA MECANICA TIPO DRESSER DE Ø 4" HF	4 days	Thu 9/12/21	Tue 14/12/21									
54		JUNTA MECANICA TIPO DRESSER DE Ø 3" HF	4 days	Tue 2/11/21	Fri 5/11/21									
55		ANCLAJE H.A. P/PIEZAS ESPECIALES 12" (SEGUN DISEÑO)	4 days	Fri 5/11/21	Wed 10/11/21									
56		ANCLAJE H.S. P/PIEZAS ESPECIALES 6, 4" Y 3" (SEGUN DISEÑO)	4 days	Thu 14/10/21	Mon 18/10/21									
57														
58		SUMINISTRO Y COLOCACION DE VALVULAS	42 days	Tue 2/11/21	Tue 14/12/21									
59		VALVULA DE COMPUERTA Ø4" H.F. PLATILLADA (INC. 2 JUNTAS DE GOMA, 2 NIPLE PLATILLADOS, 2 JUNTAS MECANICAS TIPO DRESSER Y 2 PARES DE TORNILLOS)	4 days	Thu 9/12/21	Tue 14/12/21									


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

ID	Task Mode	Task Name	Duration	Start	Finish	24 Jan '21								
						W	T	F	S	S	M	T	W	T
60		VALVULA DE COMPUERTA Ø3" H.F. PLATILLADA (INC. 2 JUNTAS DE GOMA, 2 NIPLE PLATILLADOS, 2 JUNTAS MECANICAS TIPO DRESSER Y 2 PARES DE TORNILLOS)	4 days	Tue 2/11/21	Fri 5/11/21									
61		CAJA TELESCOPICA PARA VALVULA	4 days	Fri 5/11/21	Tue 9/11/21									
62														
63		PRUEBA HIDROSTATICA	10 days	Tue 14/12/21	Thu 23/12/21									
64		Ø12" PVC	2.5 days	Tue 14/12/21	Thu 16/12/21									
65		Ø6" PVC	2.5 days	Thu 16/12/21	Sat 18/12/21									
66		Ø4" PVC	2.5 days	Sat 18/12/21	Tue 21/12/21									
67		Ø3" PVC	2.5 days	Tue 21/12/21	Thu 23/12/21									
68														
69		SEÑALIZACION, MANEJO DE TRANSITO Y SEGURIDAD VIAL (INCL OBREROS,MECHONES, CONOS,CINTA, AVISO DE PELIGRO, LETREROS)	335 days	Tue 19/1/21	Fri 17/12/21									
70		LIMPIEZA CONTINUA	305 days	Thu 4/3/21	Sat 1/1/22									
71														
72		ASFALTO	320 days	Thu 4/3/21	Mon 17/1/22									
73		CORTE DE ASFALTO	65 days	Thu 4/3/21	Fri 7/5/21									
74		EXTRACCION DE ASFALTO	30 days	Fri 7/5/21	Mon 7/6/21									


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

ID	Task Mode	Task Name	Duration	Start	Finish	24 Jan '21								
						W	T	F	S	S	M	T	W	T
75		BOTE DE CARPETA ASFALTO C/CAMION D=5 KM (INC. ESPARCIMIENTO EN BOTADERO)	4 days	Mon 7/6/21	Thu 10/6/21									
76		SUMINISTRO DE MATERIAL BASE PARA RELLENO	5 days	Fri 7/1/22	Wed 12/1/22									
77		SUMINISTRO Y COLOCCION DE IMPRIMACION	2 days	Wed 12/1/22	Fri 14/1/22									
78		SUMINISTRO Y COLOCACION DE ASFALTO CALIENTE+25% DESP e= 2"	2 days	Fri 14/1/22	Mon 17/1/22									
79		TRANSPORTE DE ASFALTO CALIENTE (50.00 KM)	2 days	Fri 14/1/22	Mon 17/1/22									
80														
81														
82		VIARIOS	335 days	Tue 19/1/21	Fri 17/12/21									
83		CAMPAMENTO (INCLUYE ALQUILER DE CASA O SOLAR CON CASETA DE MATERIALES CON (IU) BAÑO MOVIL)	335 days	Tue 19/1/21	Fri 17/12/21									


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

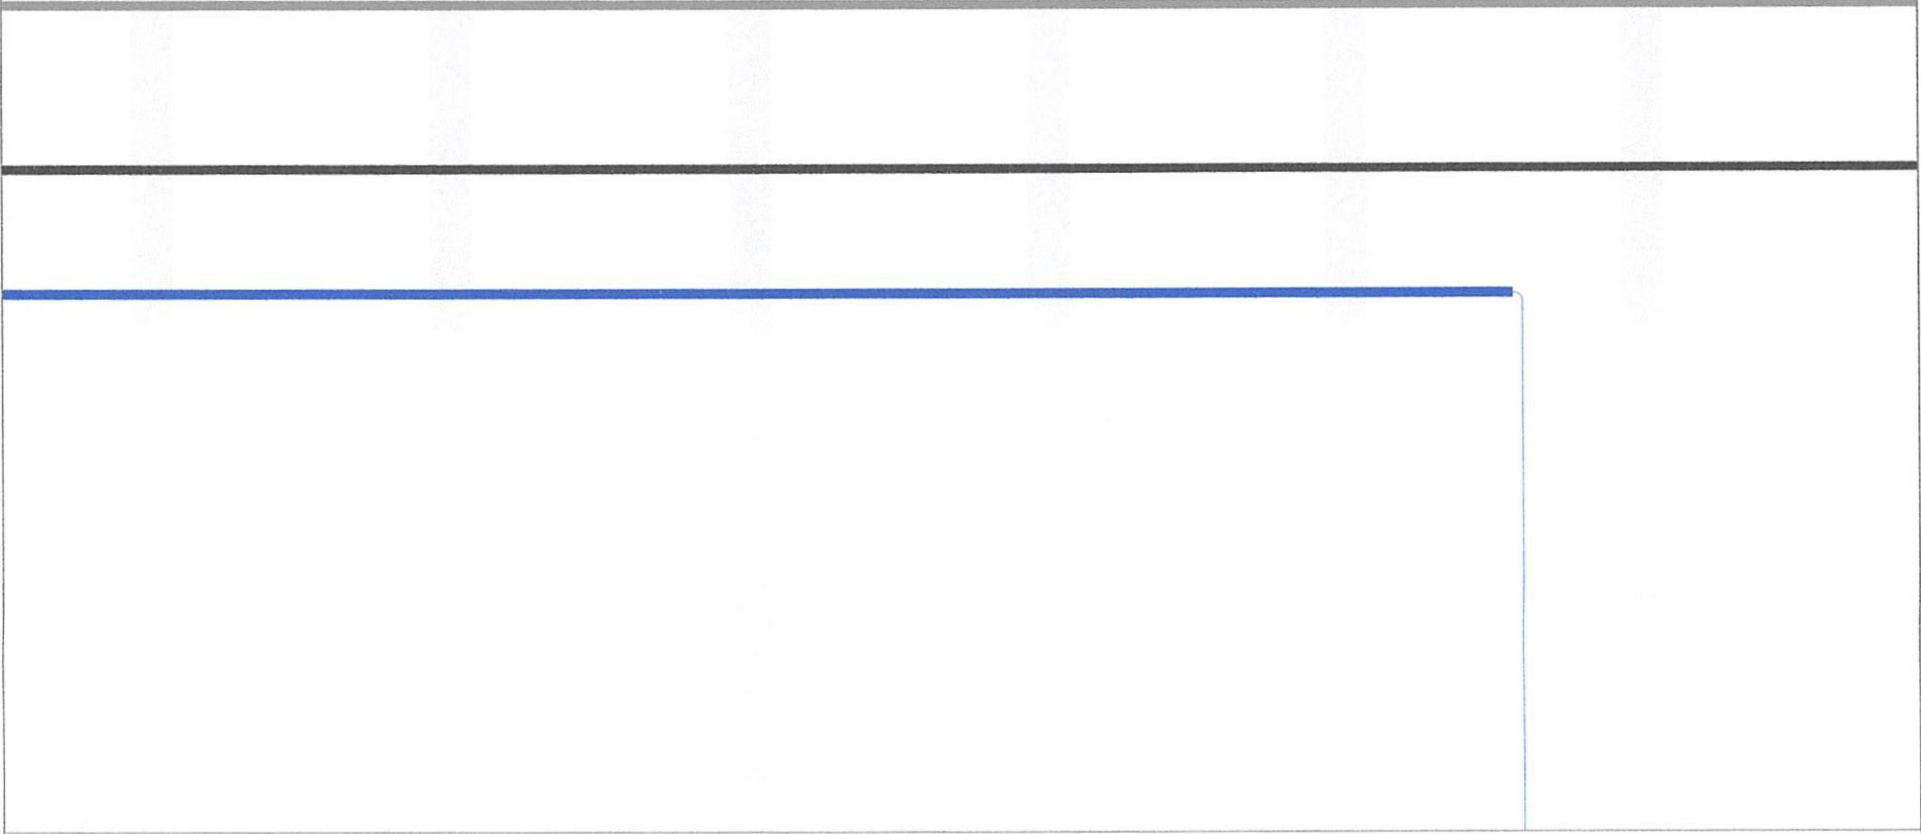


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

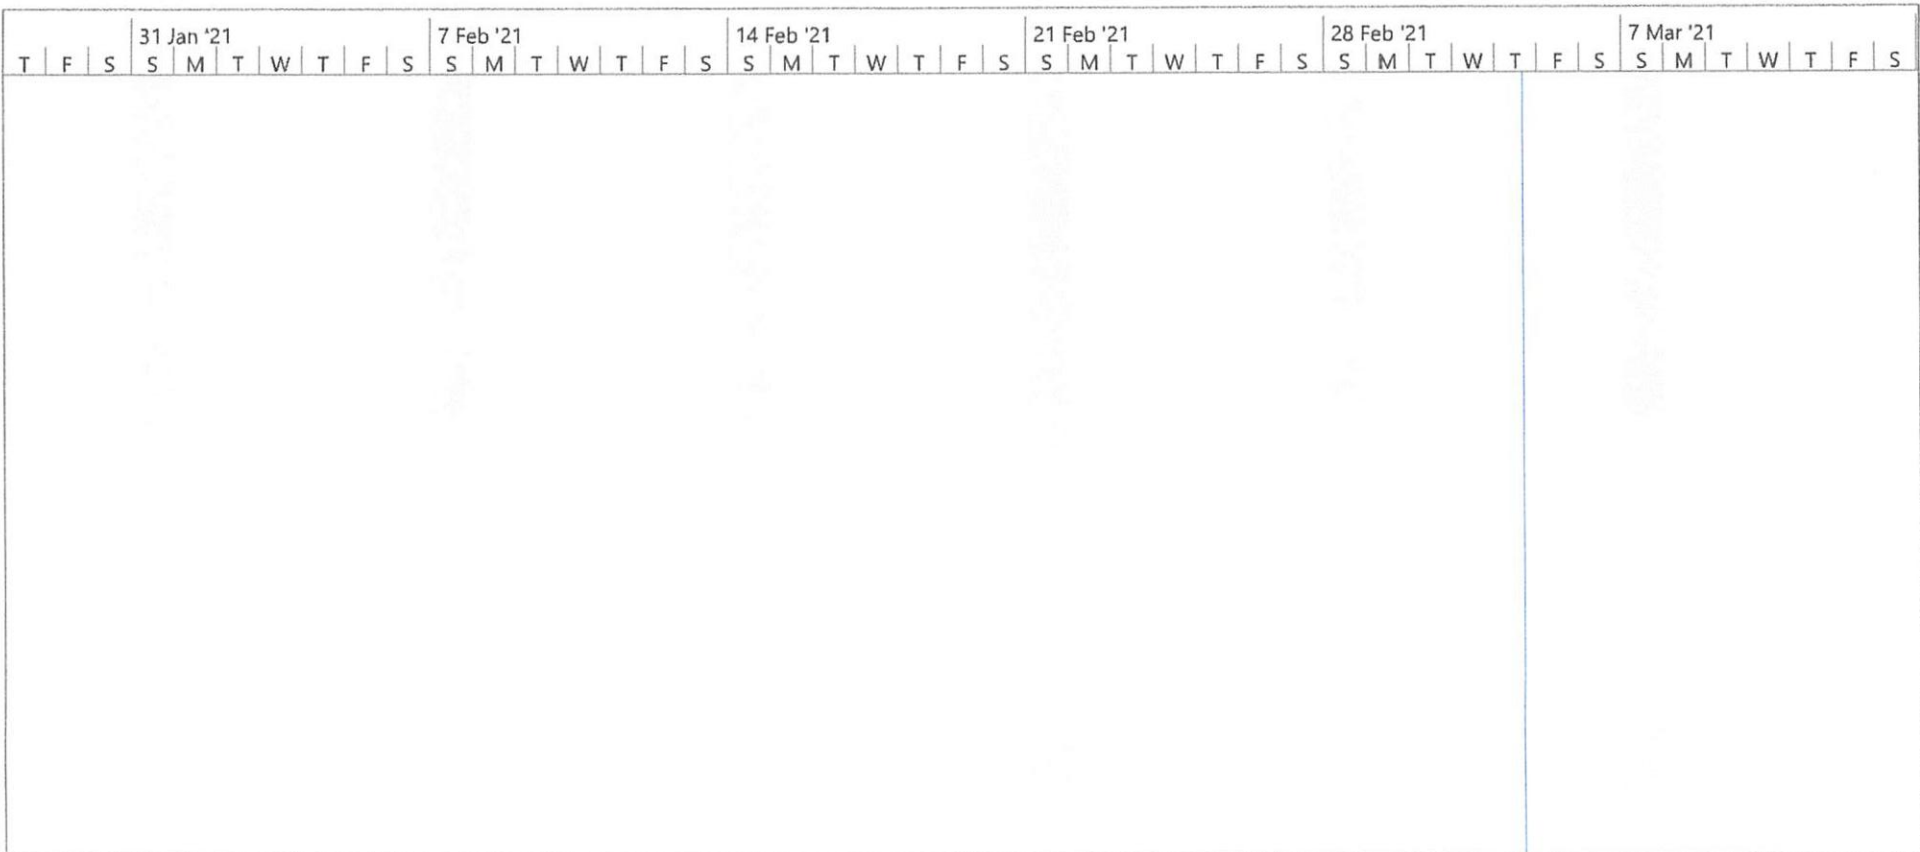


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

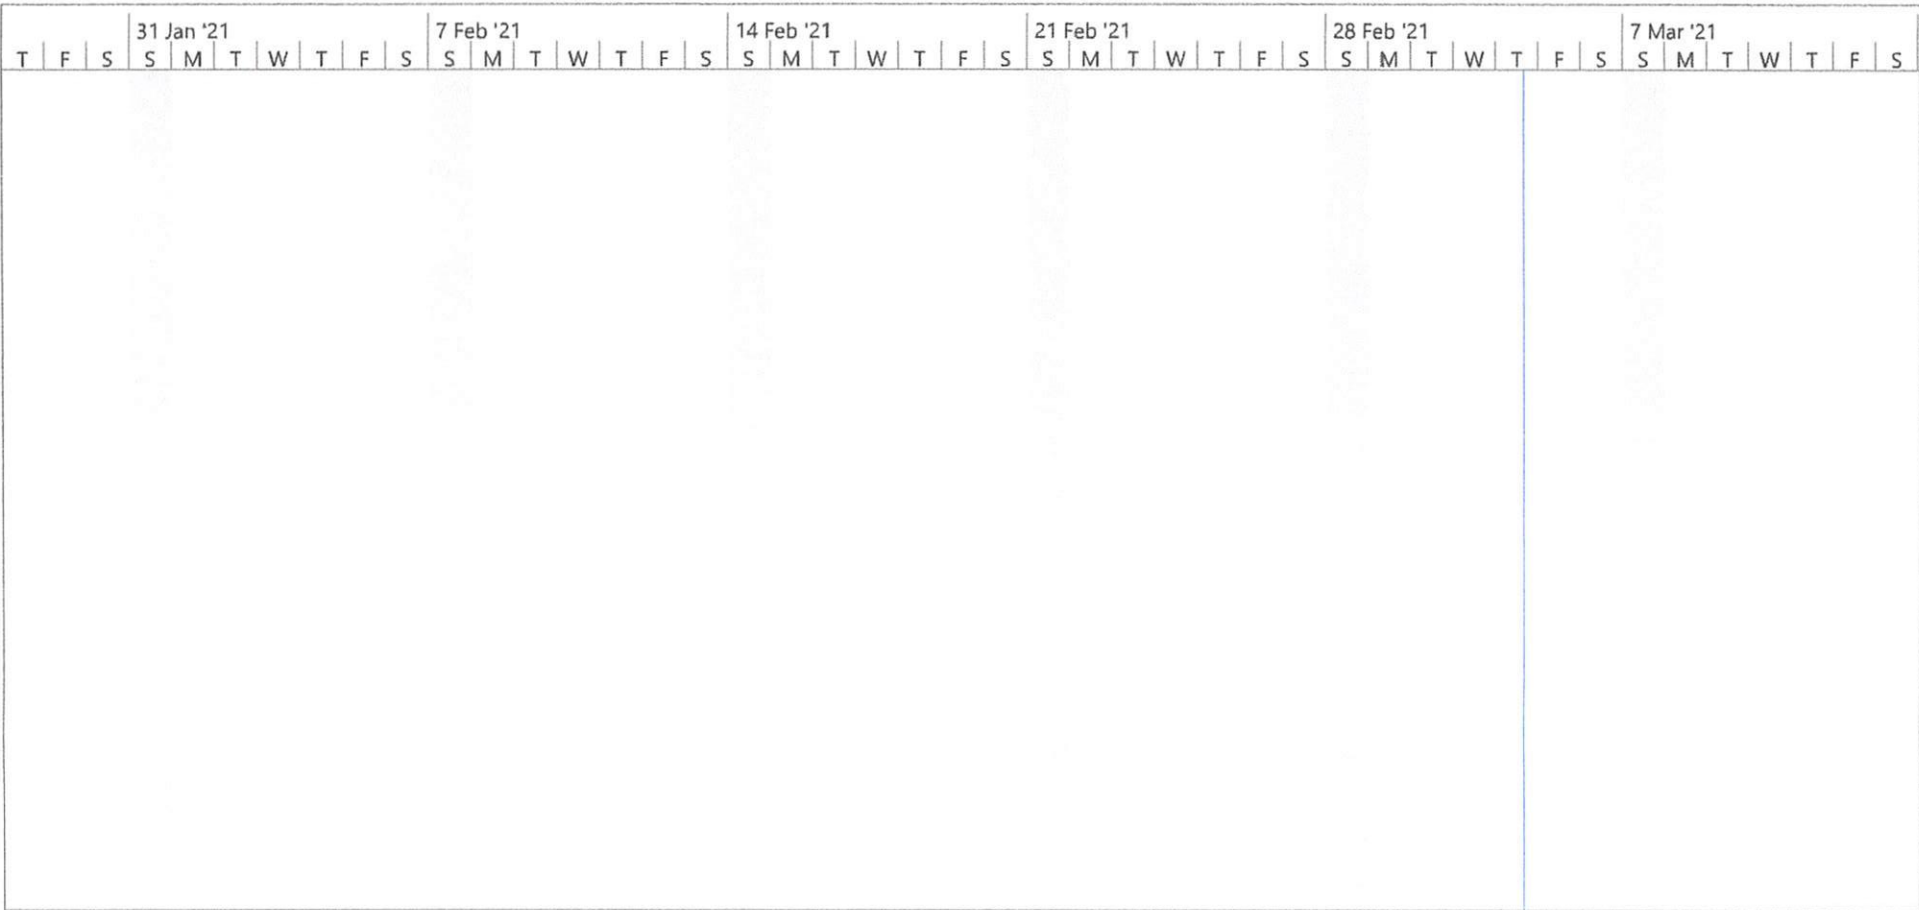


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

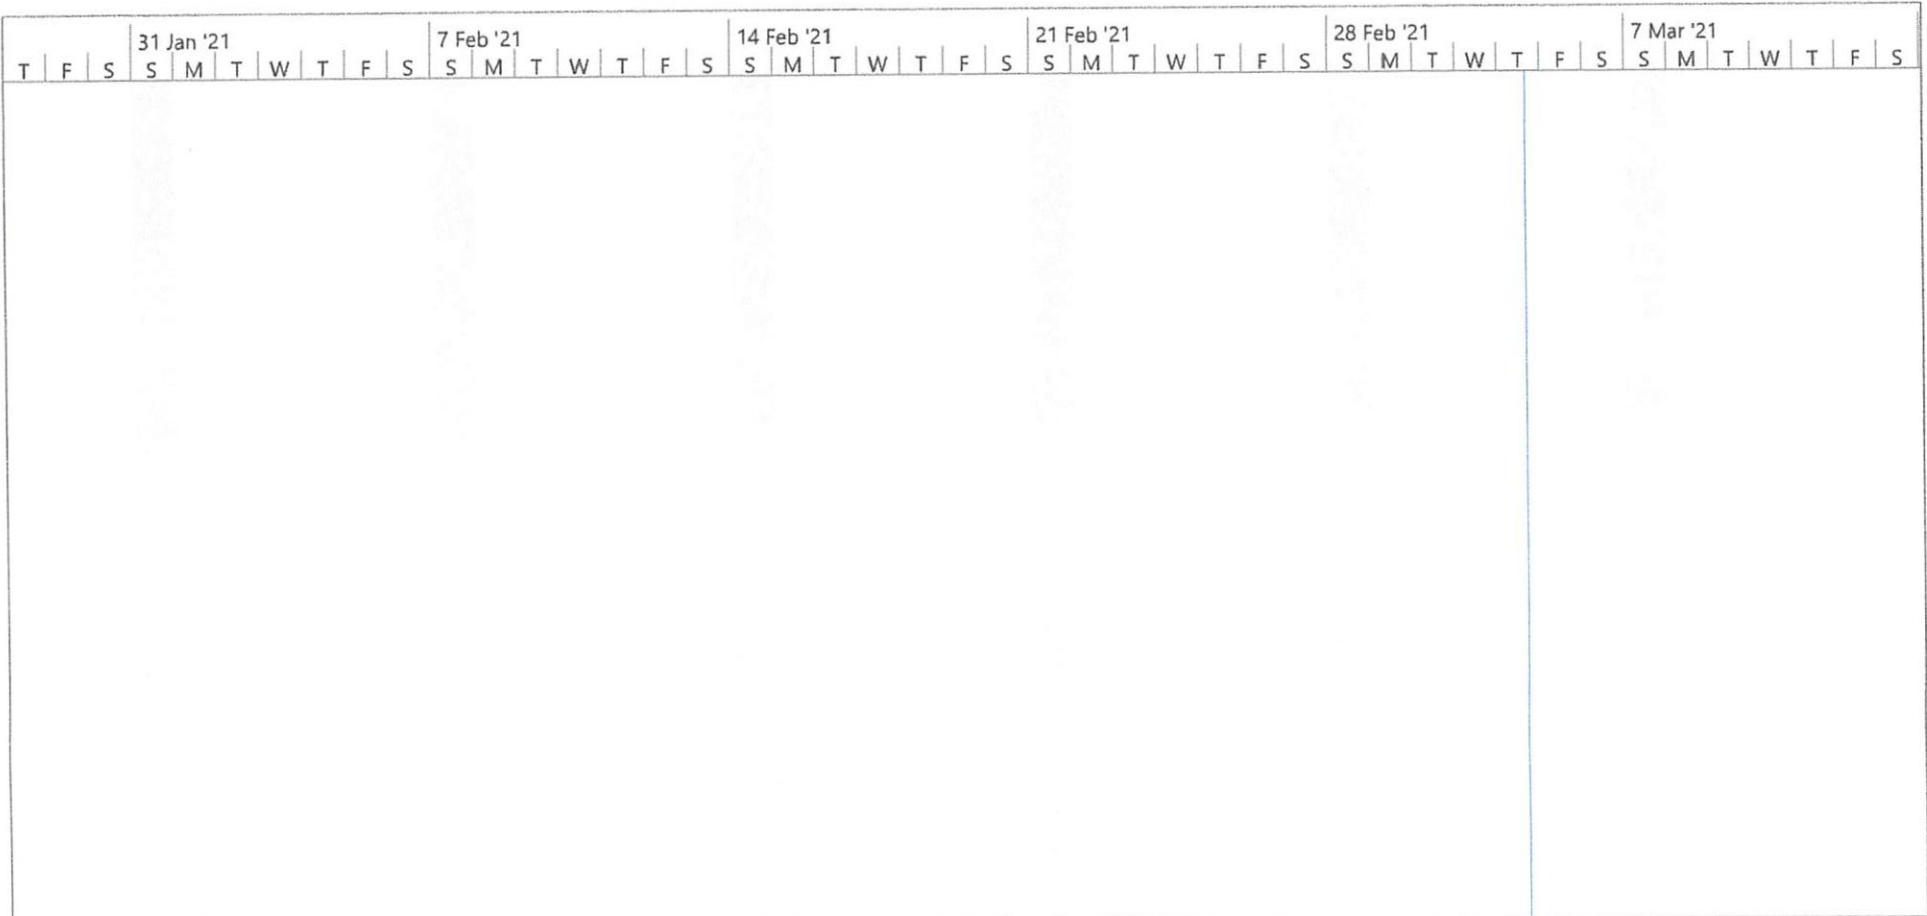


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

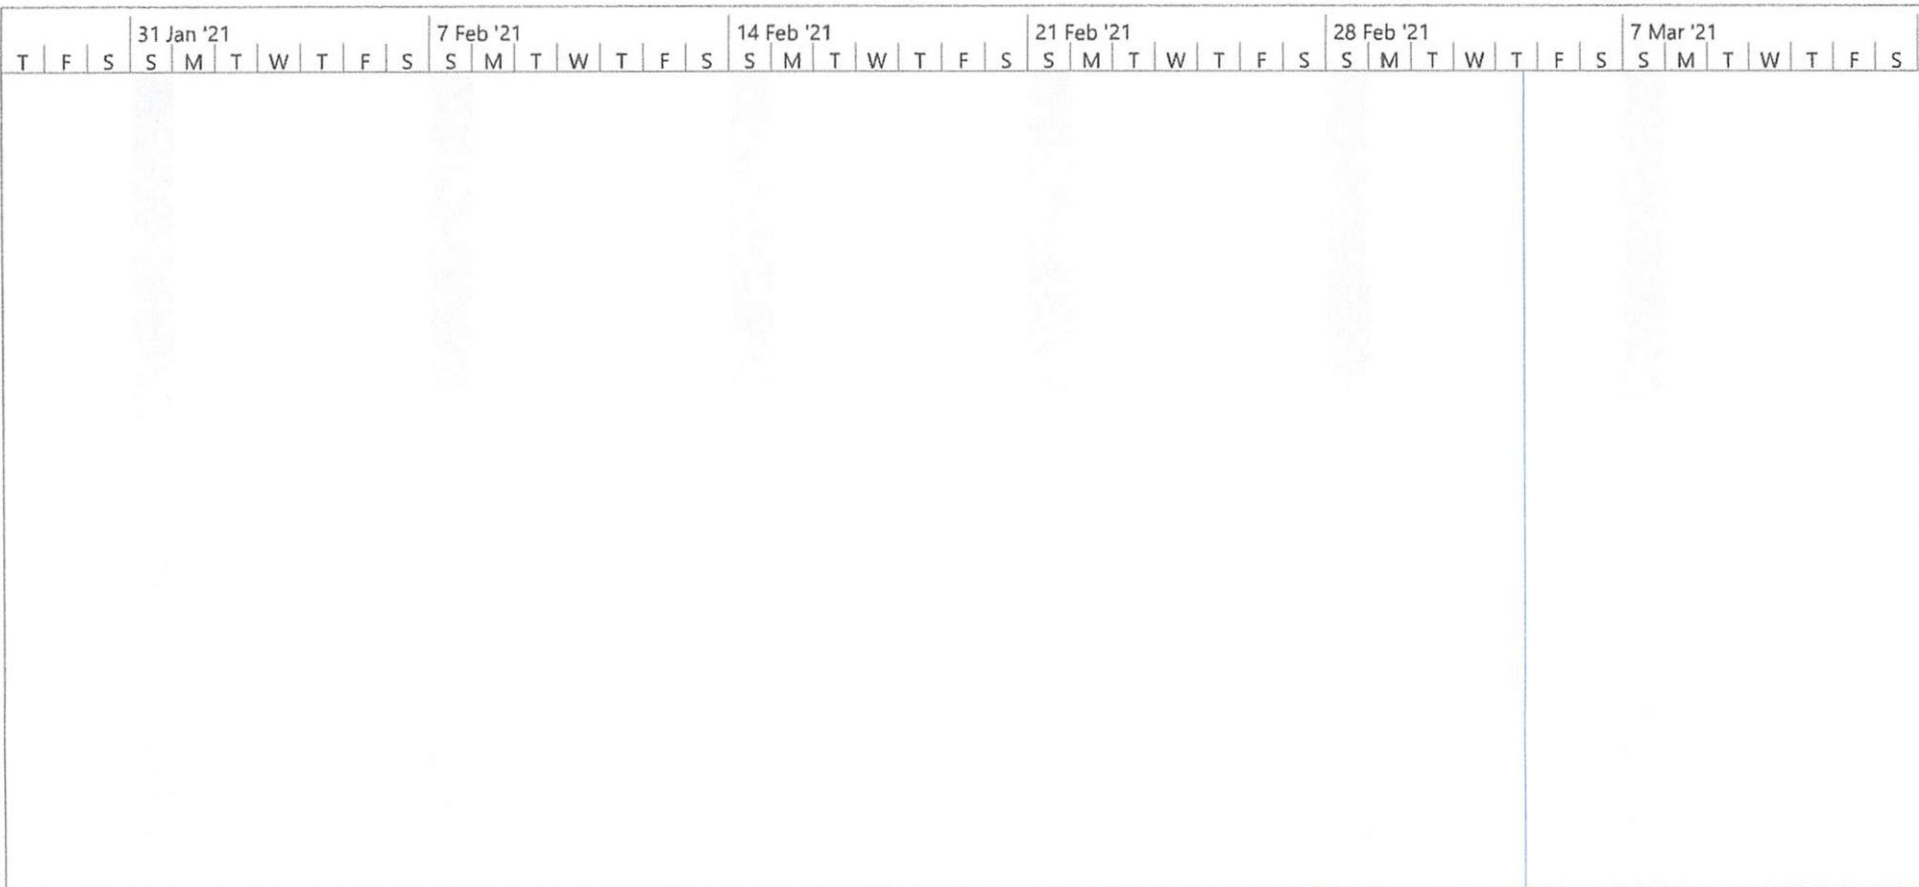

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

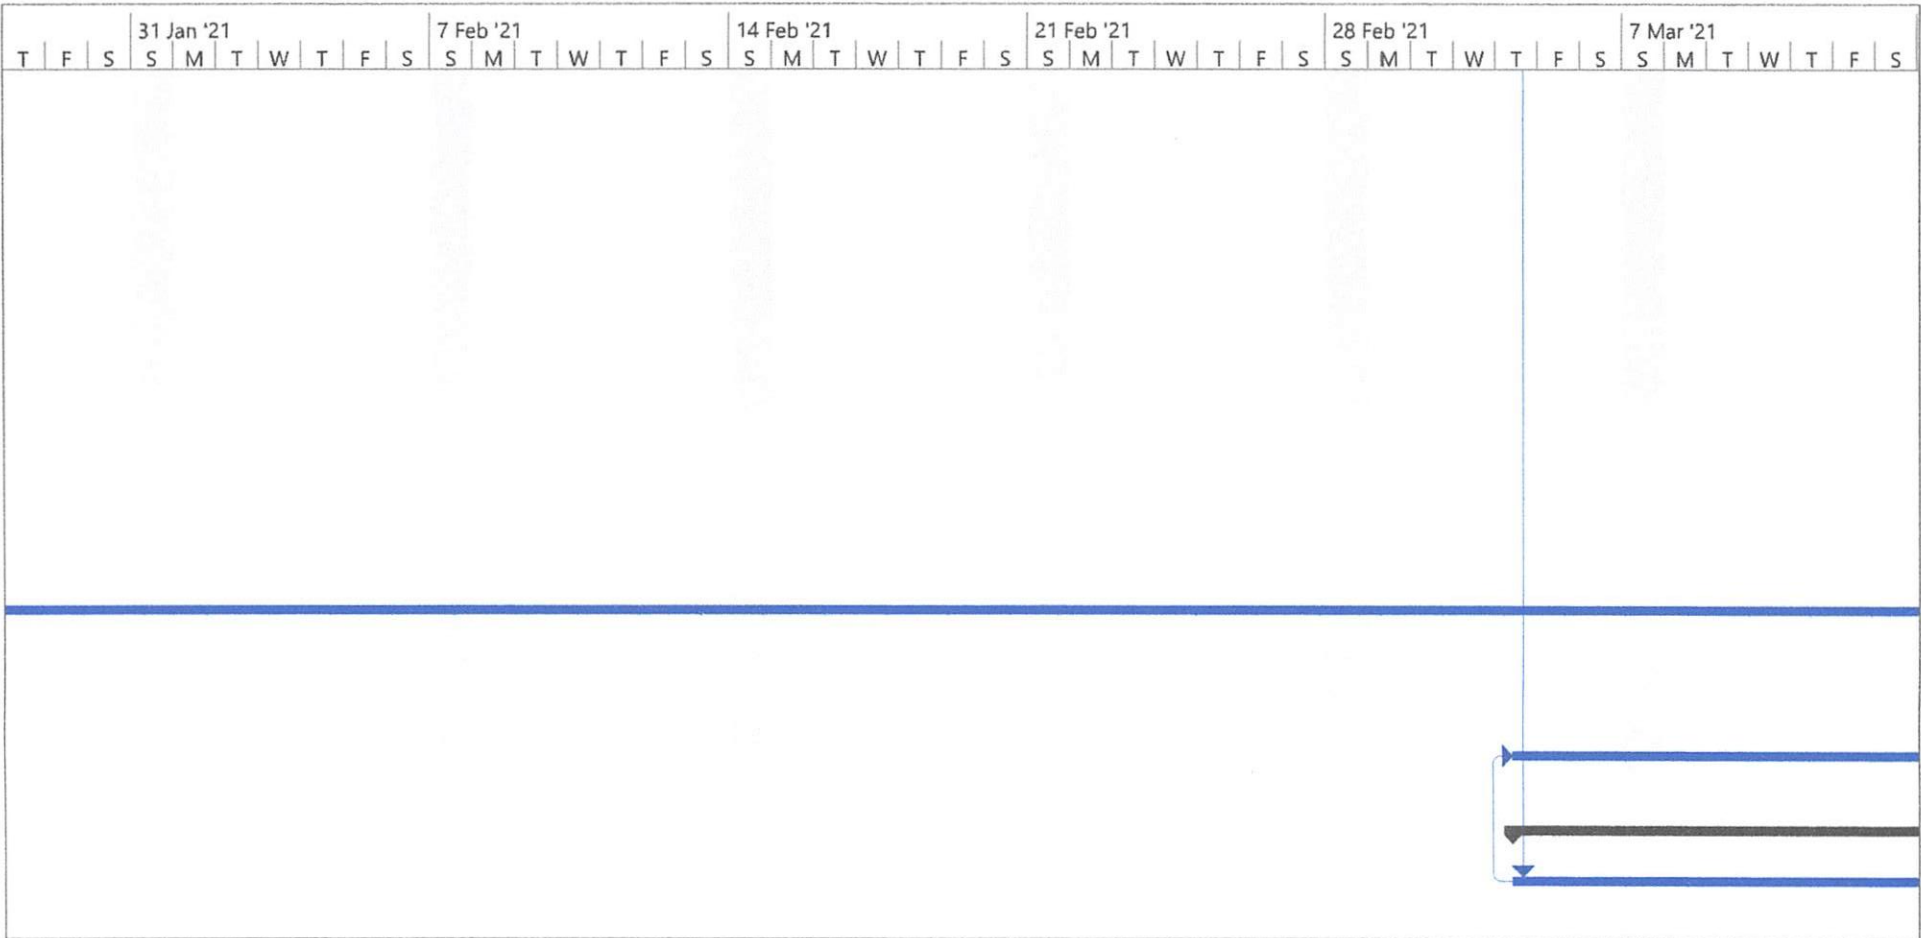


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

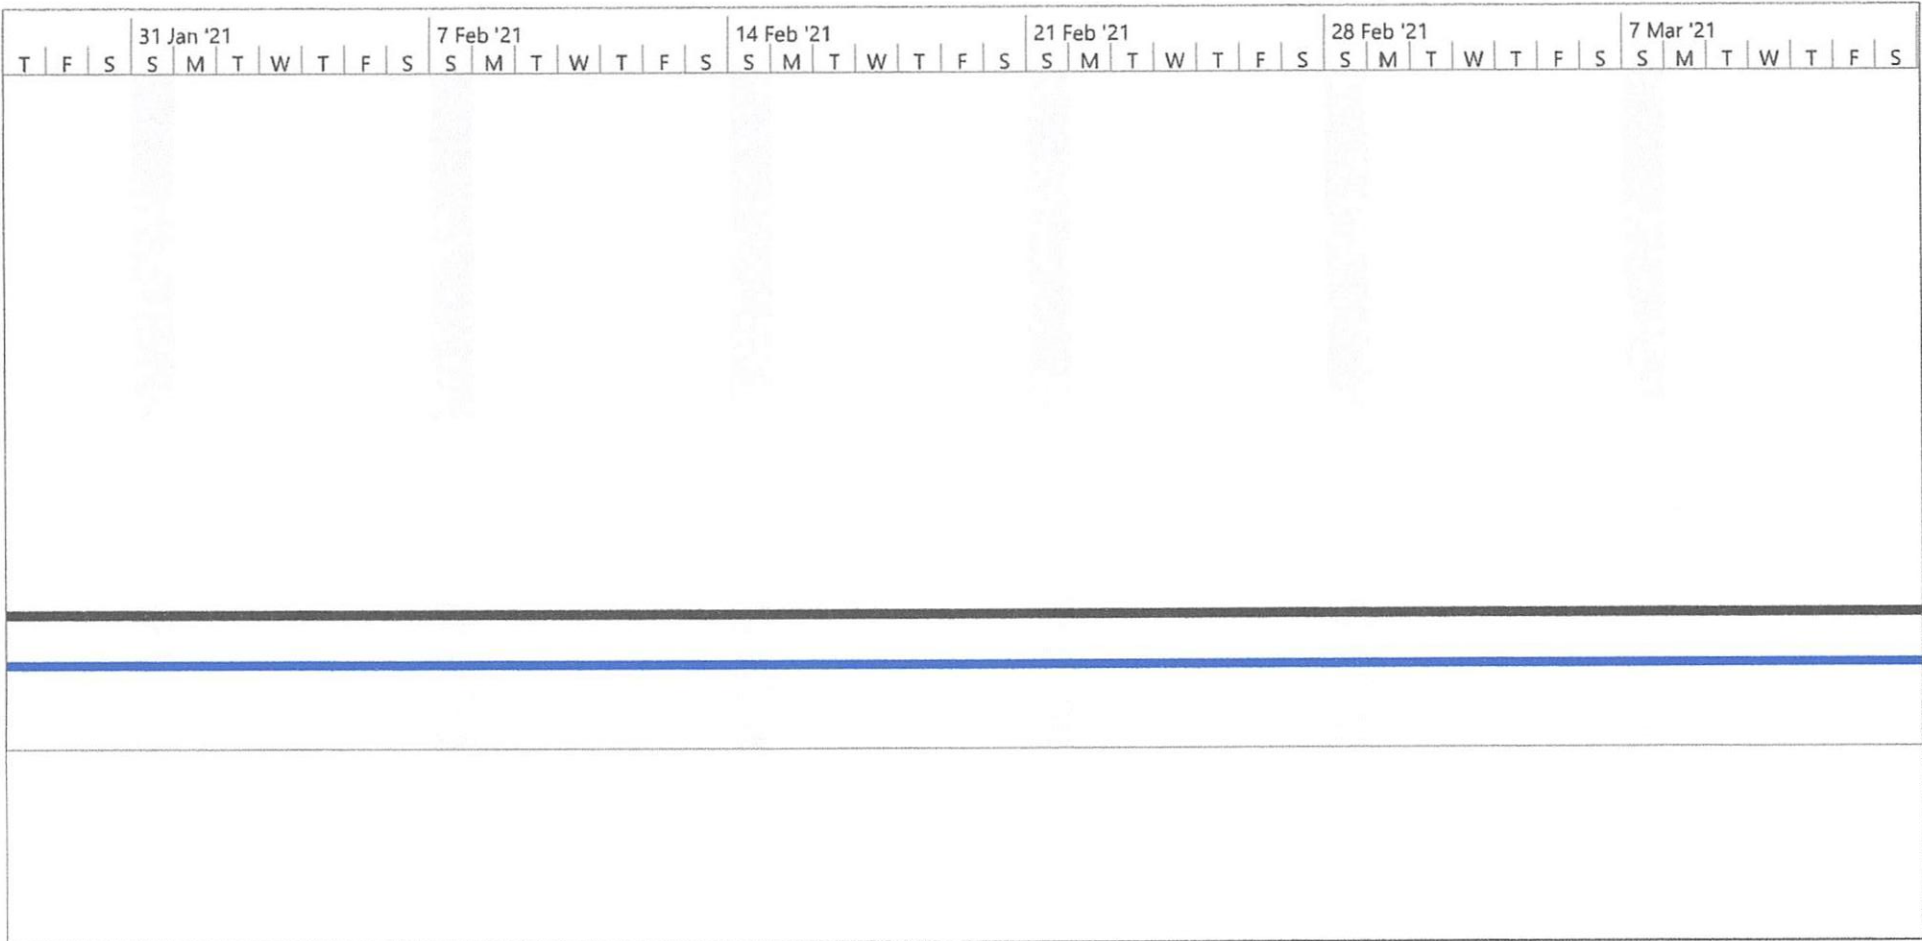

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

14 Mar '21 21 Mar '21 28 Mar '21 4 Apr '21 11 Apr '21 18 Apr '21 25 Apr '21
 S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T

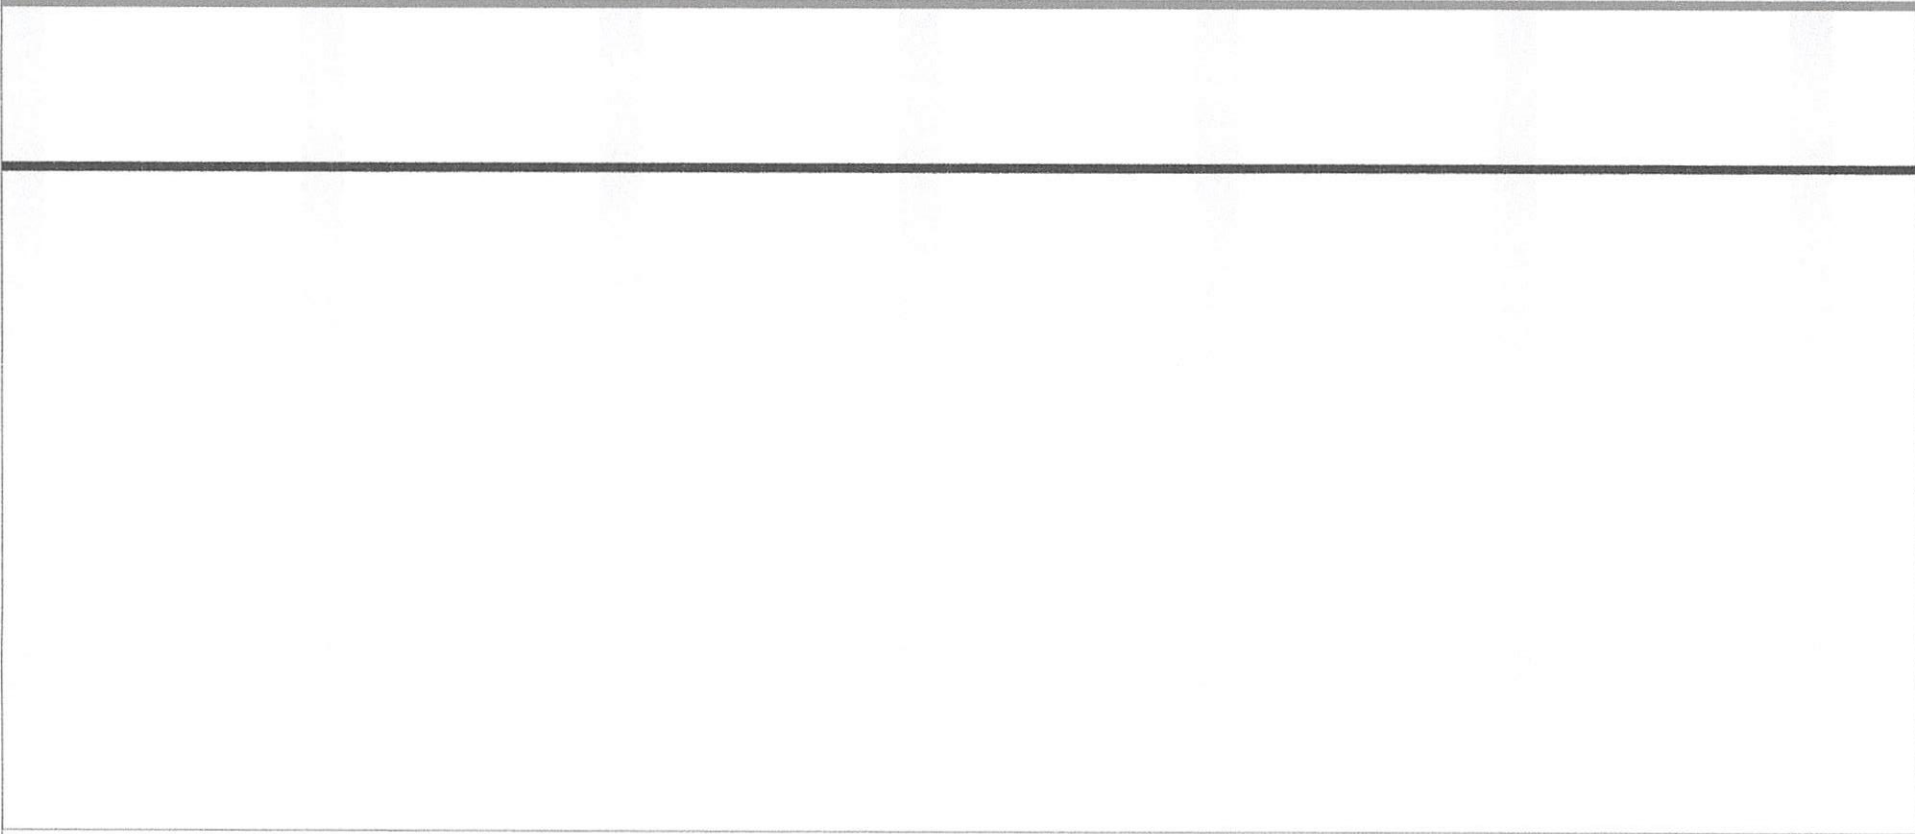


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

14 Mar '21 | 21 Mar '21 | 28 Mar '21 | 4 Apr '21 | 11 Apr '21 | 18 Apr '21 | 25 Apr '21



Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

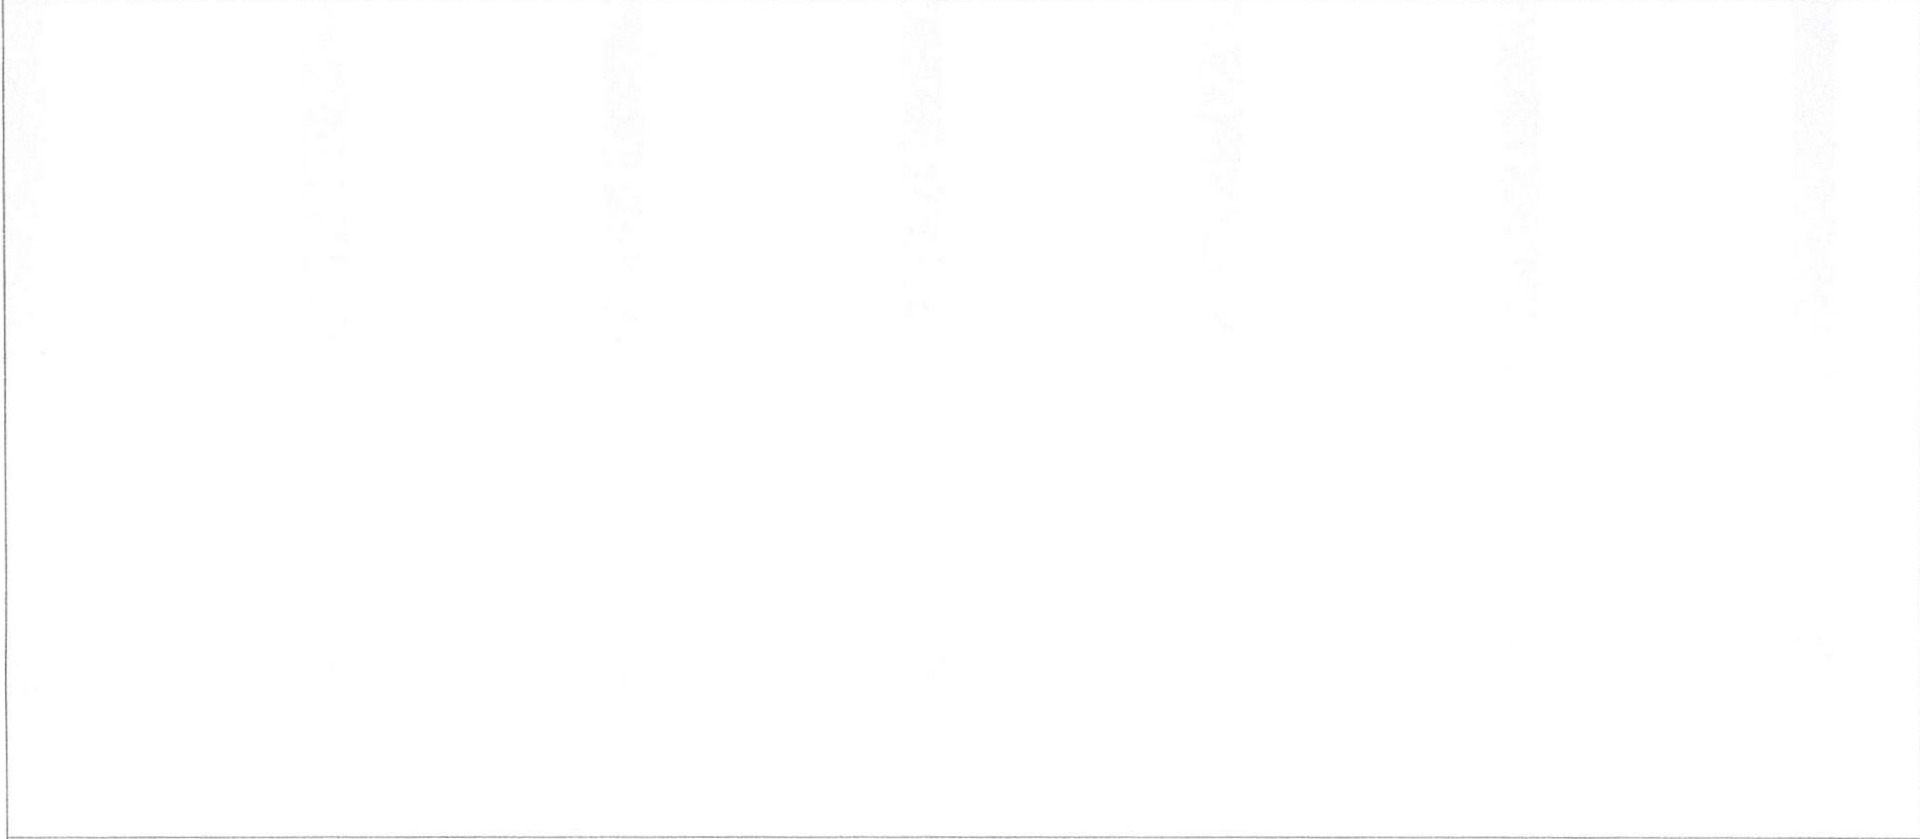

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

14 Mar '21 | 21 Mar '21 | 28 Mar '21 | 4 Apr '21 | 11 Apr '21 | 18 Apr '21 | 25 Apr '21




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

14 Mar '21 | 21 Mar '21 | 28 Mar '21 | 4 Apr '21 | 11 Apr '21 | 18 Apr '21 | 25 Apr '21
 S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T



Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

14 Mar '21 | 21 Mar '21 | 28 Mar '21 | 4 Apr '21 | 11 Apr '21 | 18 Apr '21 | 25 Apr '21
 S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T

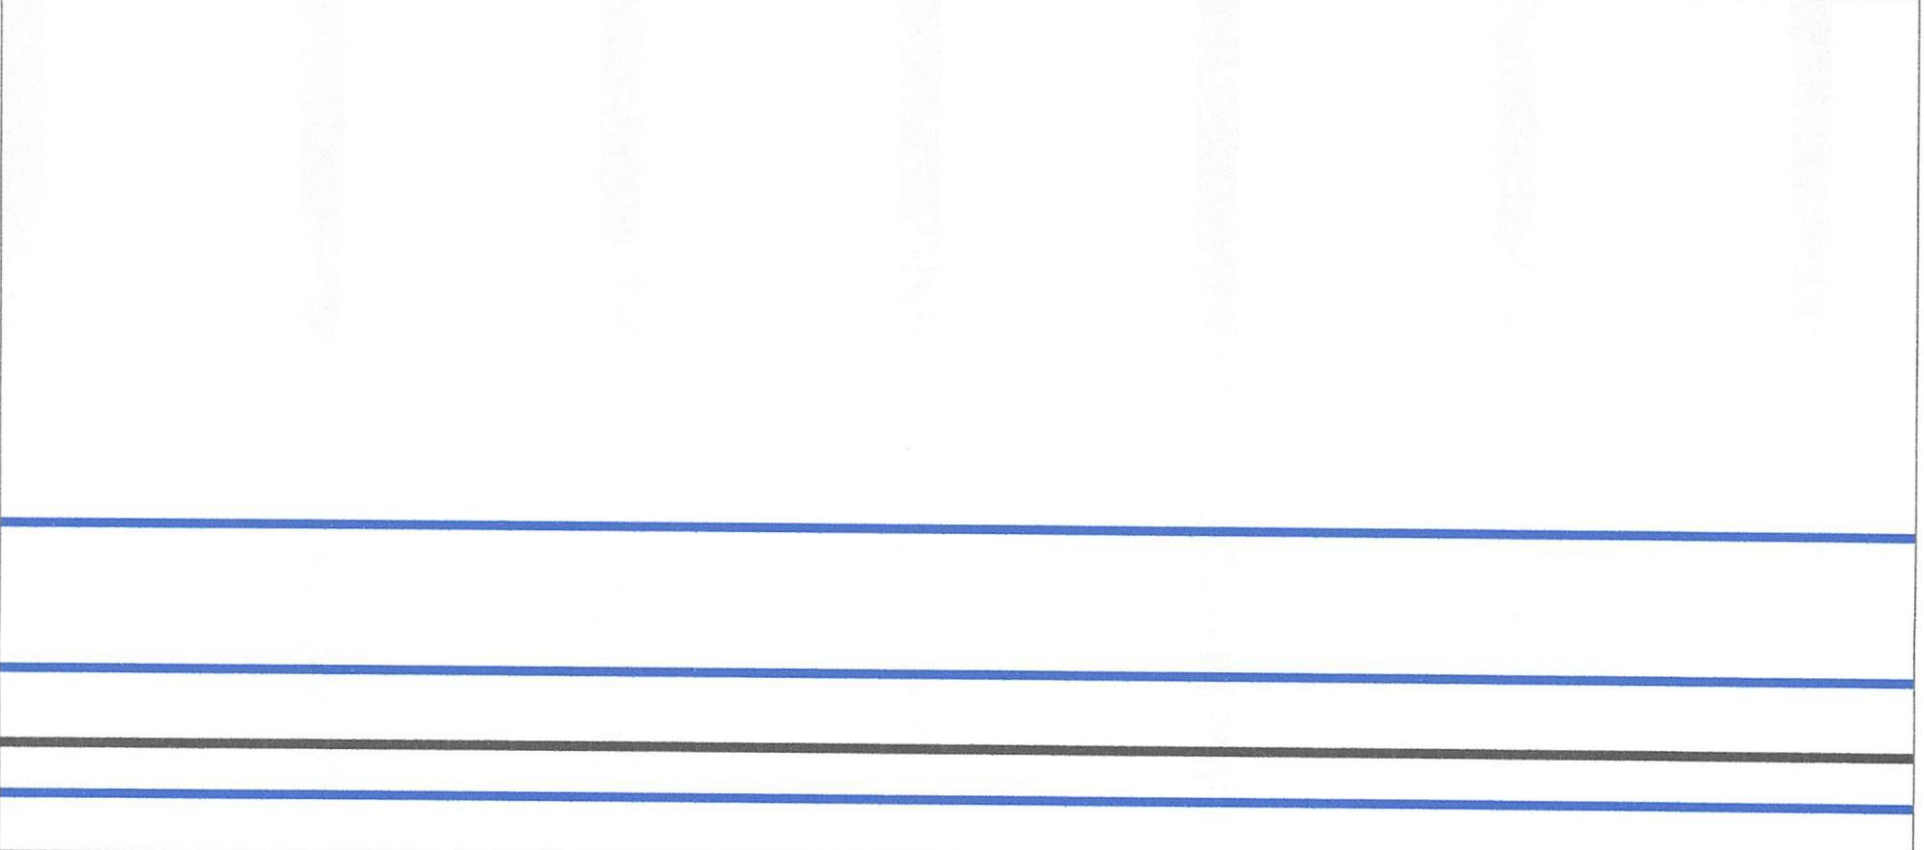


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

14 Mar '21 | 21 Mar '21 | 28 Mar '21 | 4 Apr '21 | 11 Apr '21 | 18 Apr '21 | 25 Apr '21
 S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T W T F S | S M T




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			


W T F S | 2 May '21 | S M T W T F S | 9 May '21 | S M T W T F S | 16 May '21 | S M T W T F S | 23 May '21 | S M T W T F S | 30 May '21 | S M T W T F S | 6 Jun '21 | S M T W T F

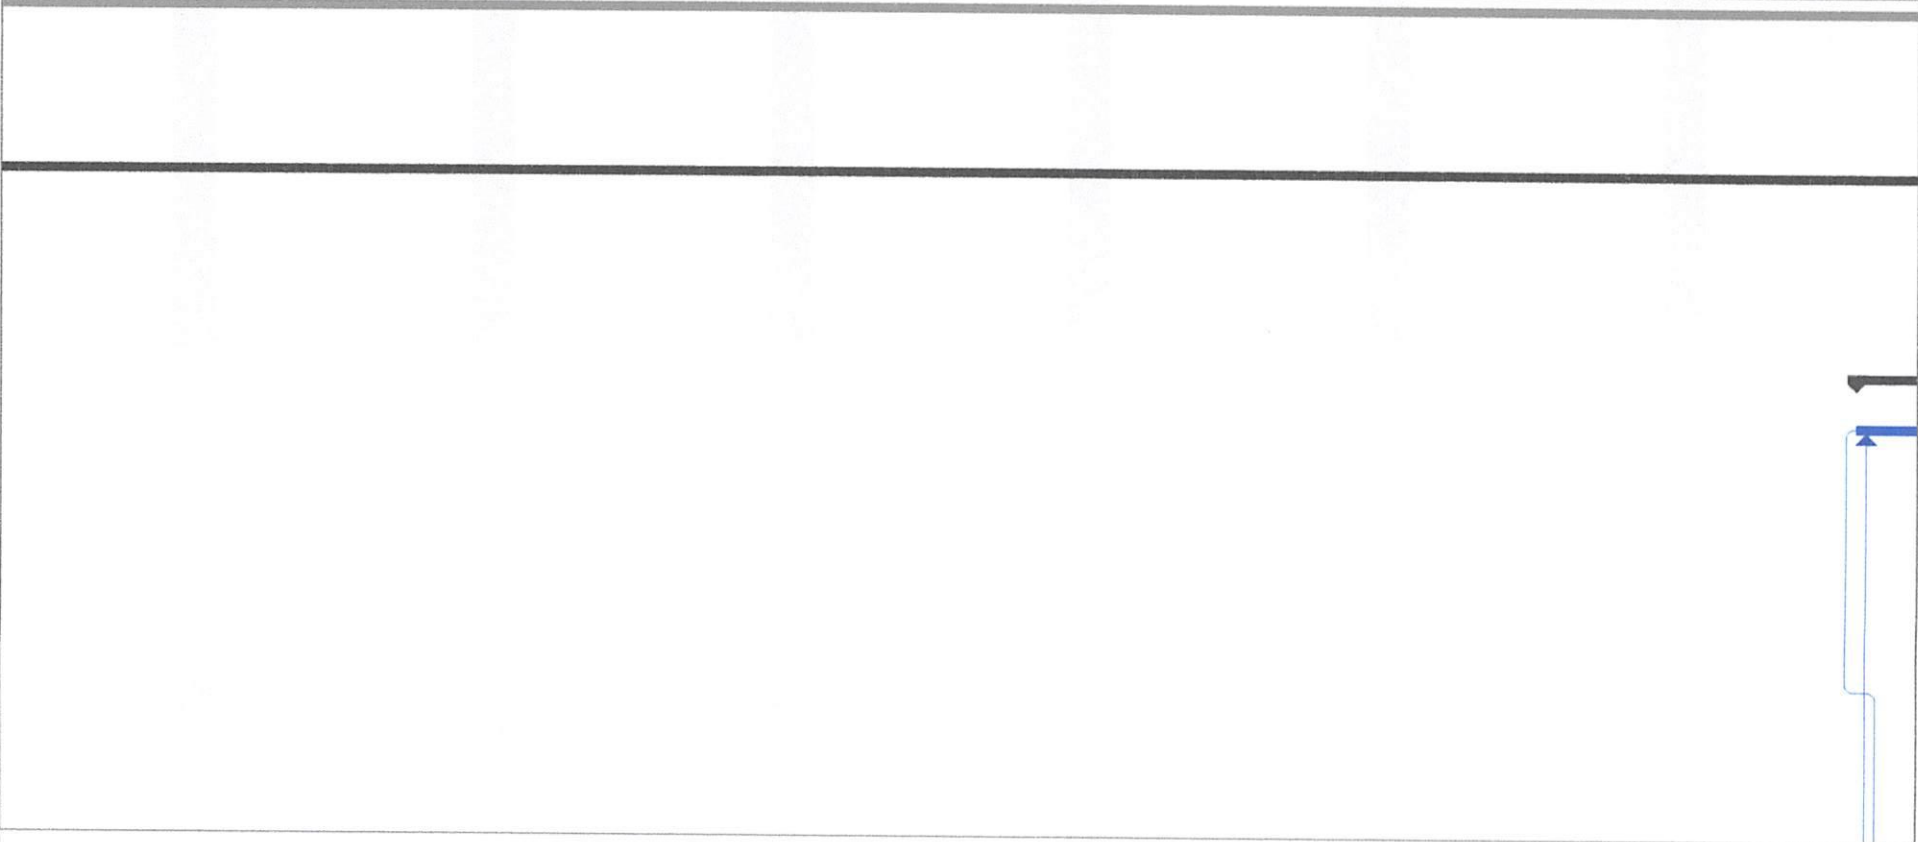


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

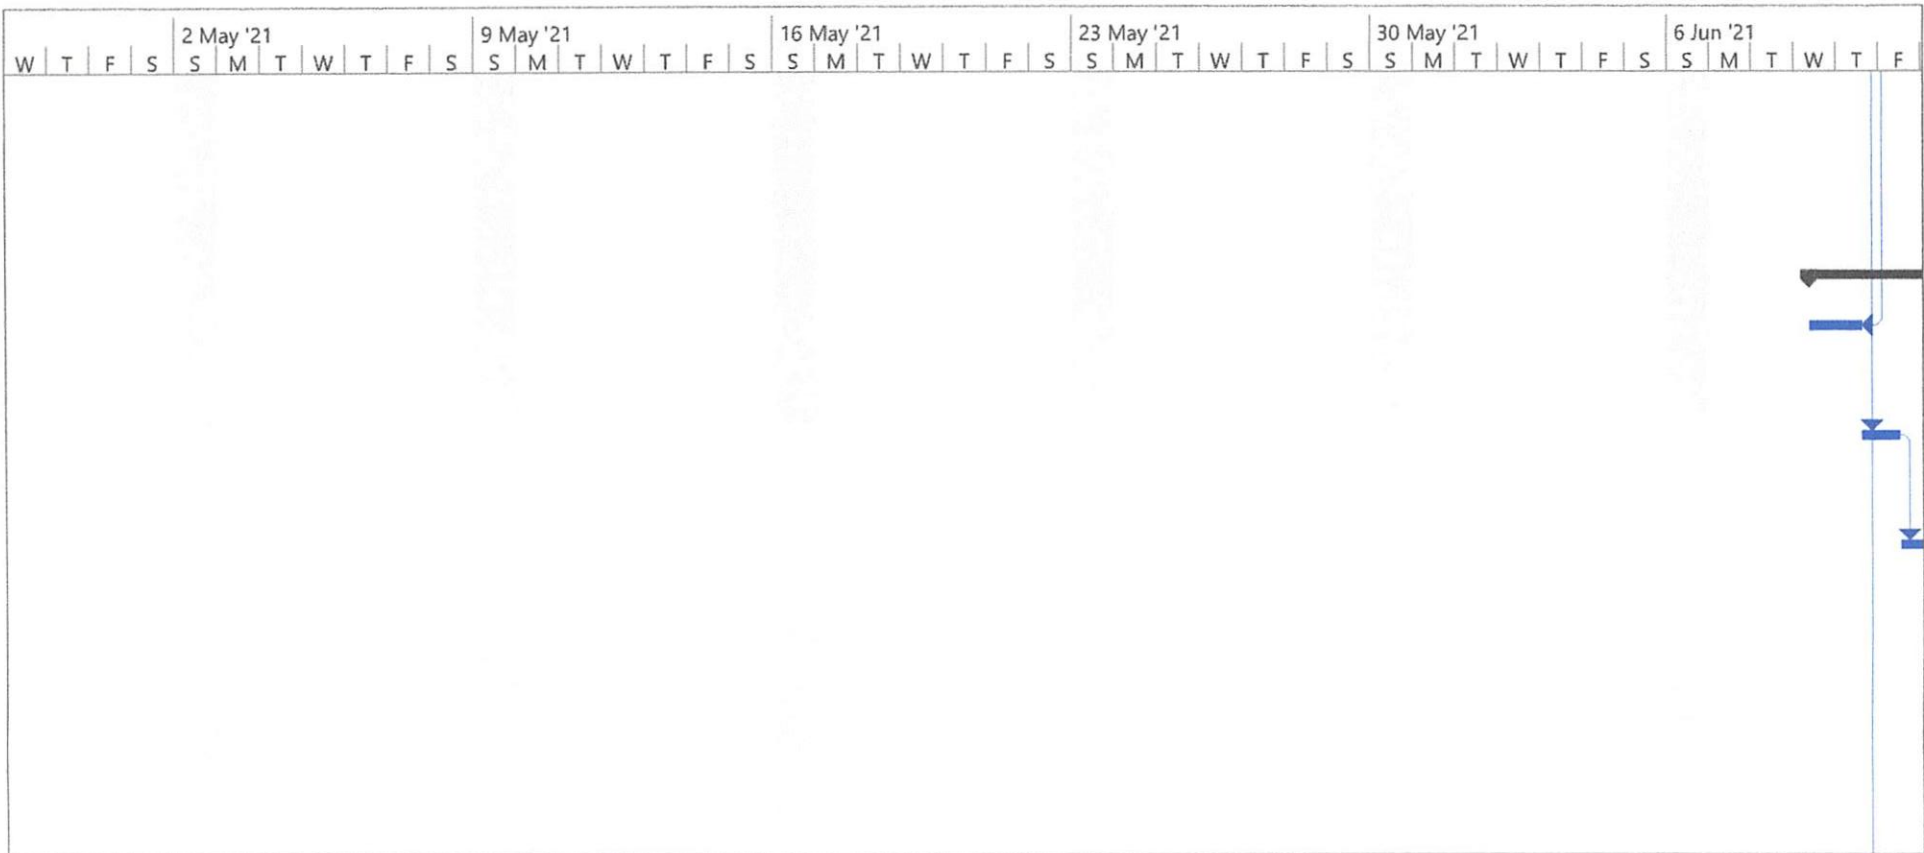

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

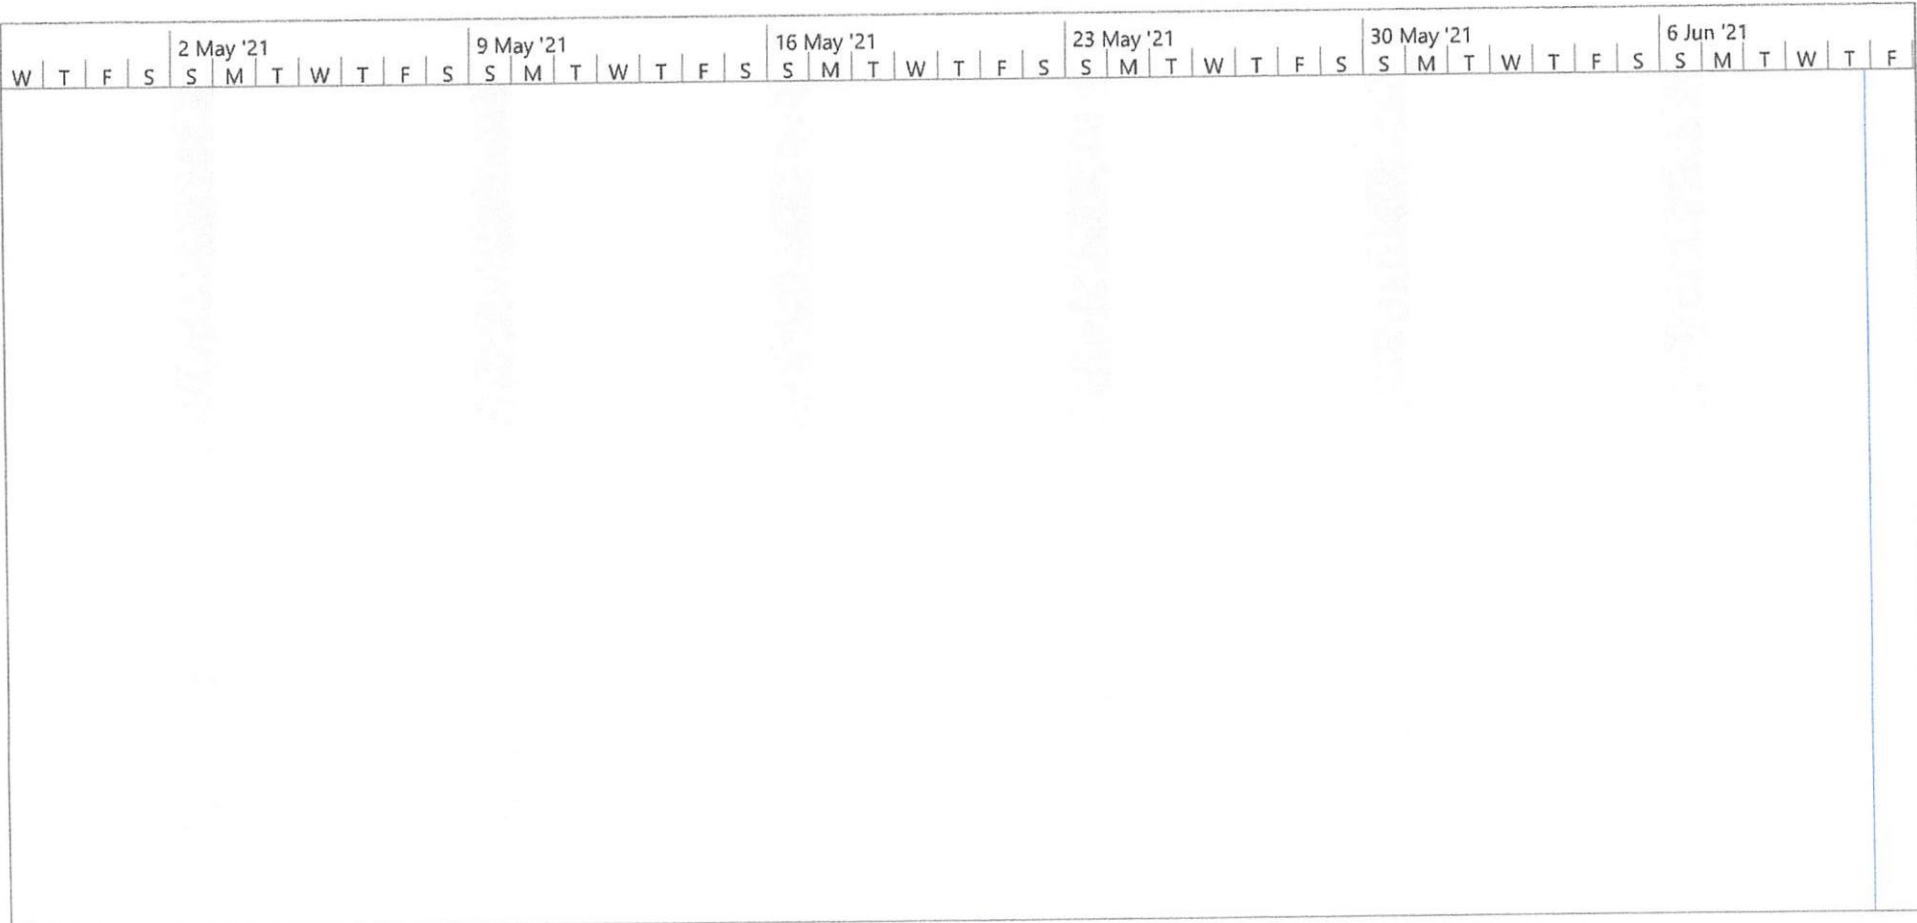

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

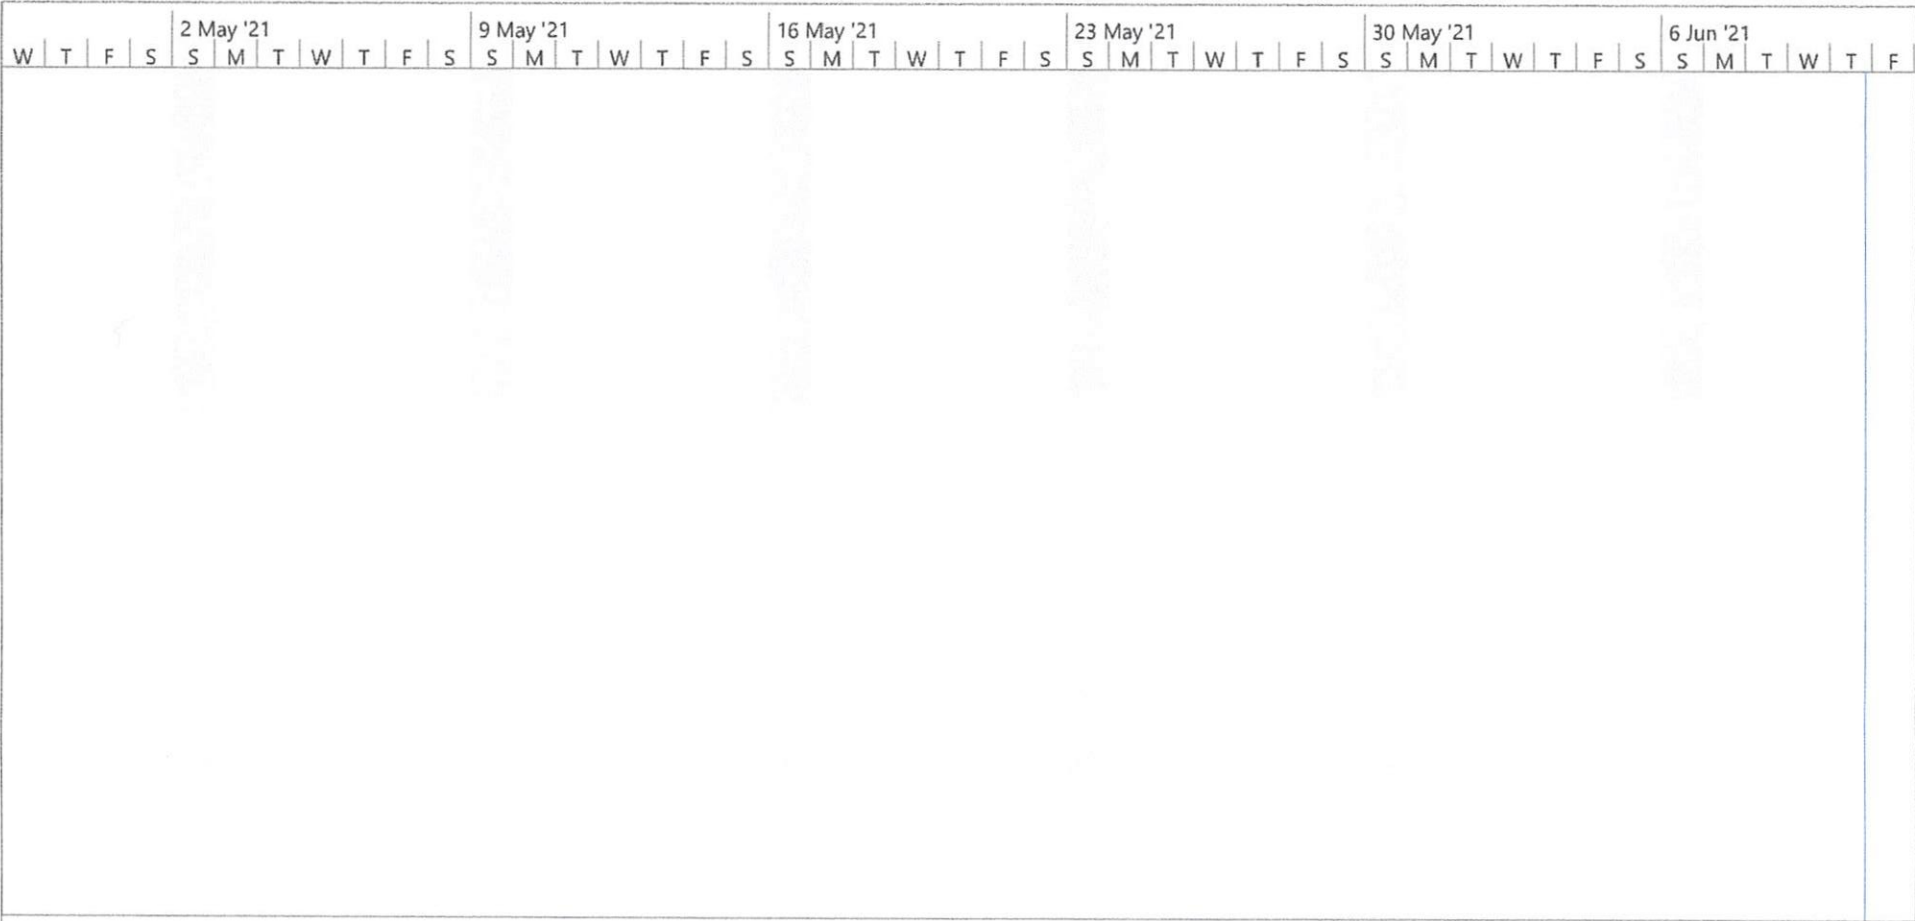


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

W T F S 2 May '21 S M T W T F S 9 May '21 S M T W T F S 16 May '21 S M T W T F S 23 May '21 S M T W T F S 30 May '21 S M T W T F S 6 Jun '21 S M T W T F




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

W T F S 2 May '21 S M T W T F S 9 May '21 S M T W T F S 16 May '21 S M T W T F S 23 May '21 S M T W T F S 30 May '21 S M T W T F S 6 Jun '21 S M T W T F

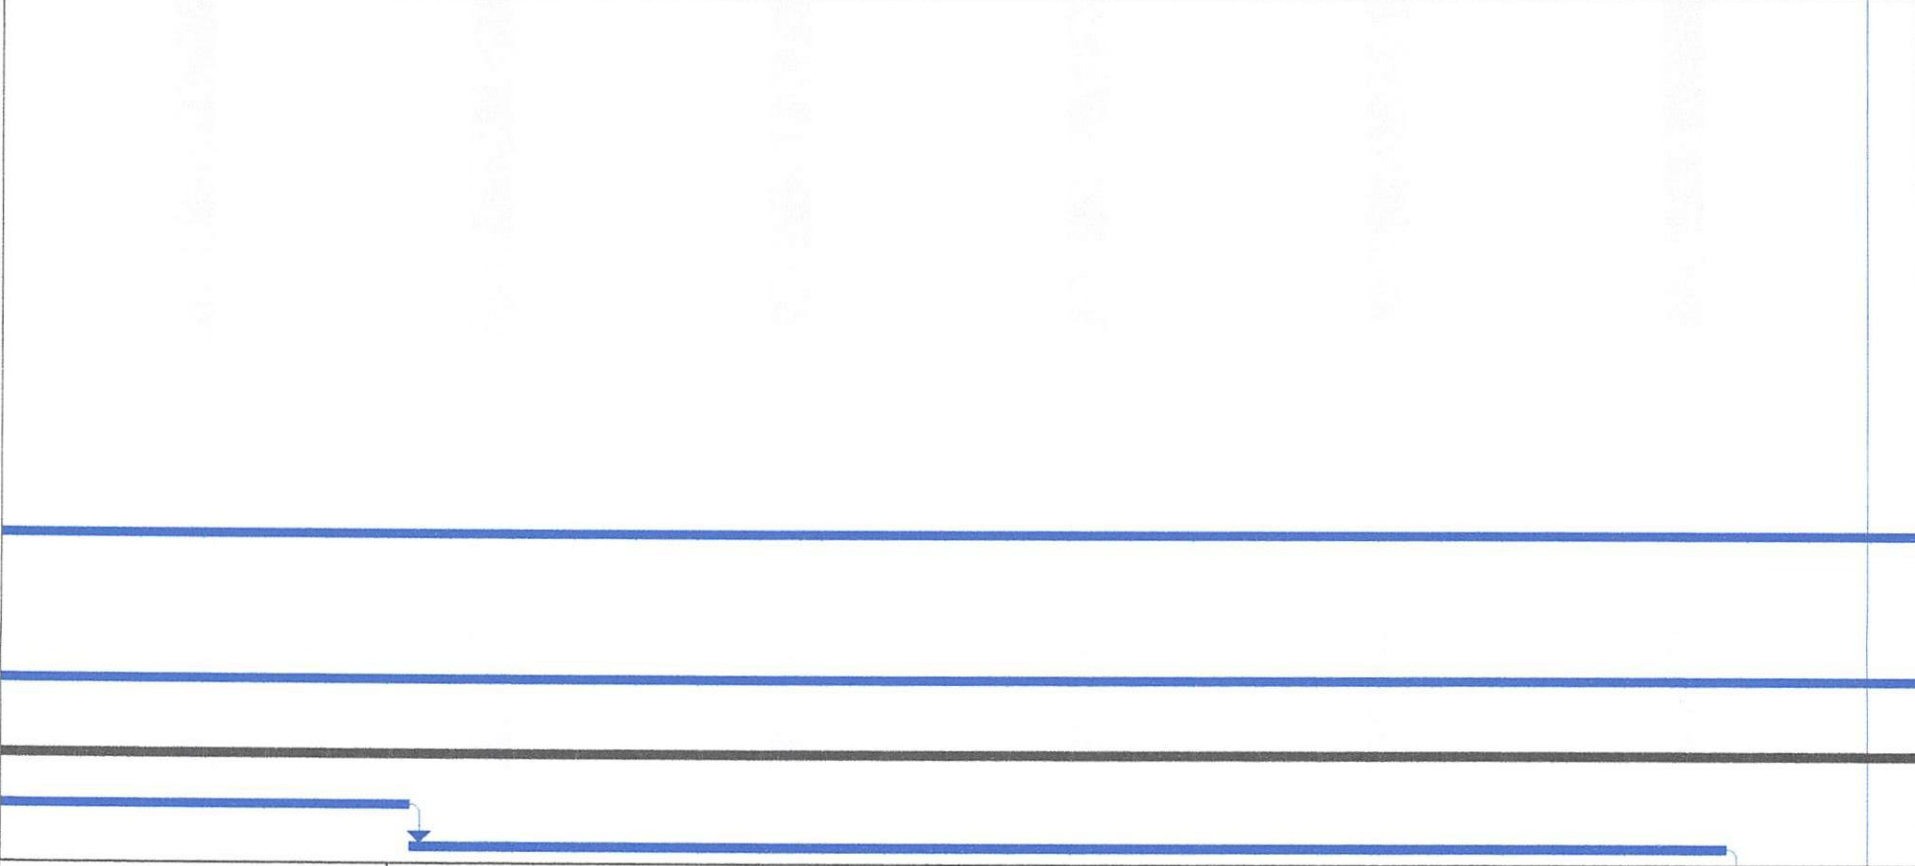


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			


W T F S | 2 May '21 | S M T W T F S | 9 May '21 | S M T W T F S | 16 May '21 | S M T W T F S | 23 May '21 | S M T W T F S | 30 May '21 | S M T W T F S | 6 Jun '21




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

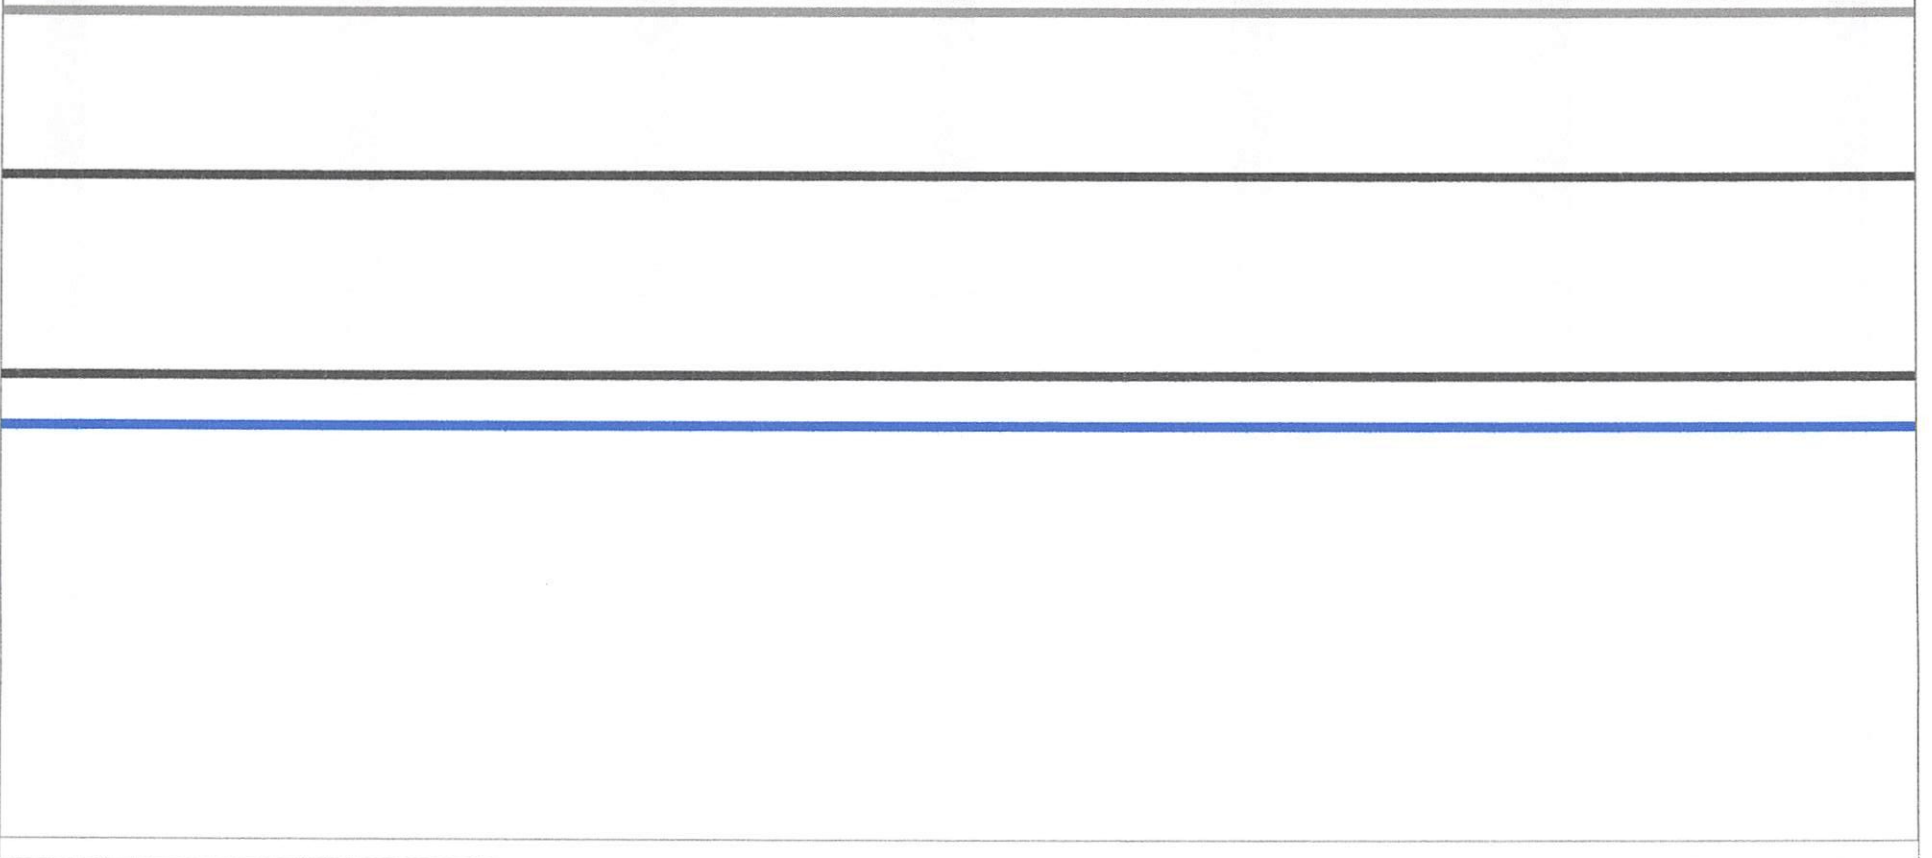


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

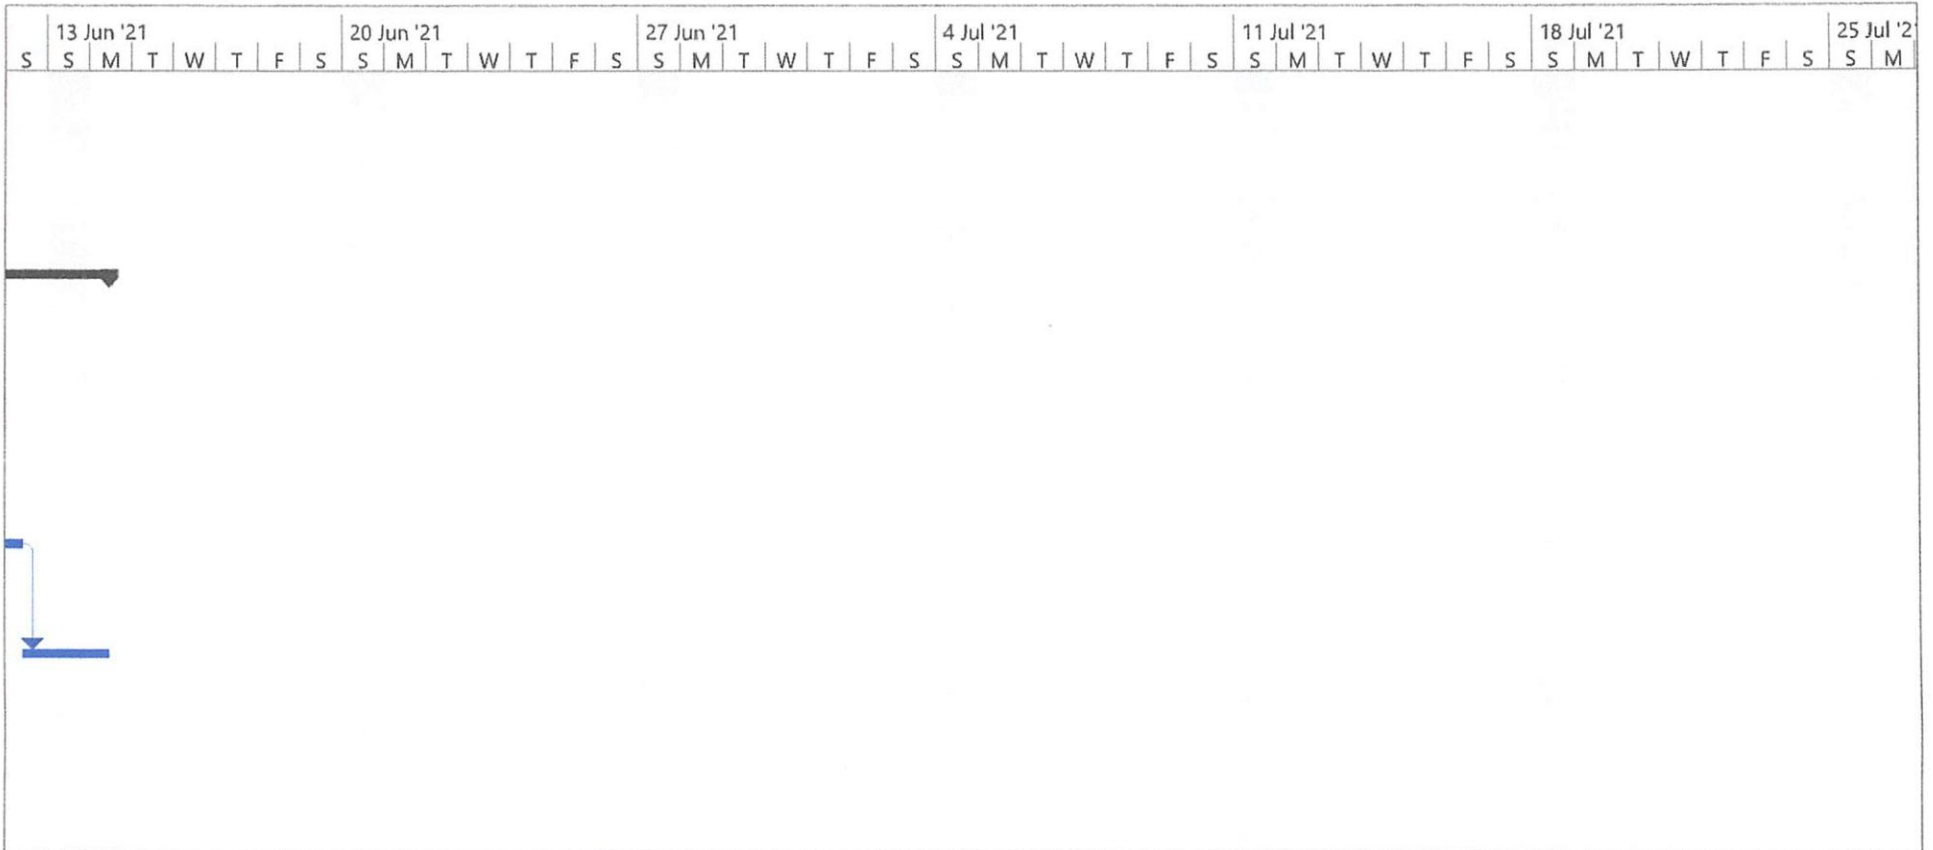


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

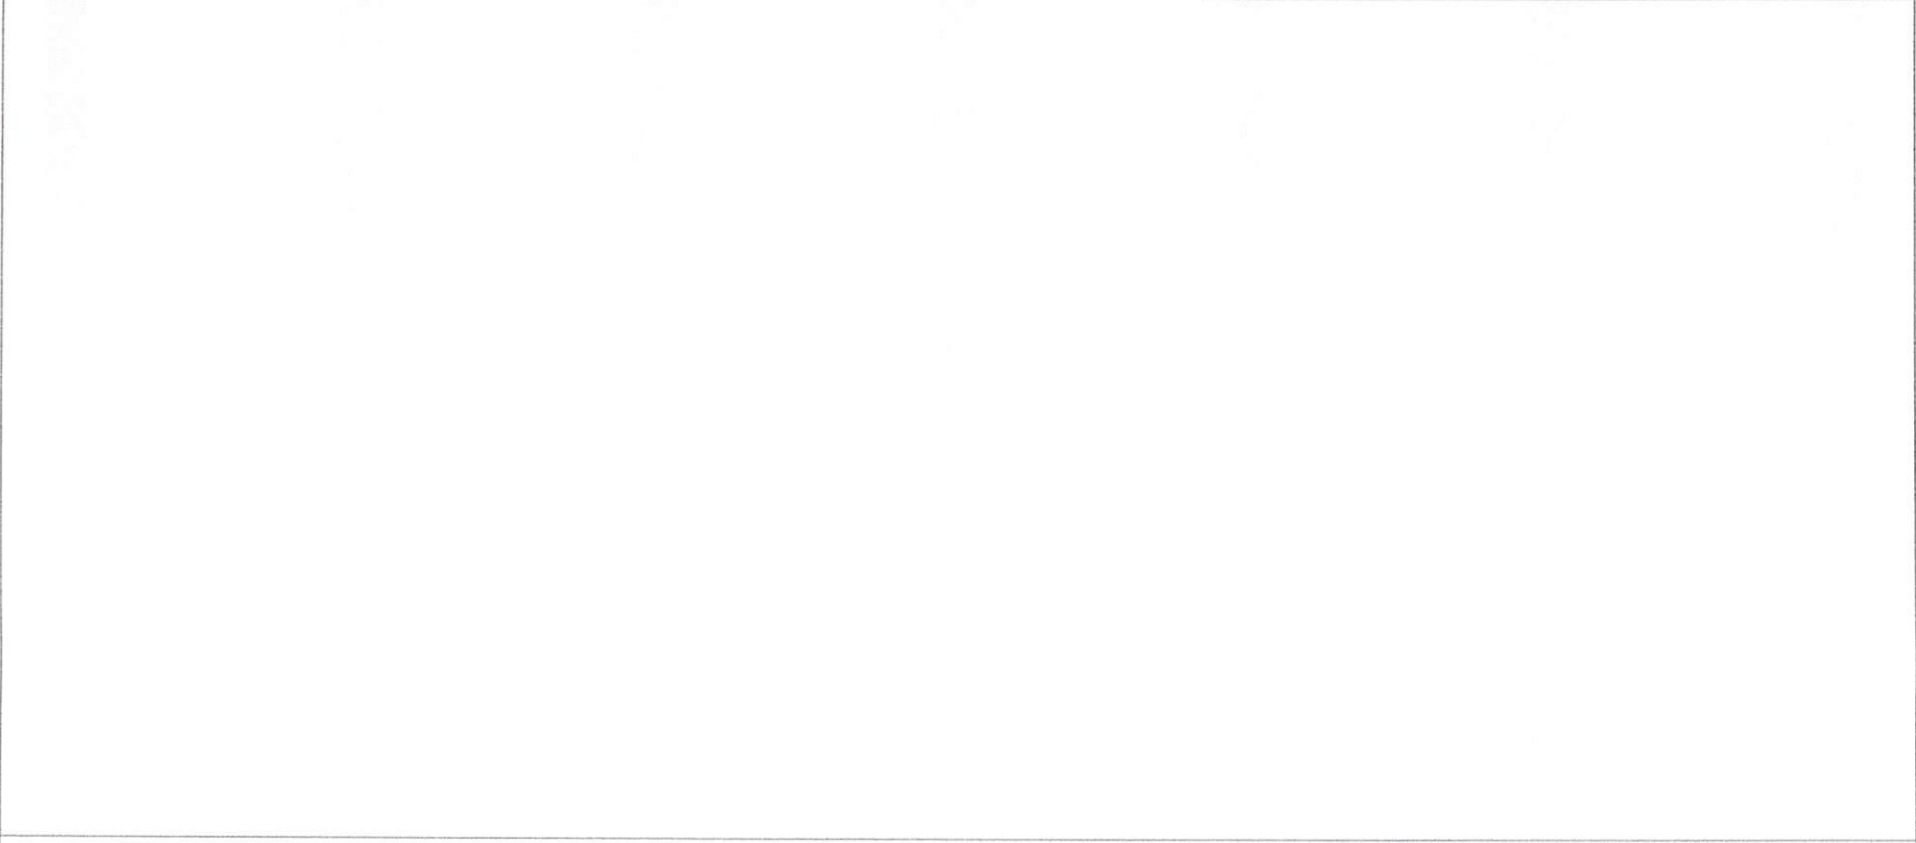

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

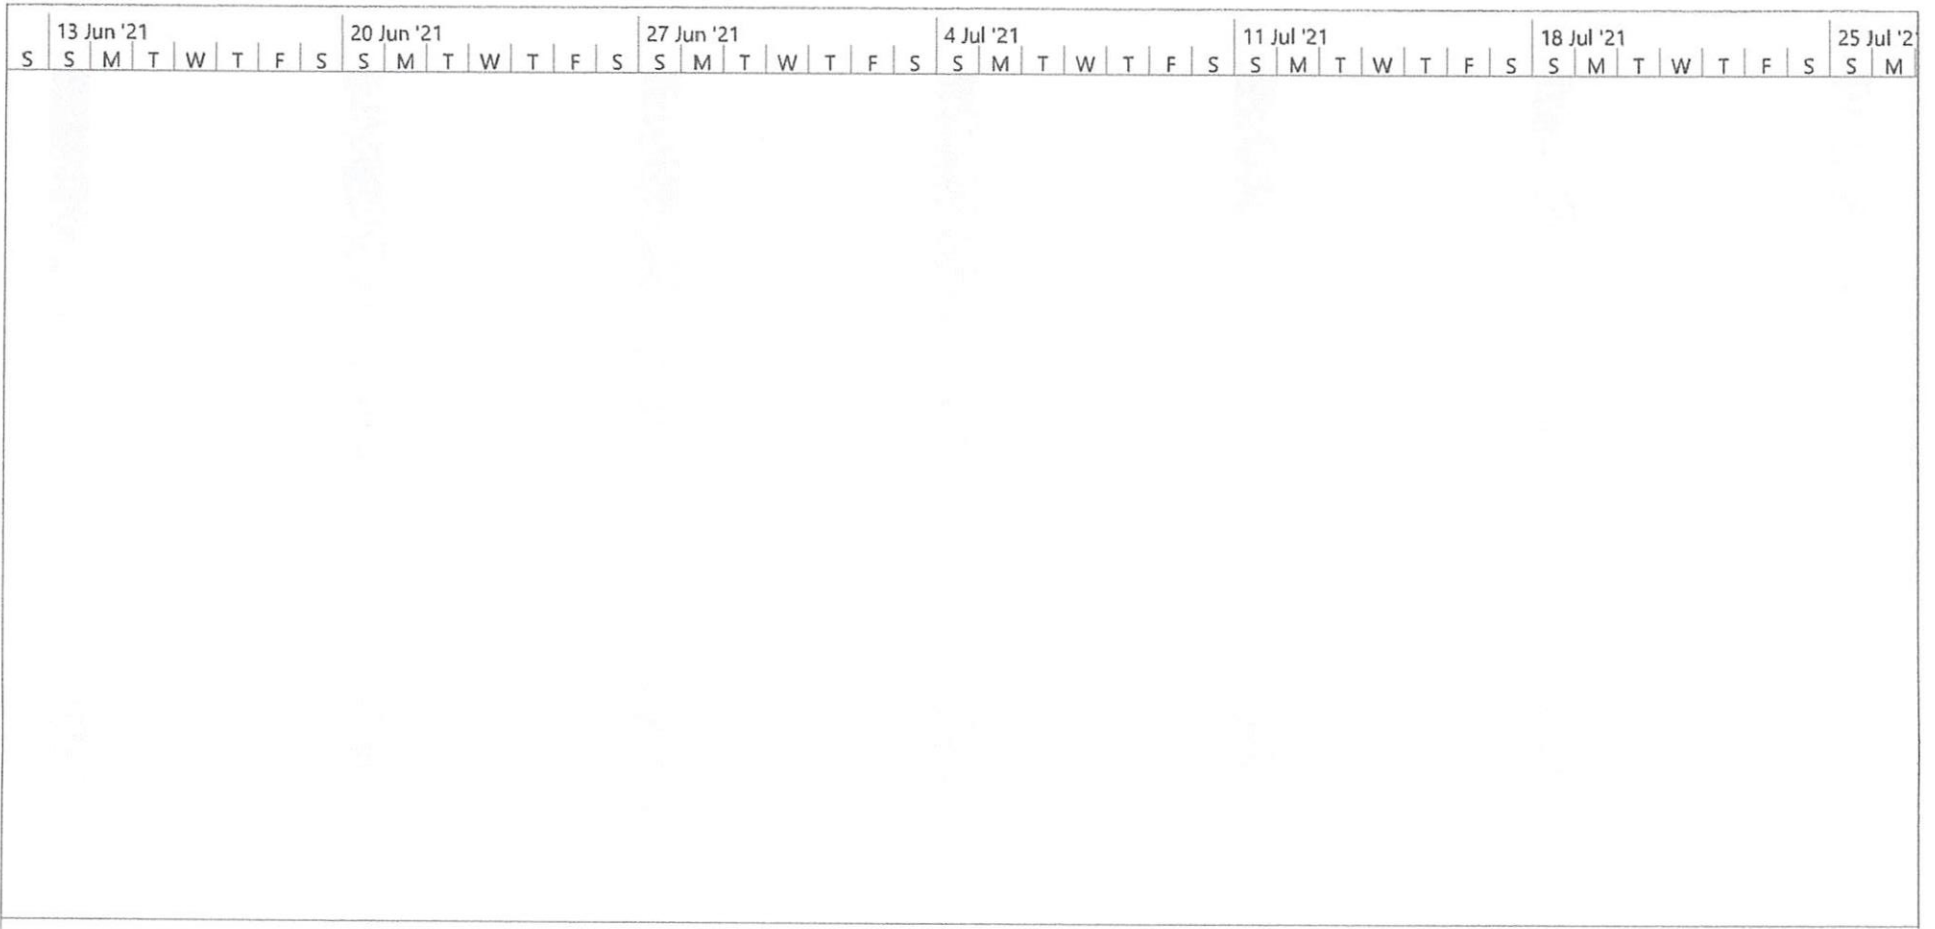


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

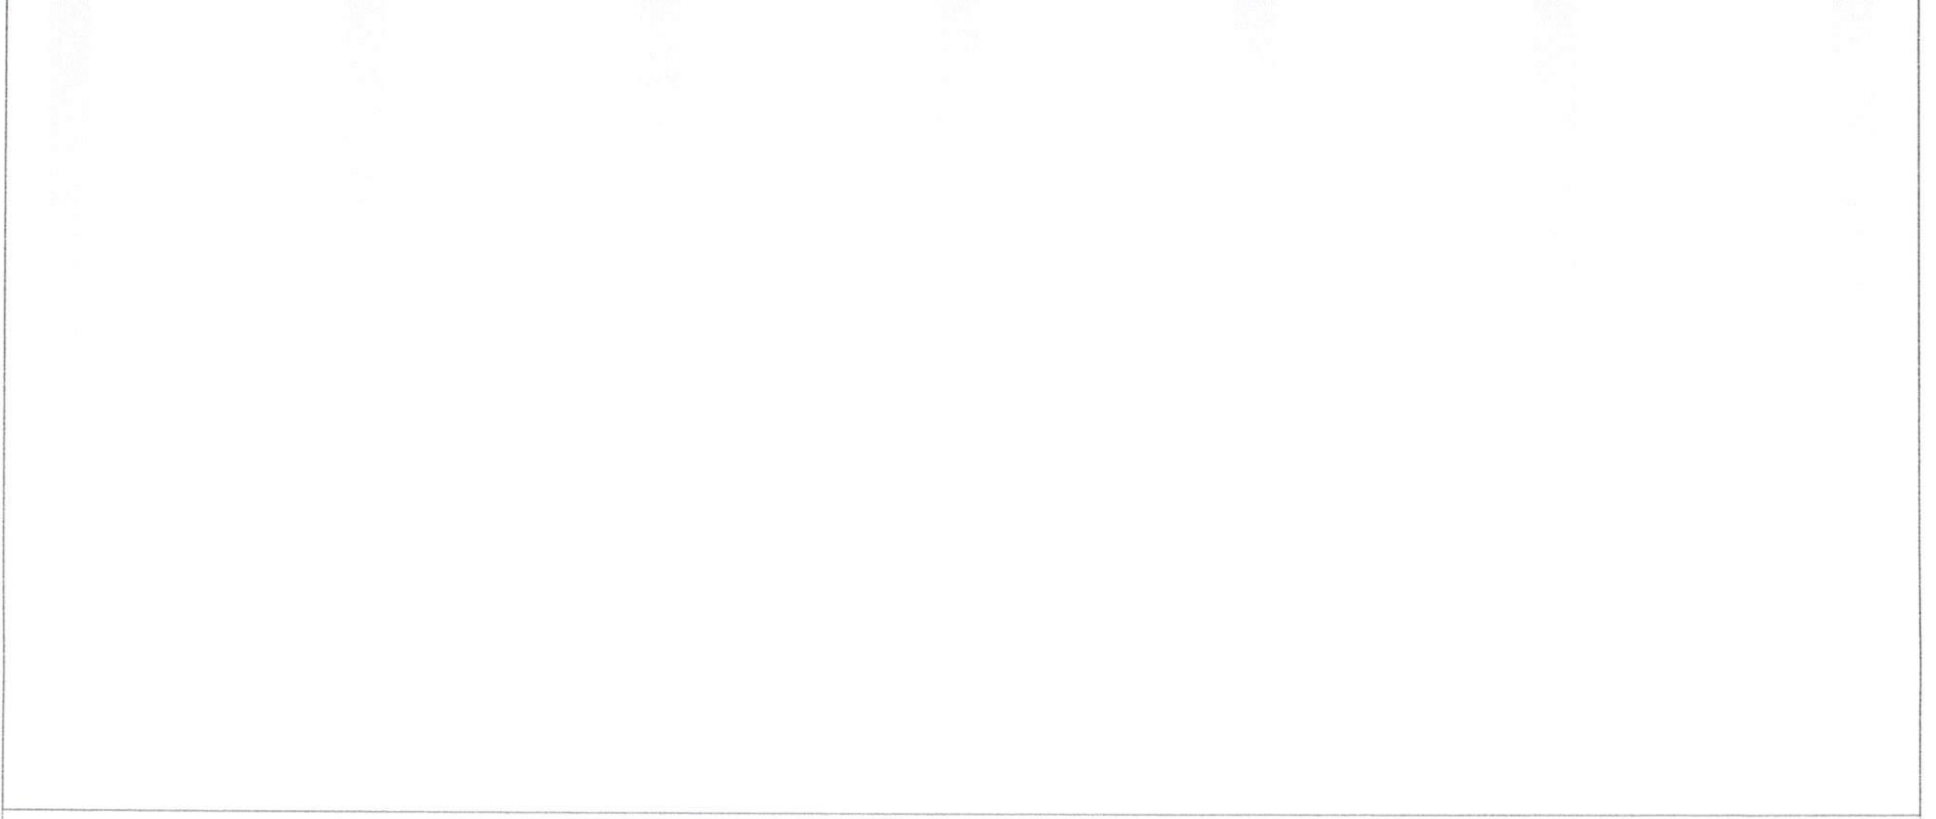


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			


13 Jun '21 20 Jun '21 27 Jun '21 4 Jul '21 11 Jul '21 18 Jul '21 25 Jul '21

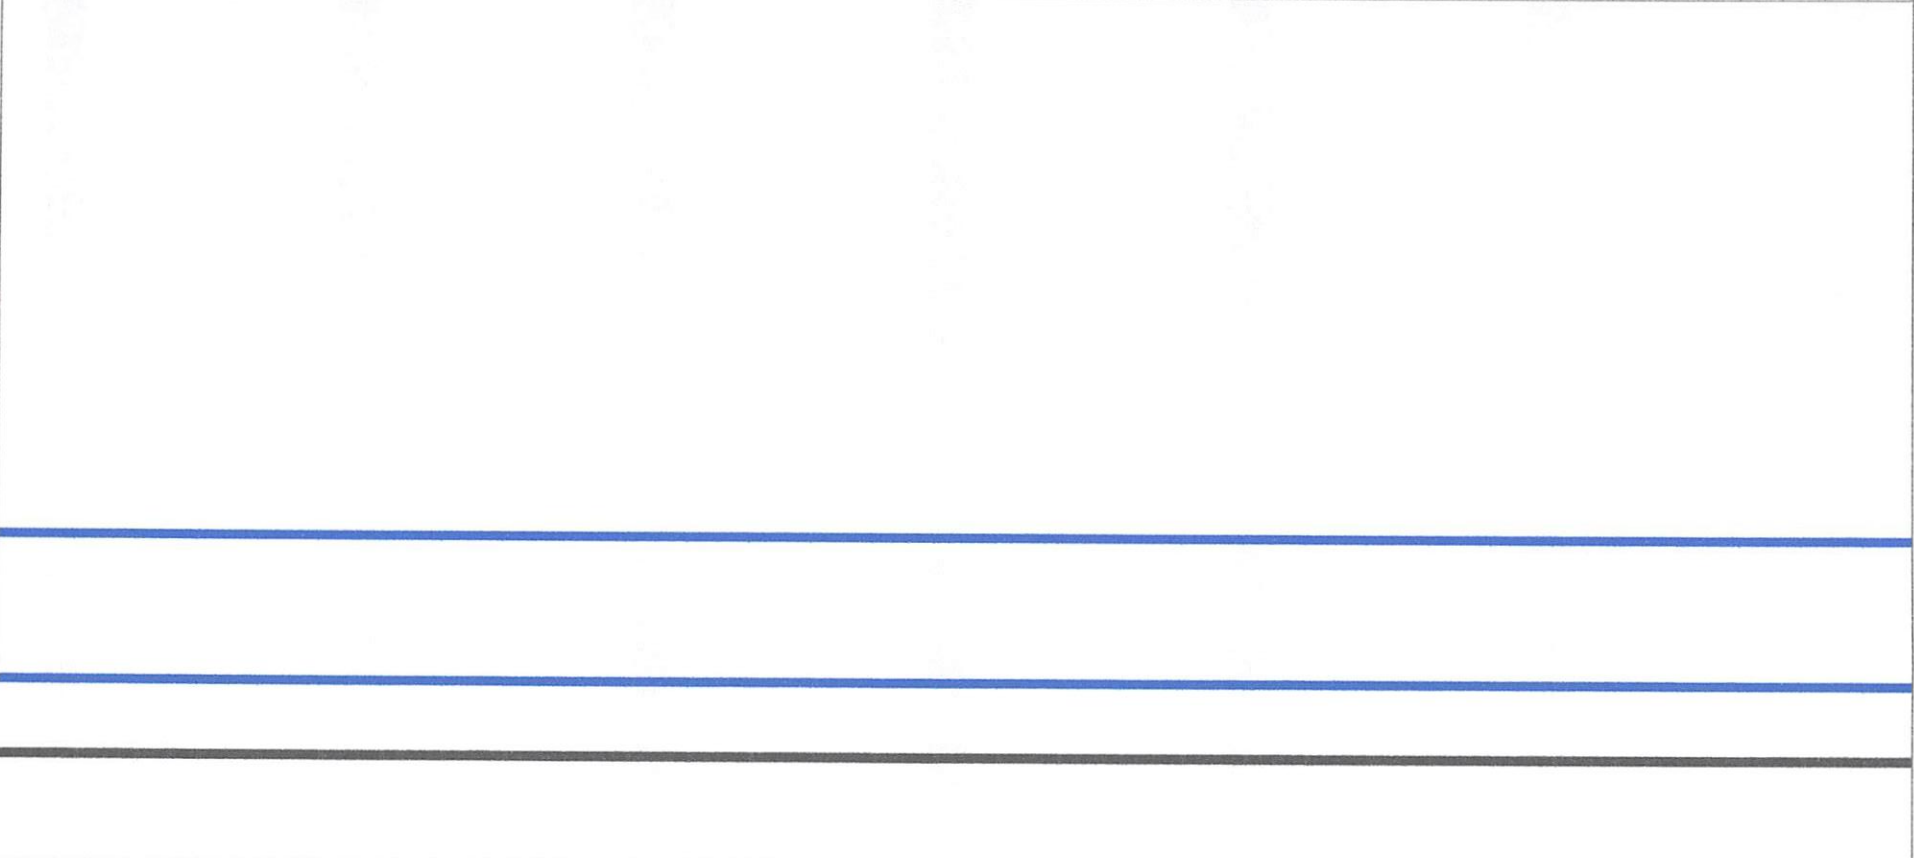


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone	Manual Summary Rollup		
Milestone		Rolled Up Progress	Manual Summary		
Baseline Milestone		Baseline Split	Start-only		
Summary		External Tasks	Finish-only		
Project Summary		External Milestone	Deadline		
Group By Summary		Inactive Task	Baseline		
Rolled Up Task		Inactive Milestone	Progress		
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

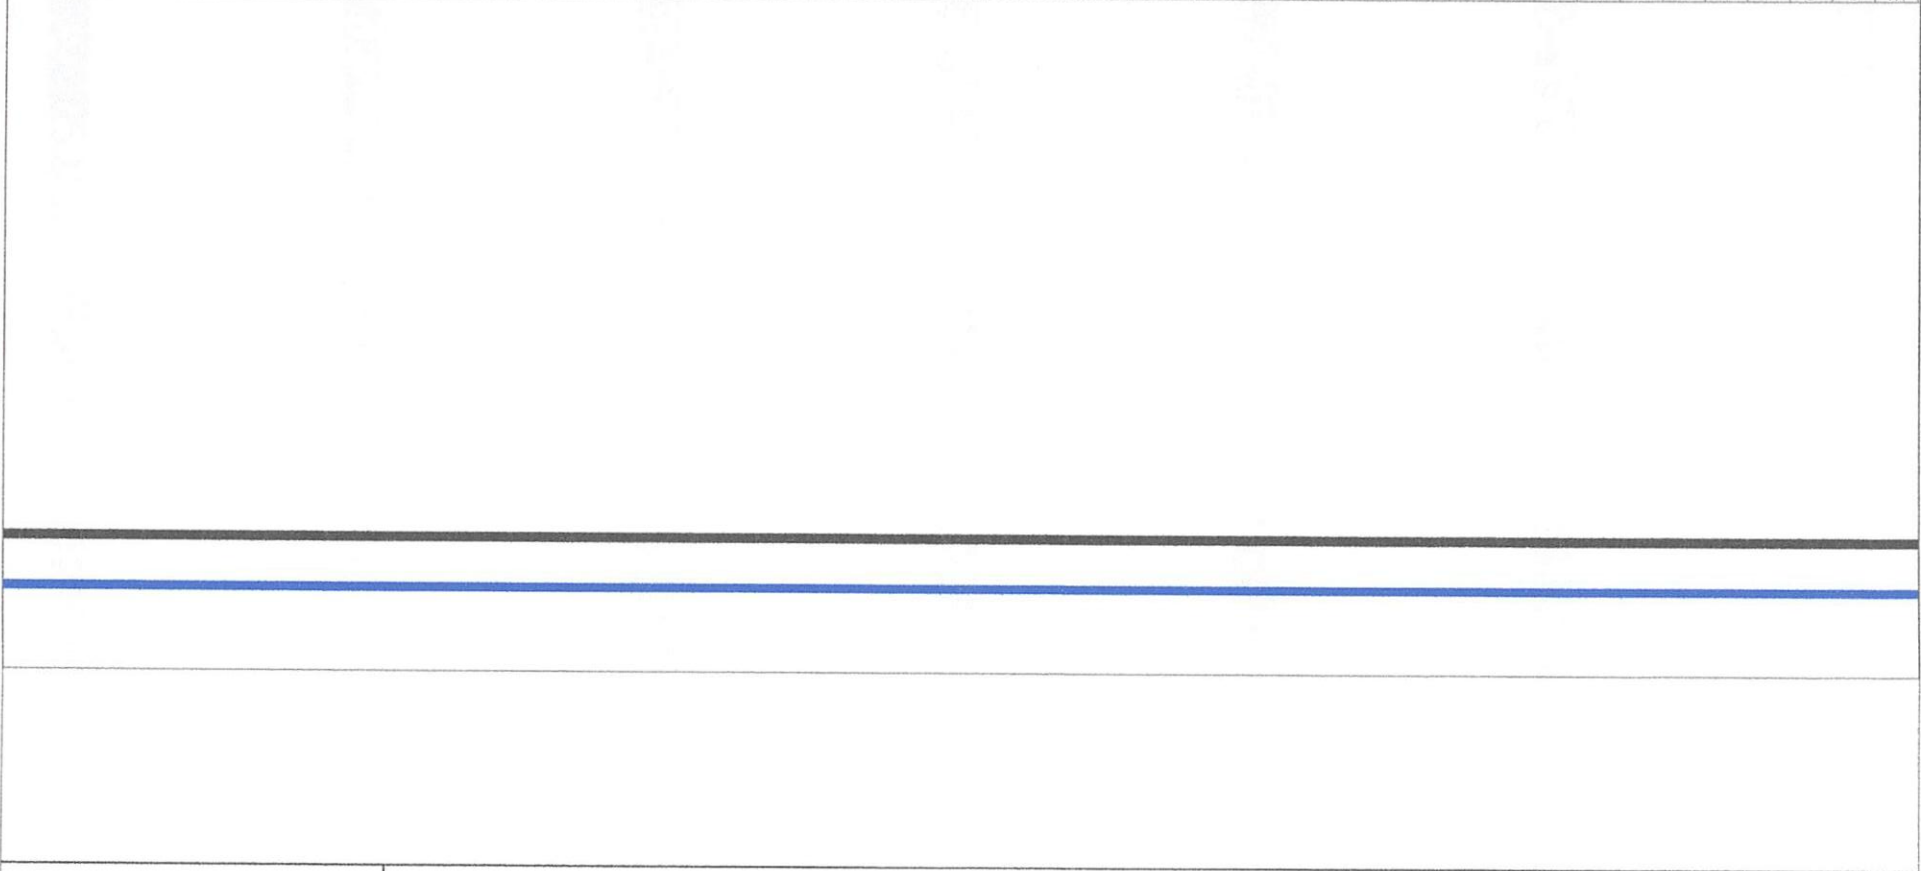


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

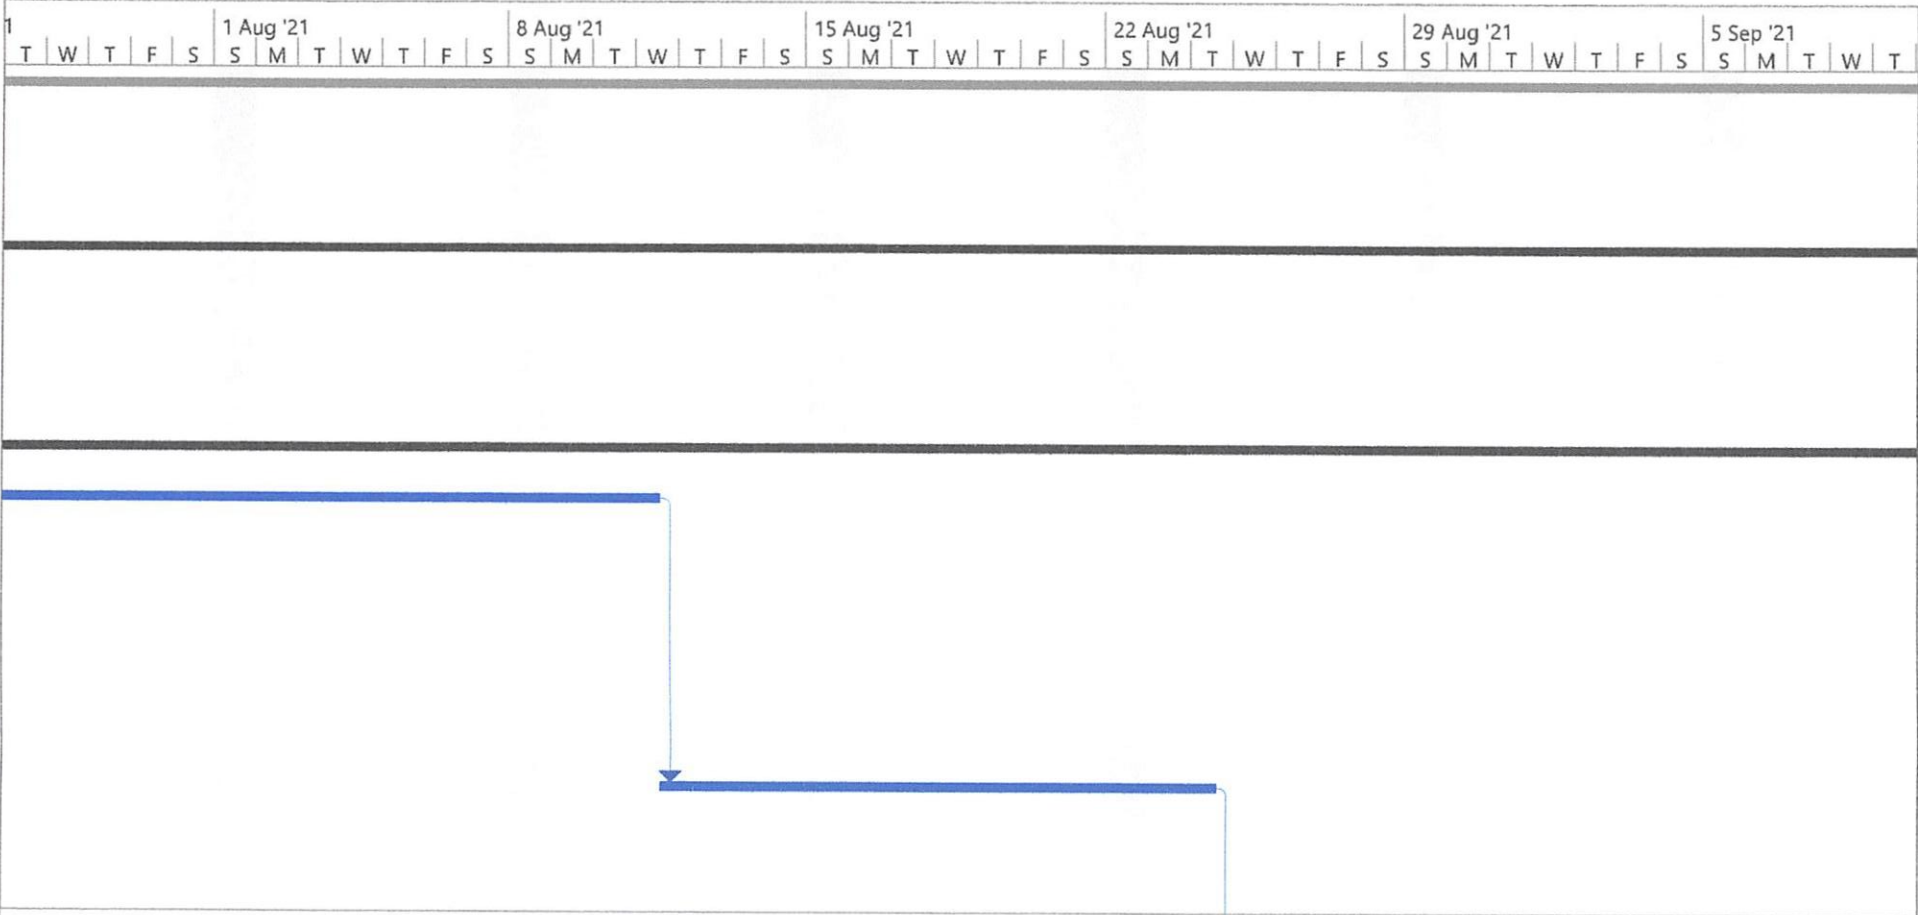


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

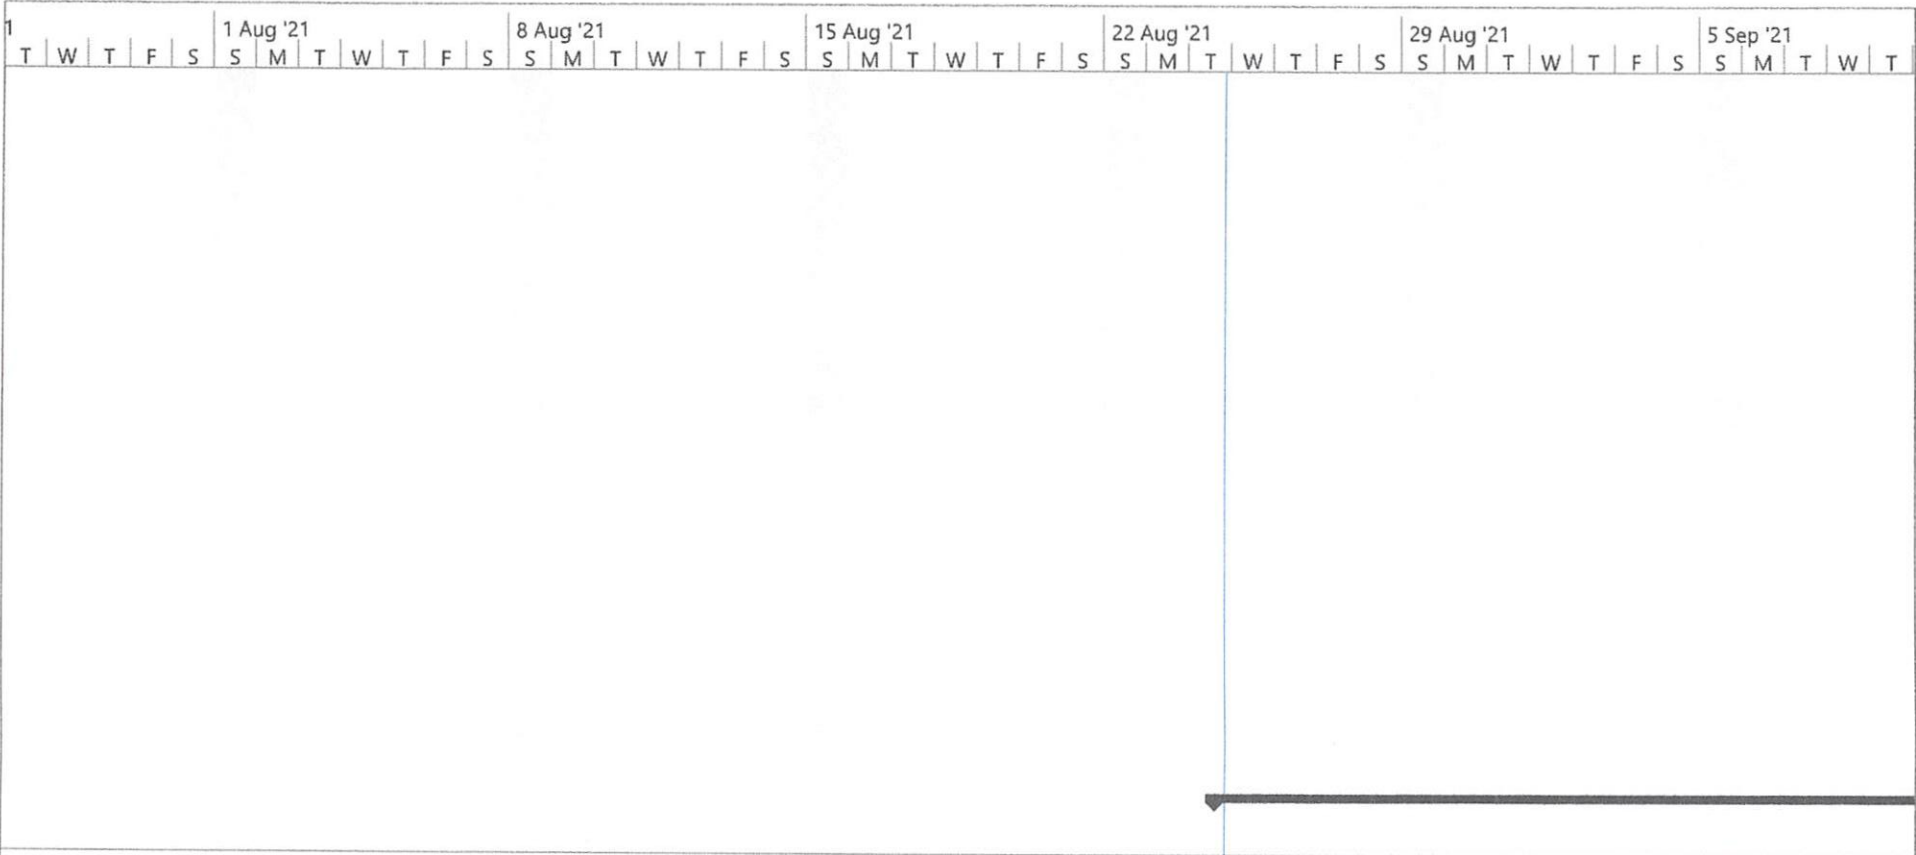

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

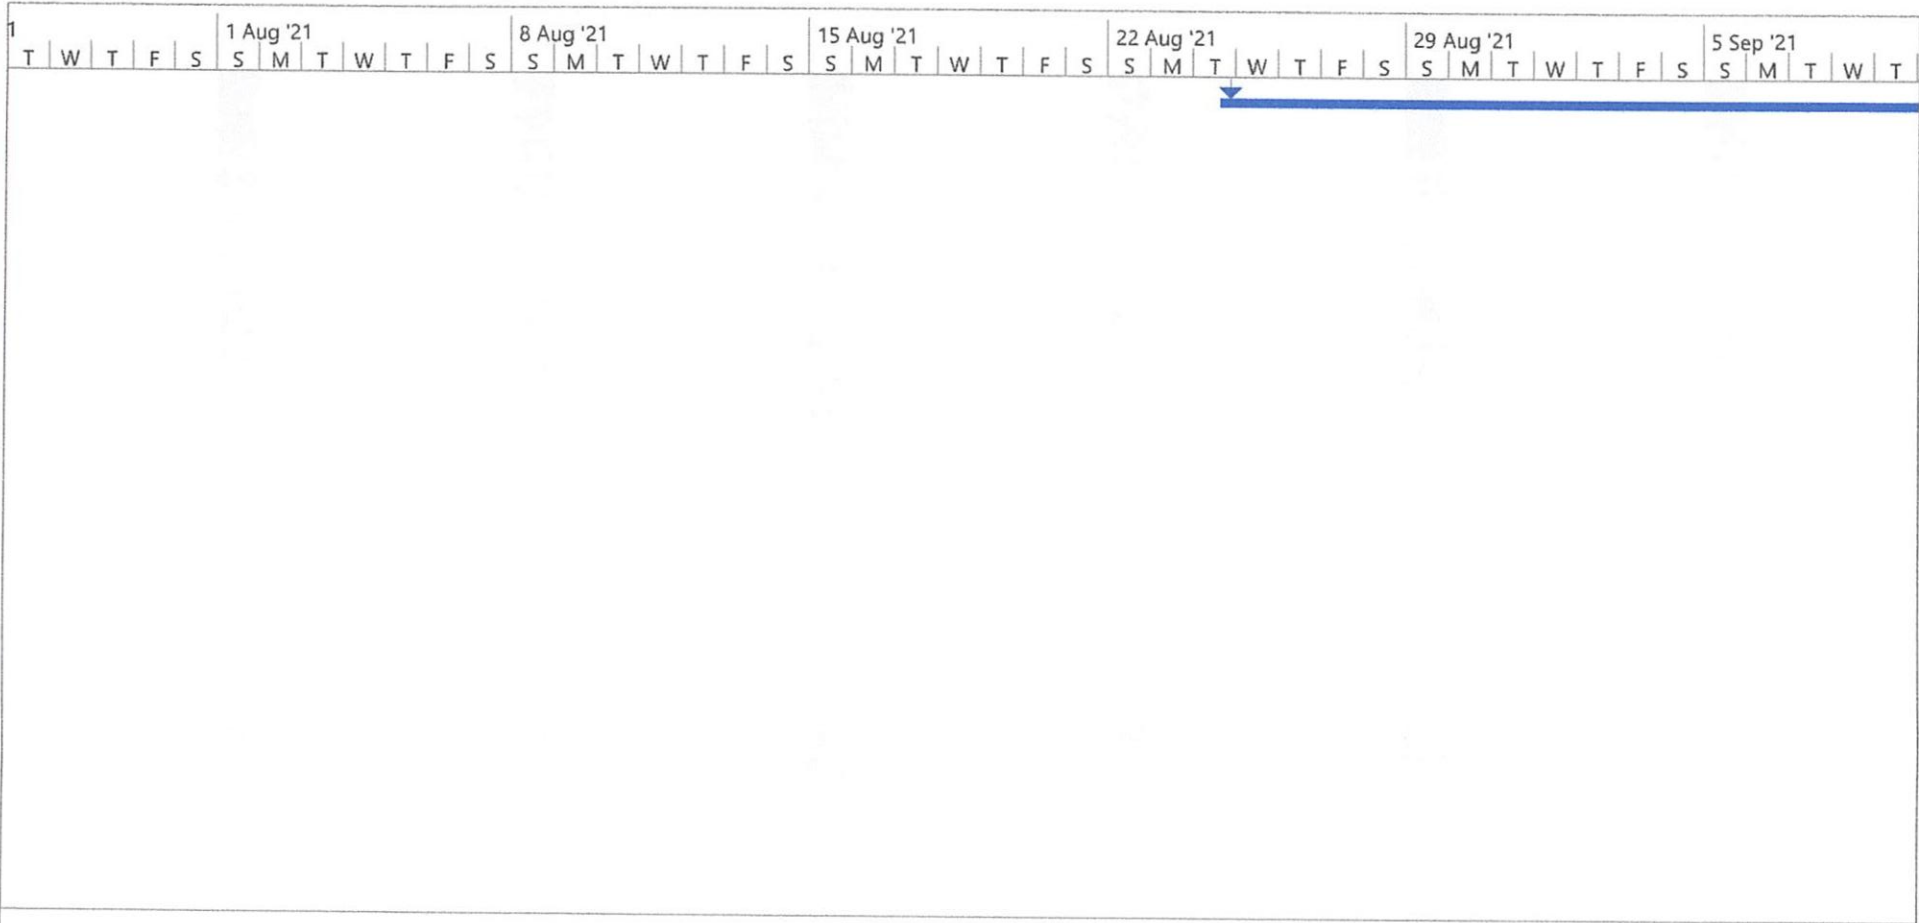

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

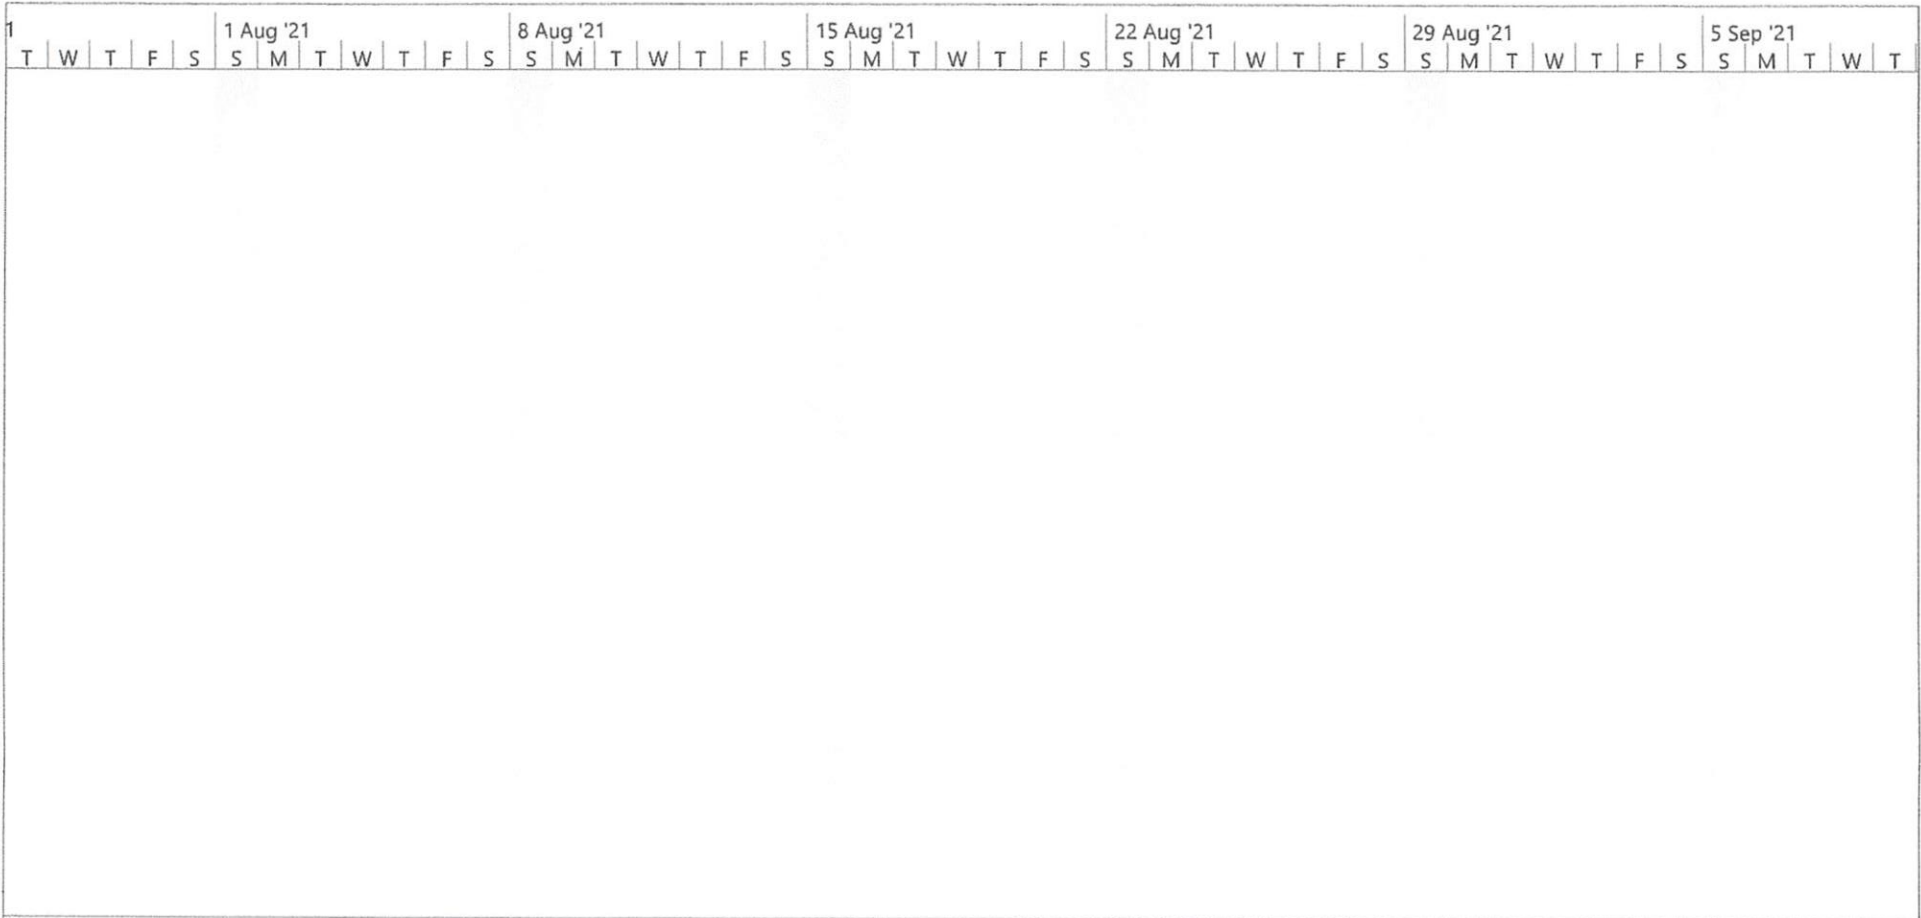


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			


1 T W T F S 1 Aug '21 S M T W T F S 8 Aug '21 S M T W T F S 15 Aug '21 S M T W T F S 22 Aug '21 S M T W T F S 29 Aug '21 S M T W T F S 5 Sep '21 S M T W T

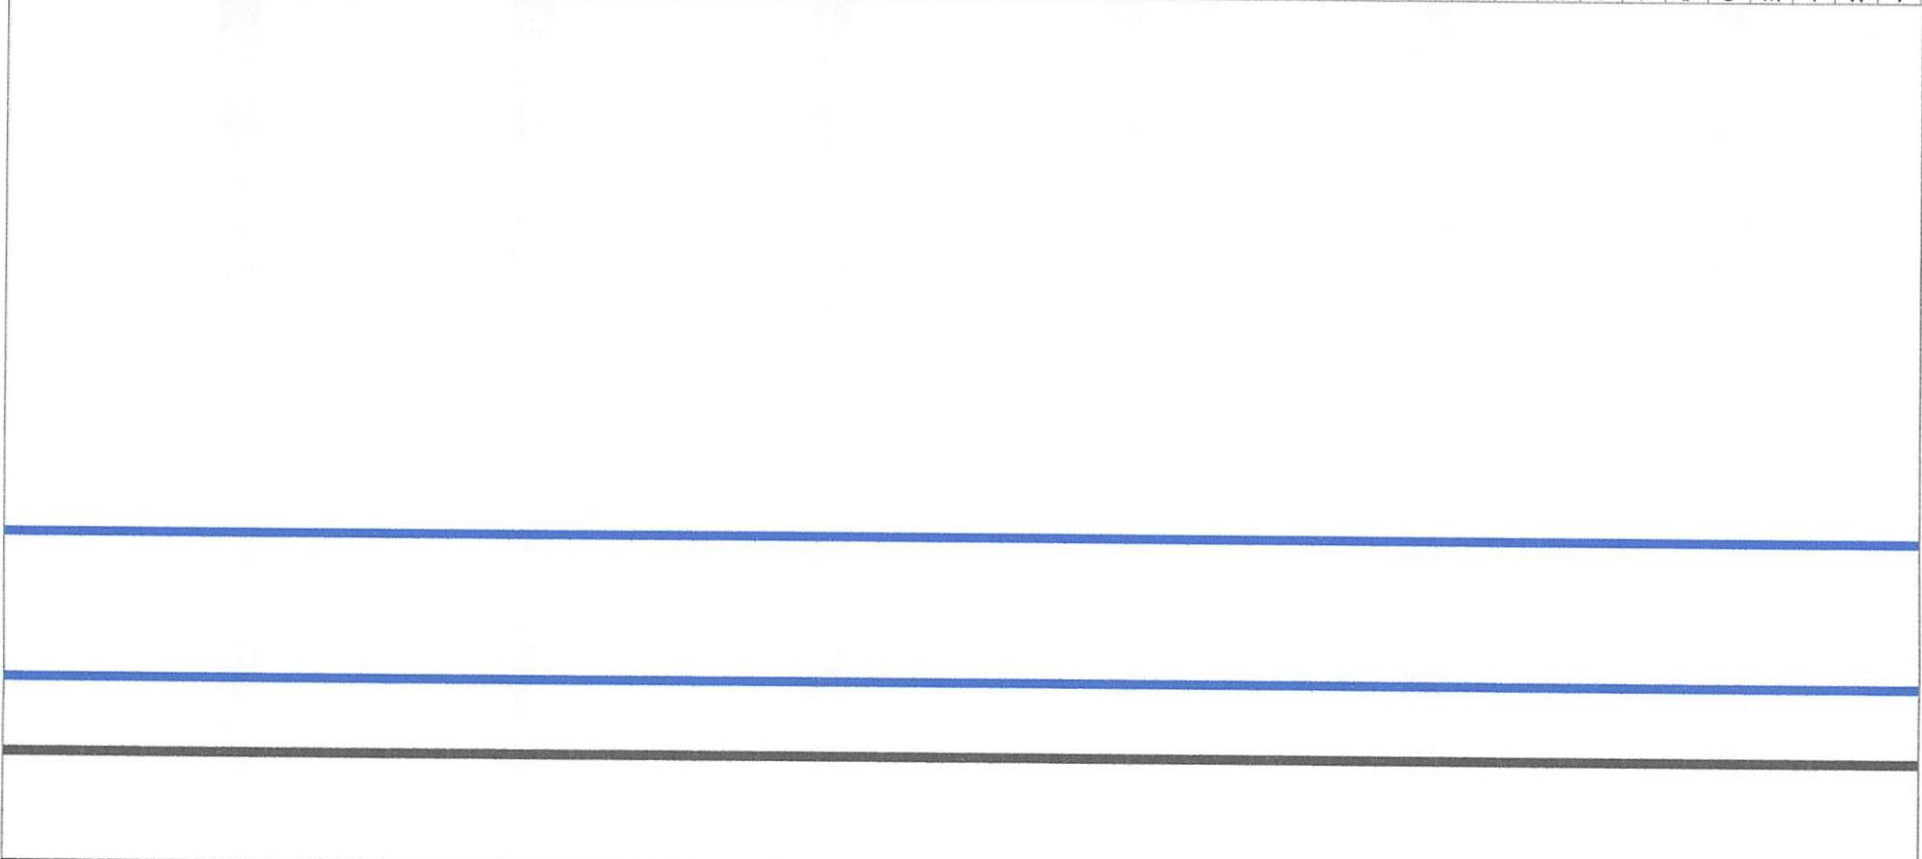



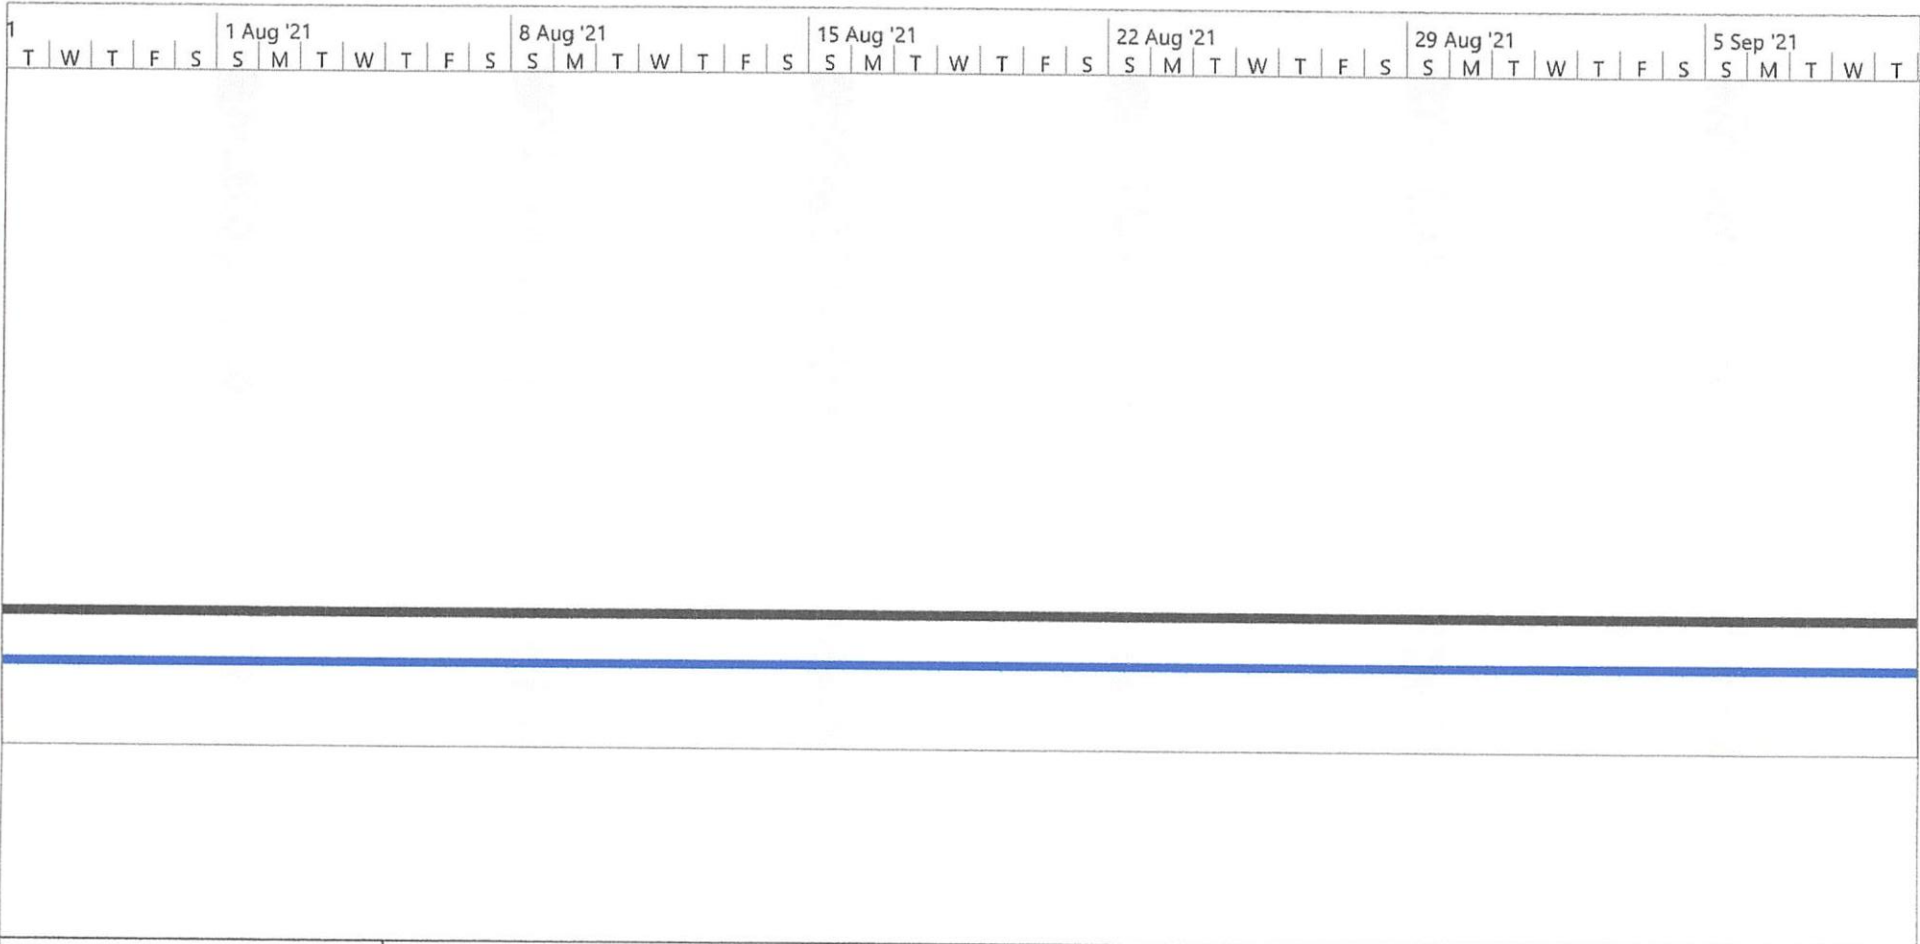



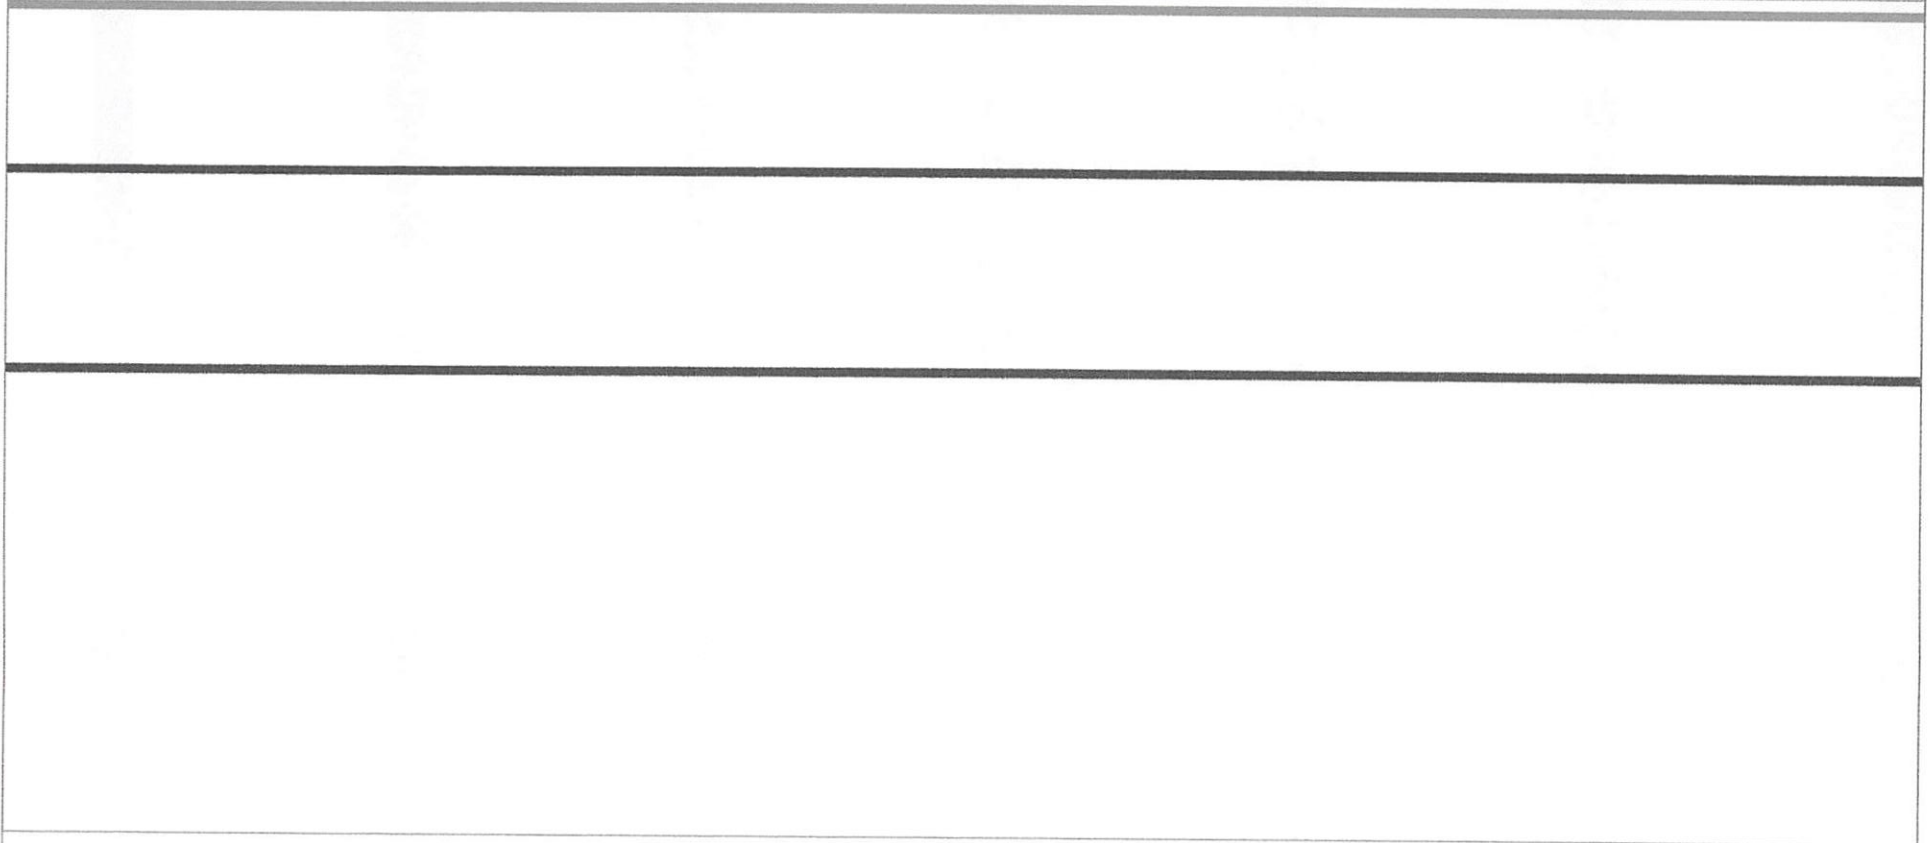


















Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			



Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			


12 Sep '21							19 Sep '21							26 Sep '21							3 Oct '21							10 Oct '21							17 Oct '21							24 Oct '21						
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S				
		Task		Rolled Up Baseline		Duration-only																																										
		Split		Rolled Up Baseline Milestone		Manual Summary Rollup																																										
		Milestone		Rolled Up Progress		Manual Summary																																										
		Baseline Milestone		Baseline Split		Start-only																																										
		Summary		External Tasks		Finish-only																																										
		Project Summary		External Milestone		Deadline																																										
		Group By Summary		Inactive Task		Baseline																																										
		Rolled Up Task		Inactive Milestone		Progress																																										
		Rolled Up Milestone		Inactive Summary																																												
		Baseline Summary		Manual Task																																												

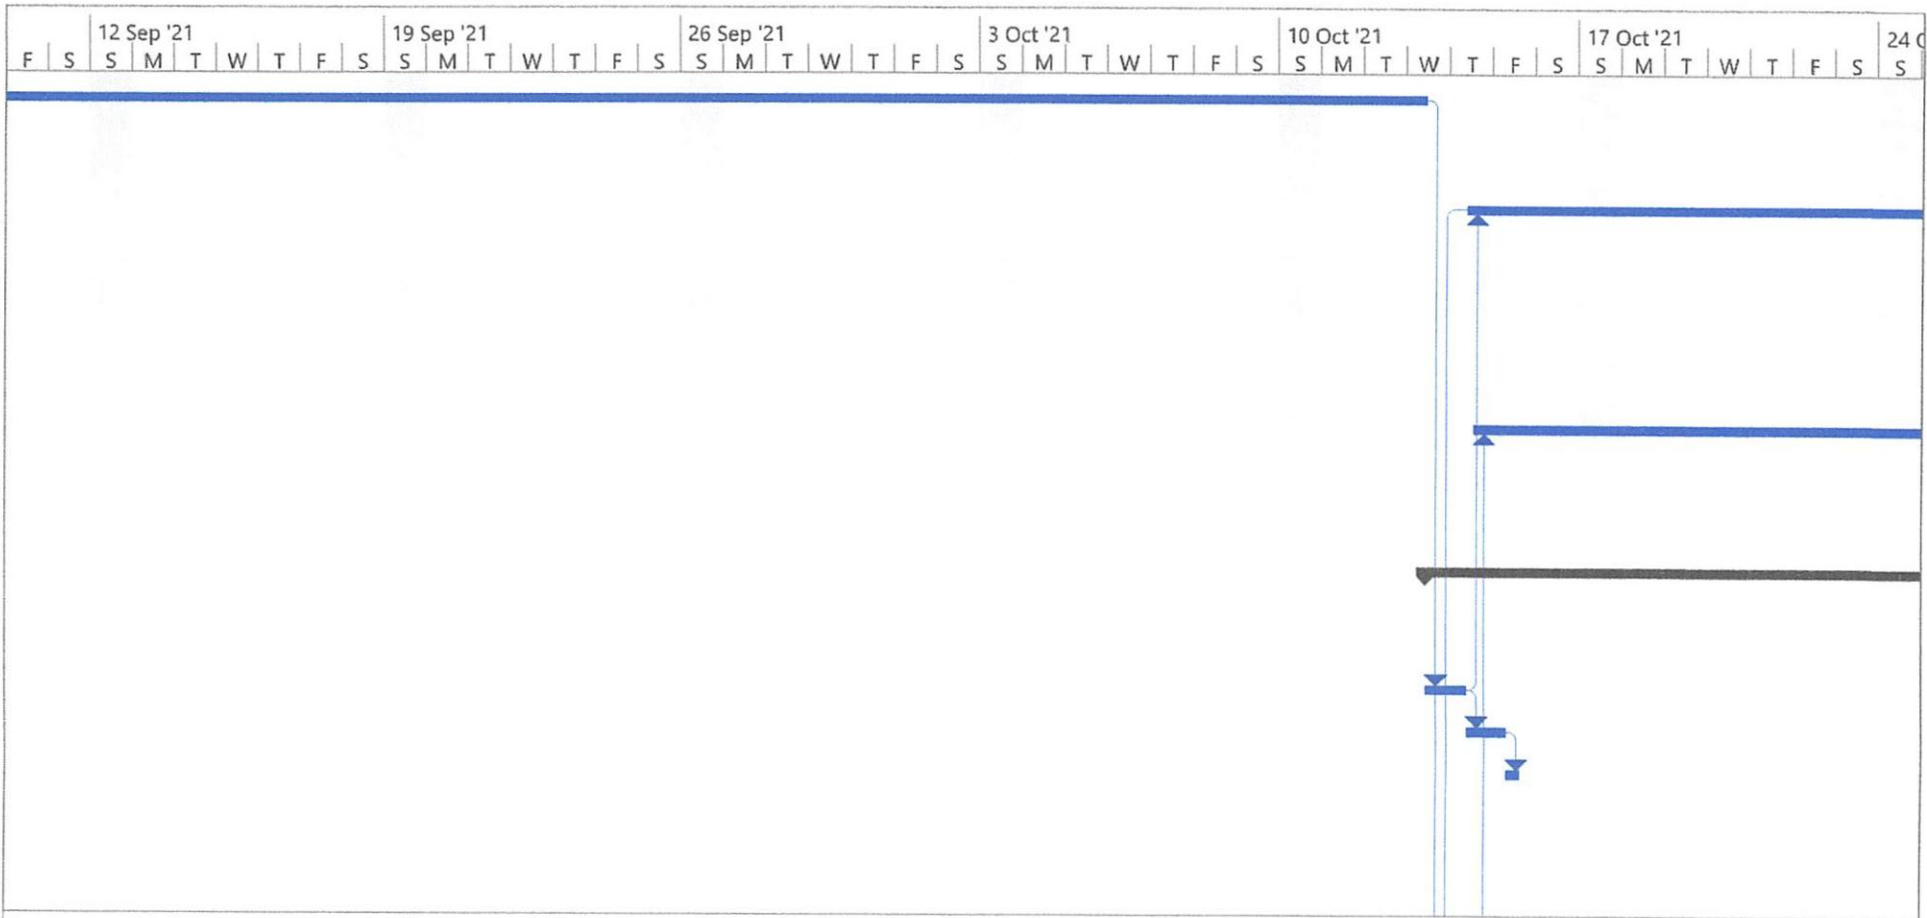


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

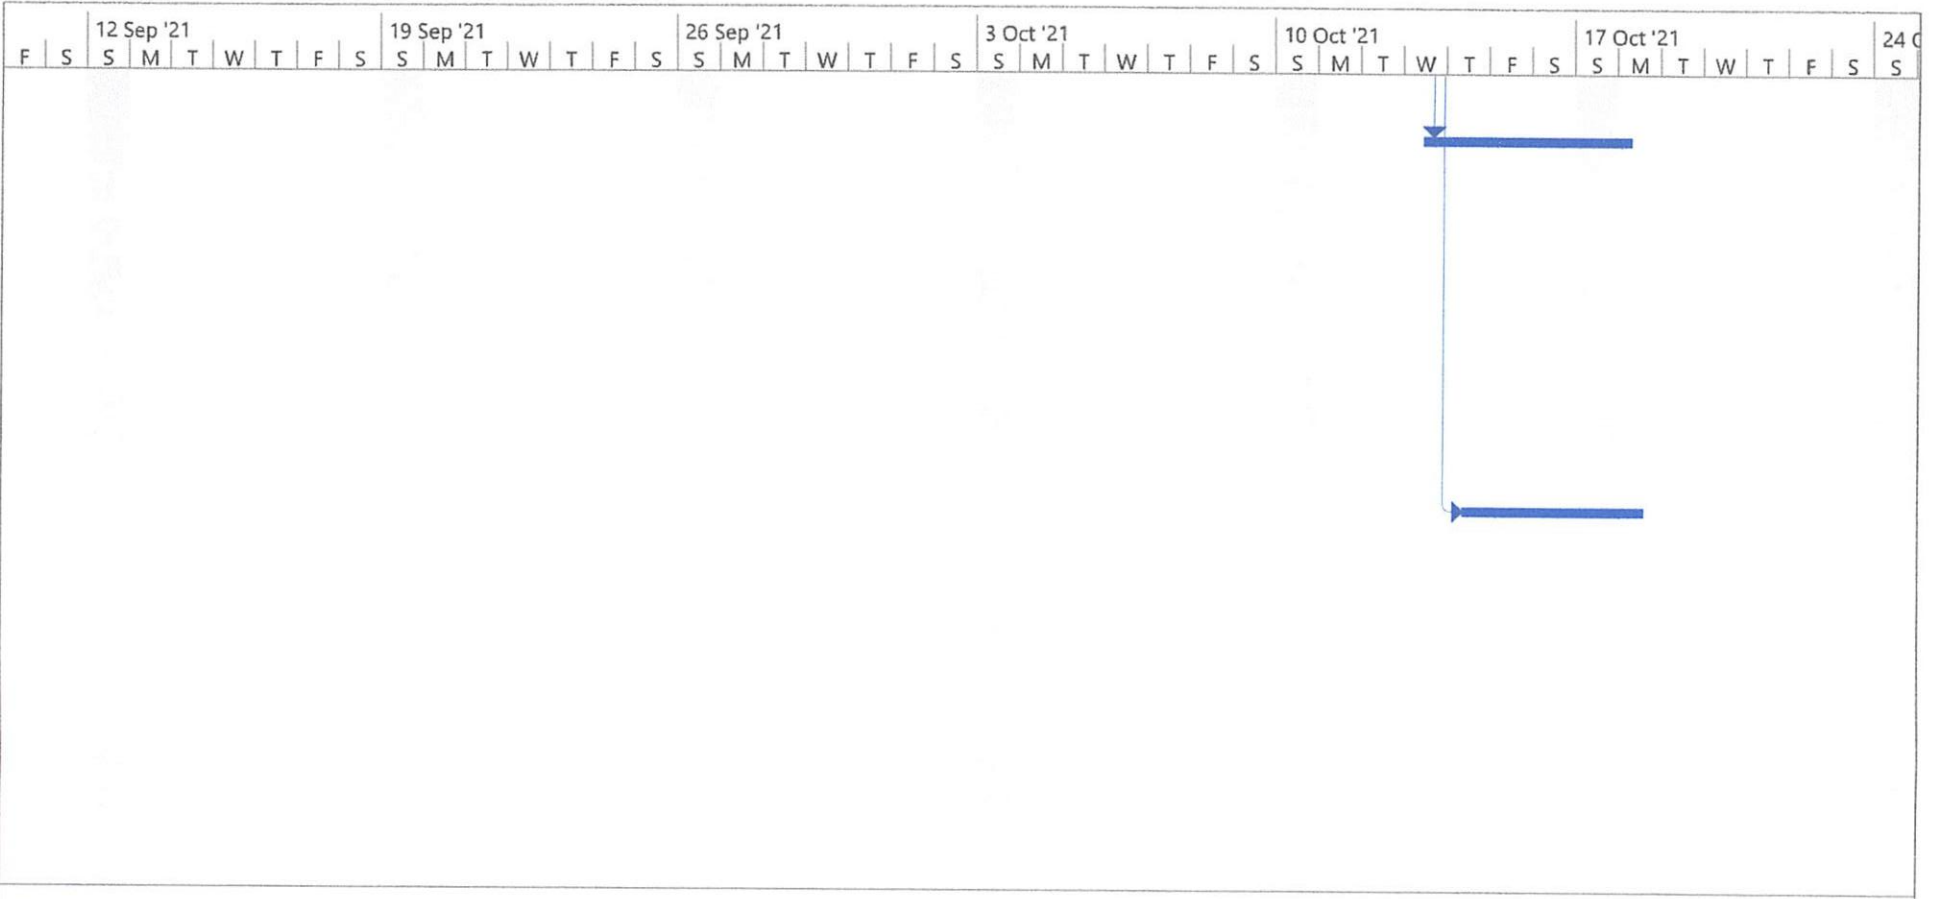

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

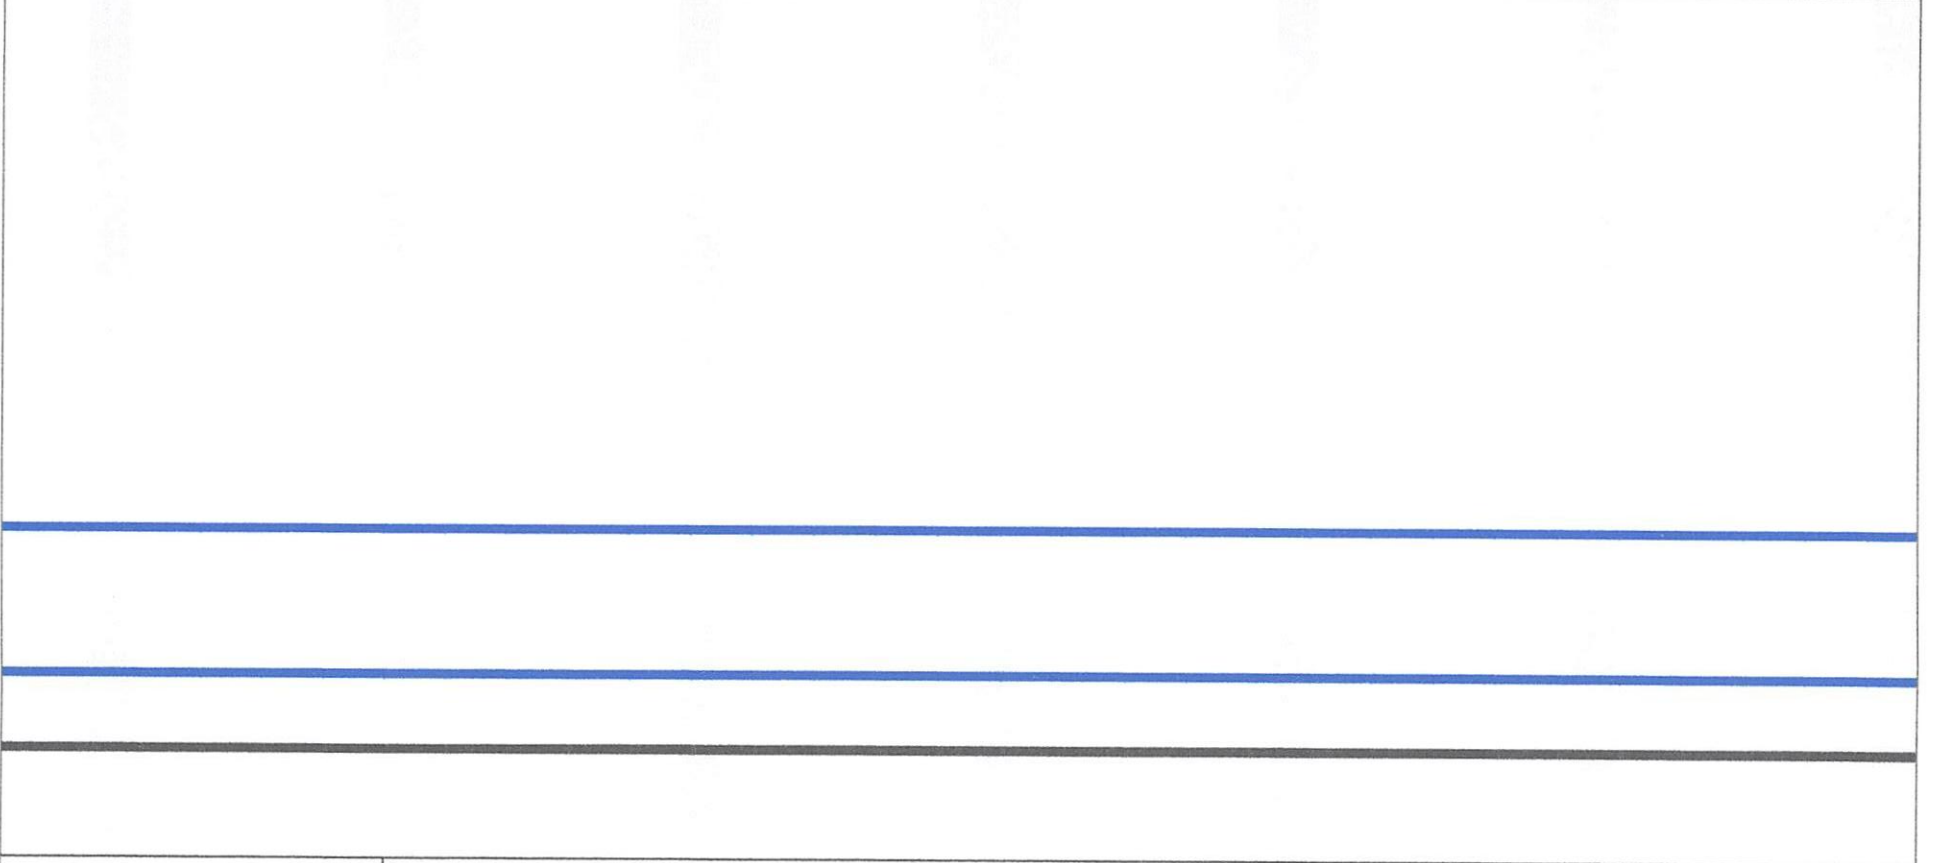


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			




Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			


Oct '21 | 31 Oct '21 | 7 Nov '21 | 14 Nov '21 | 21 Nov '21 | 28 Nov '21 | 5 Dec '21
M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W T F S S M T W

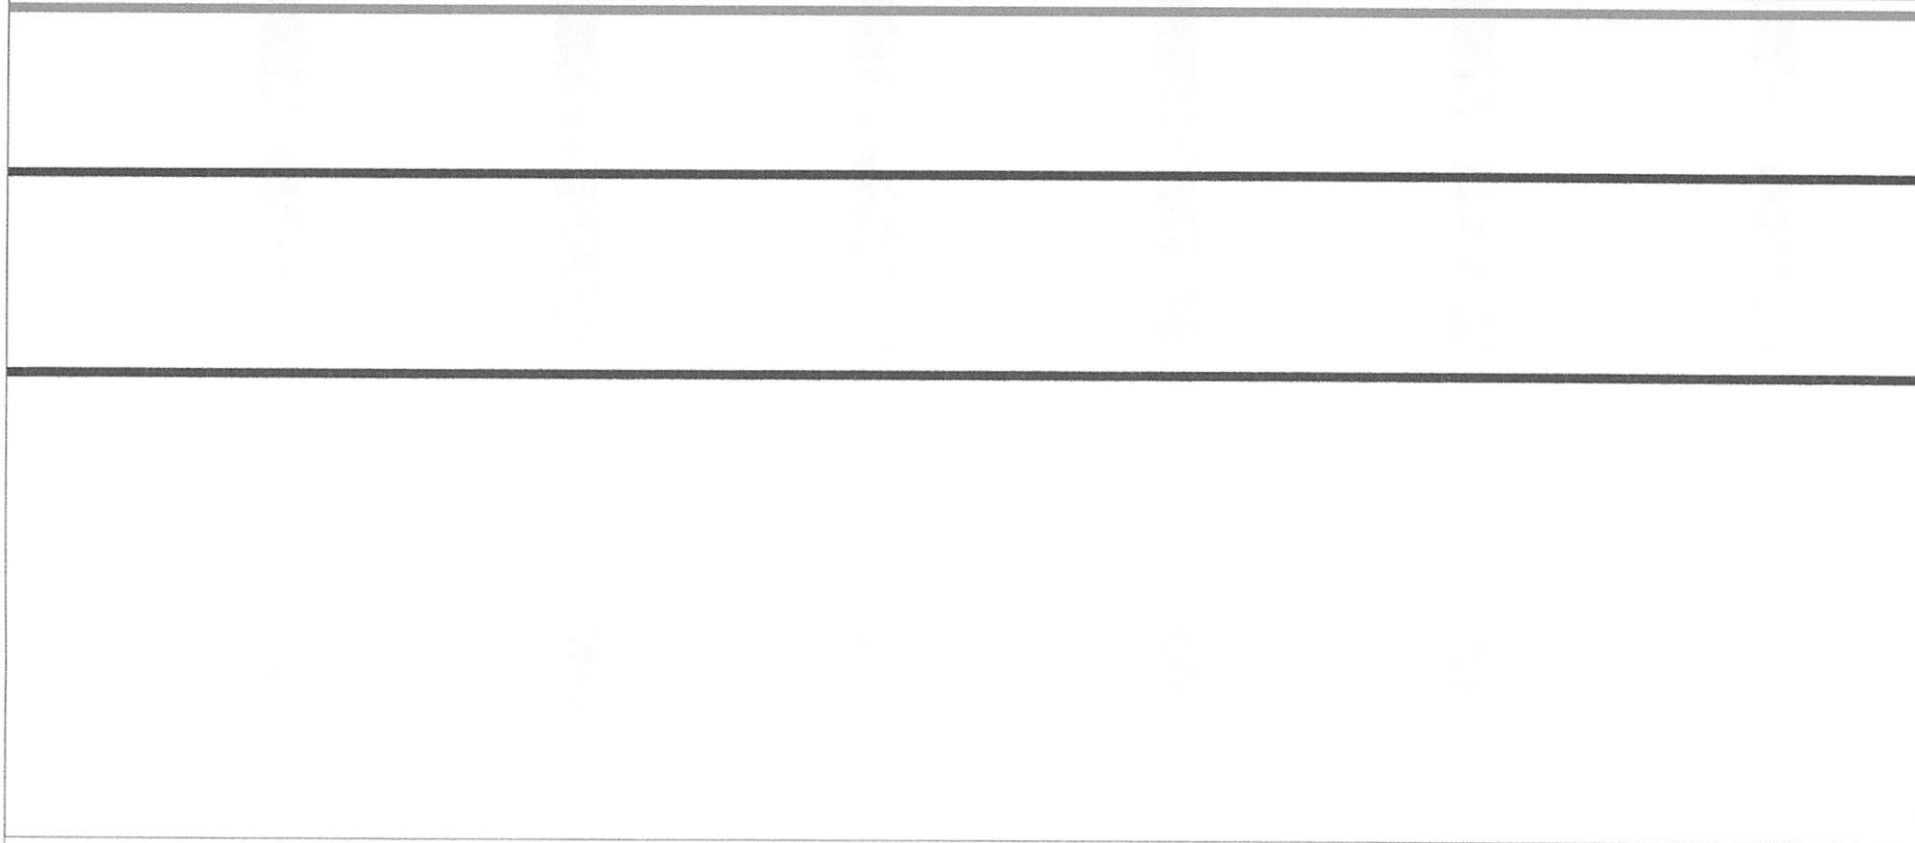


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

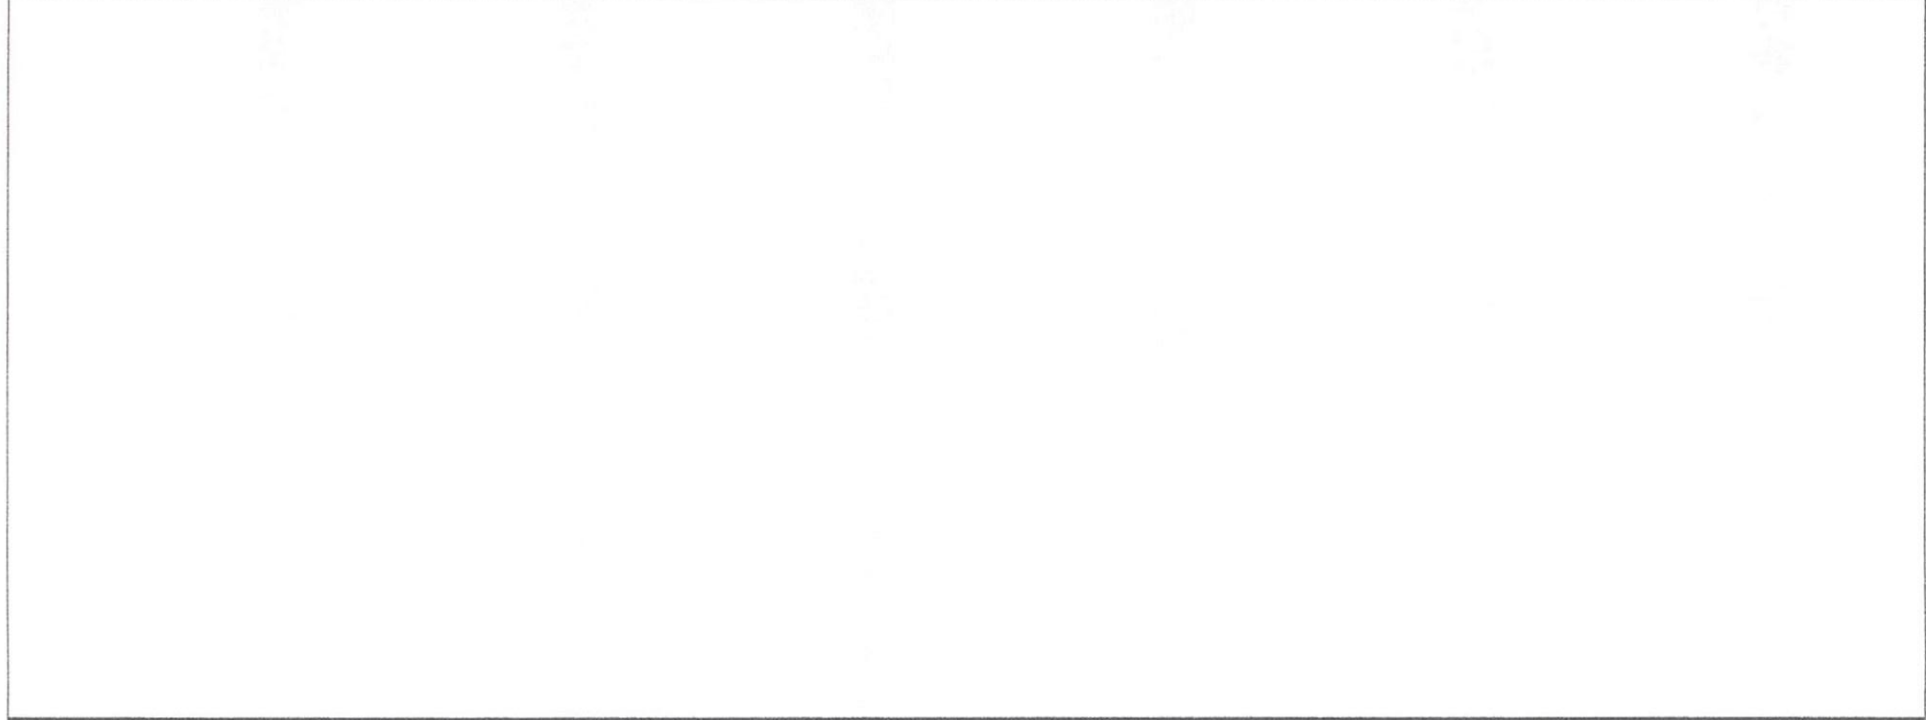


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

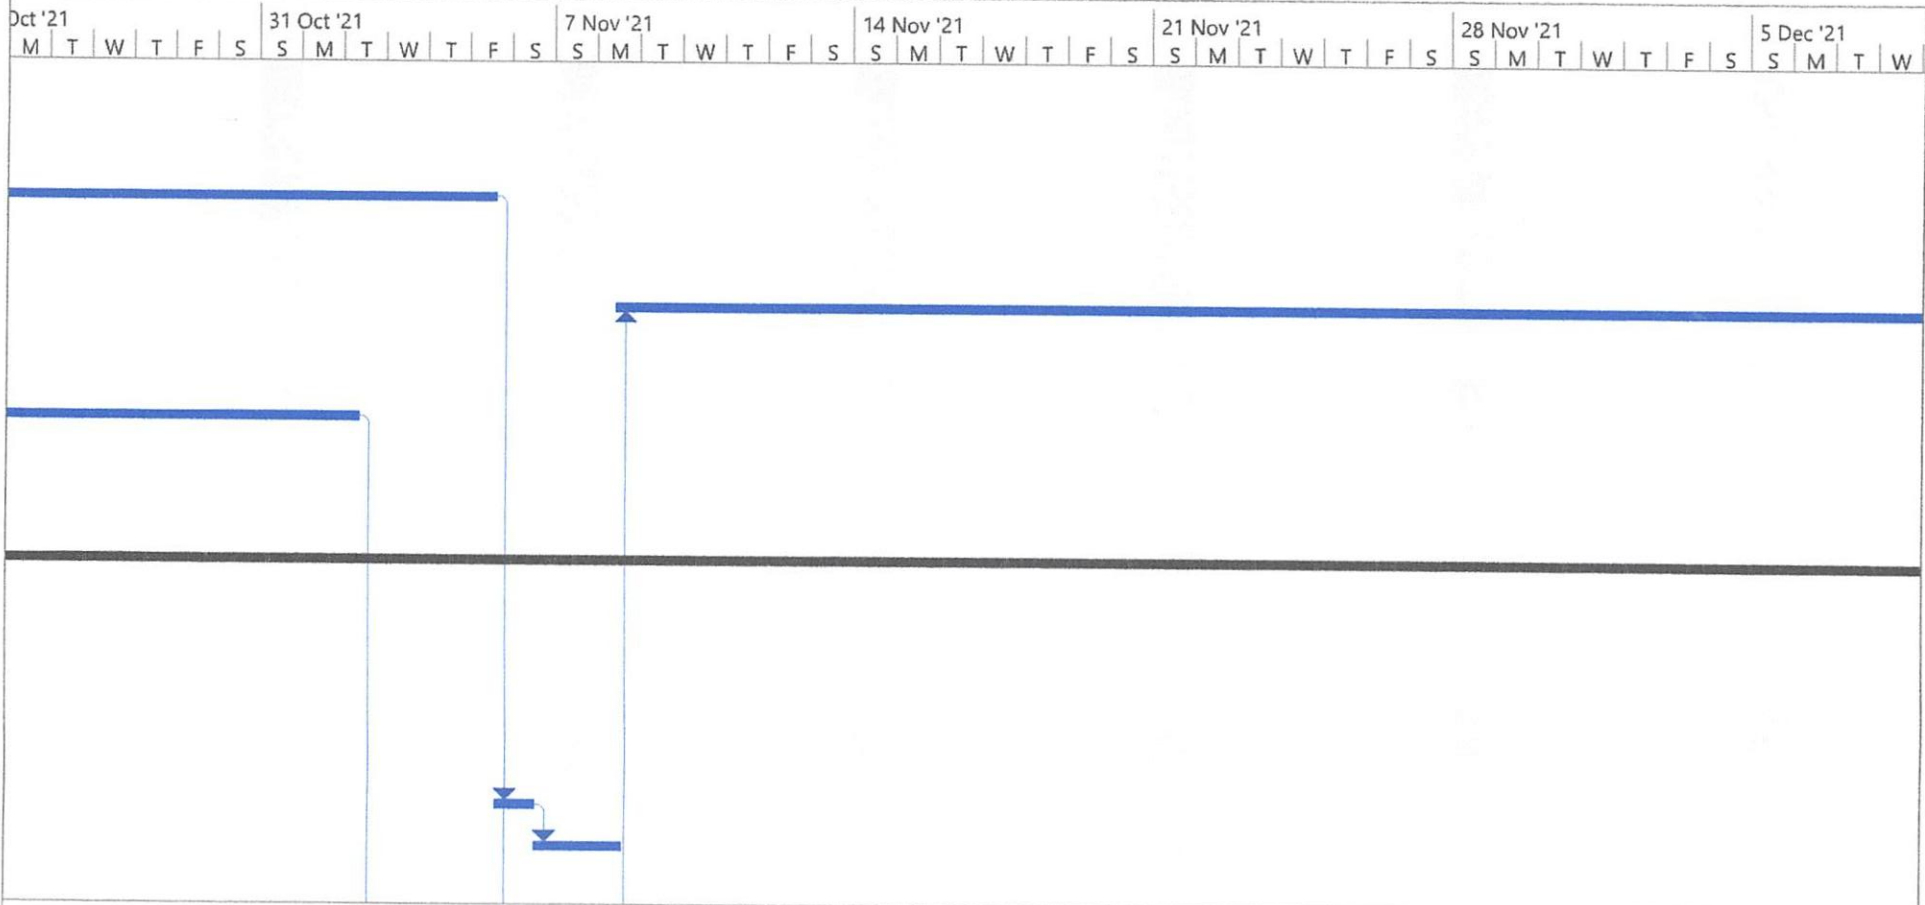

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

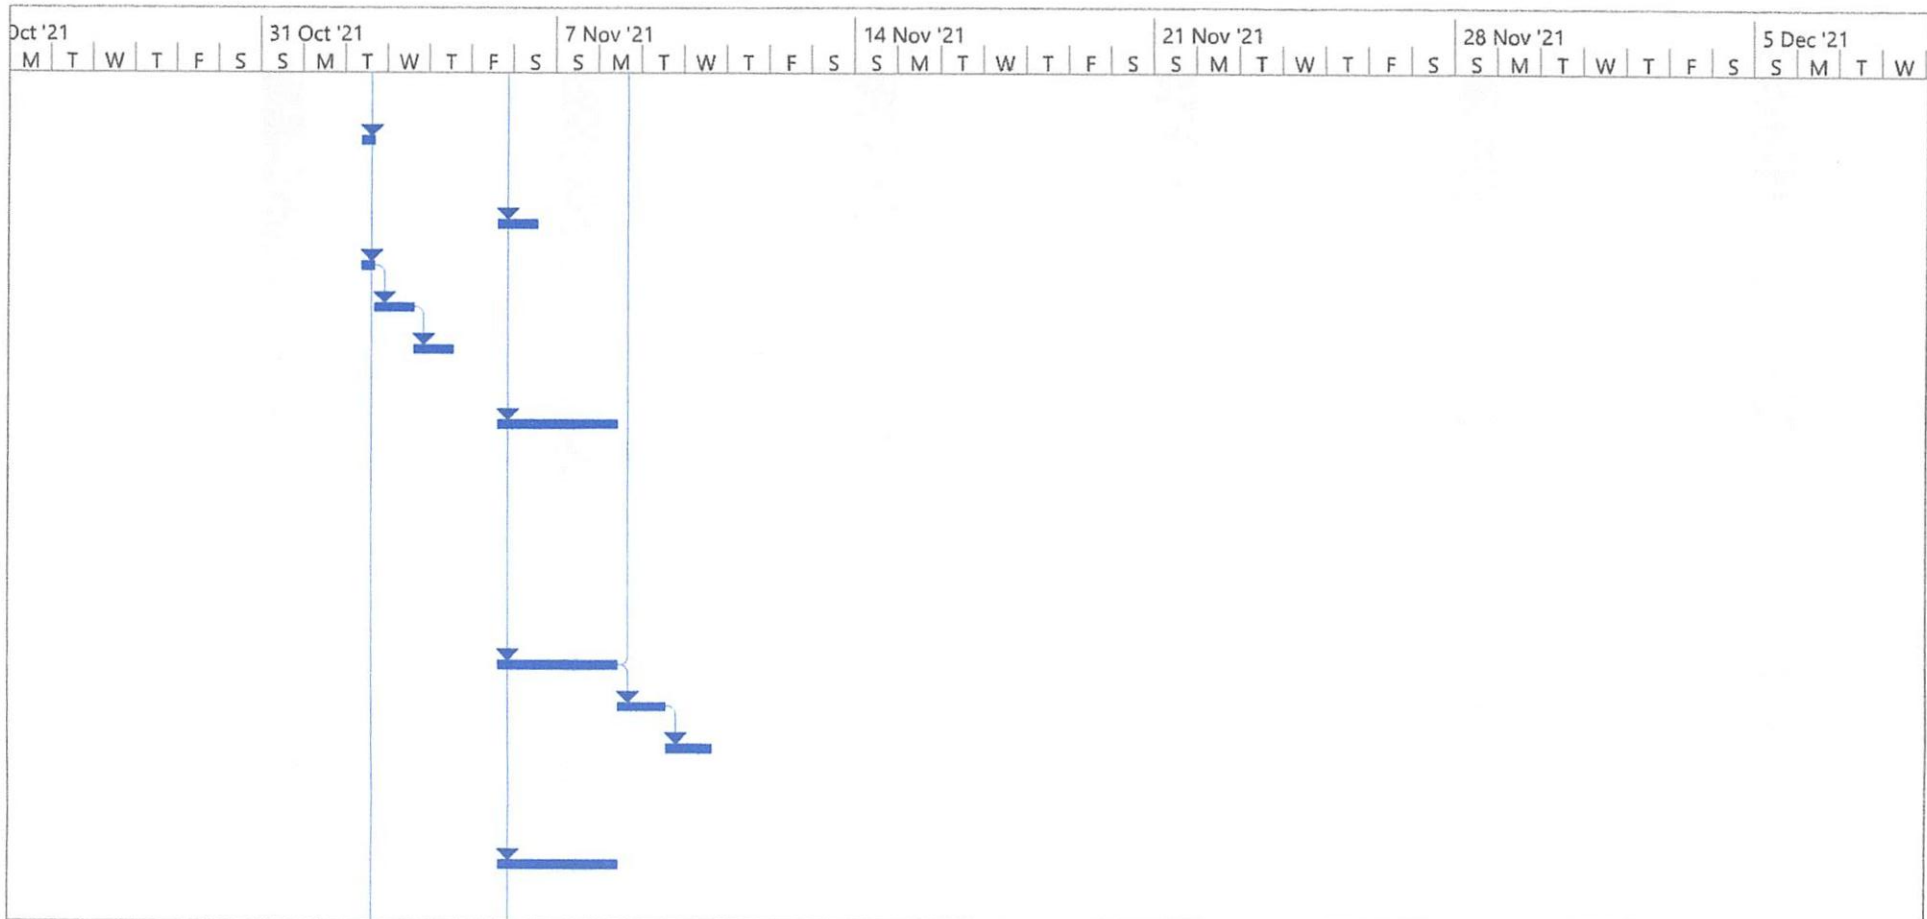


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

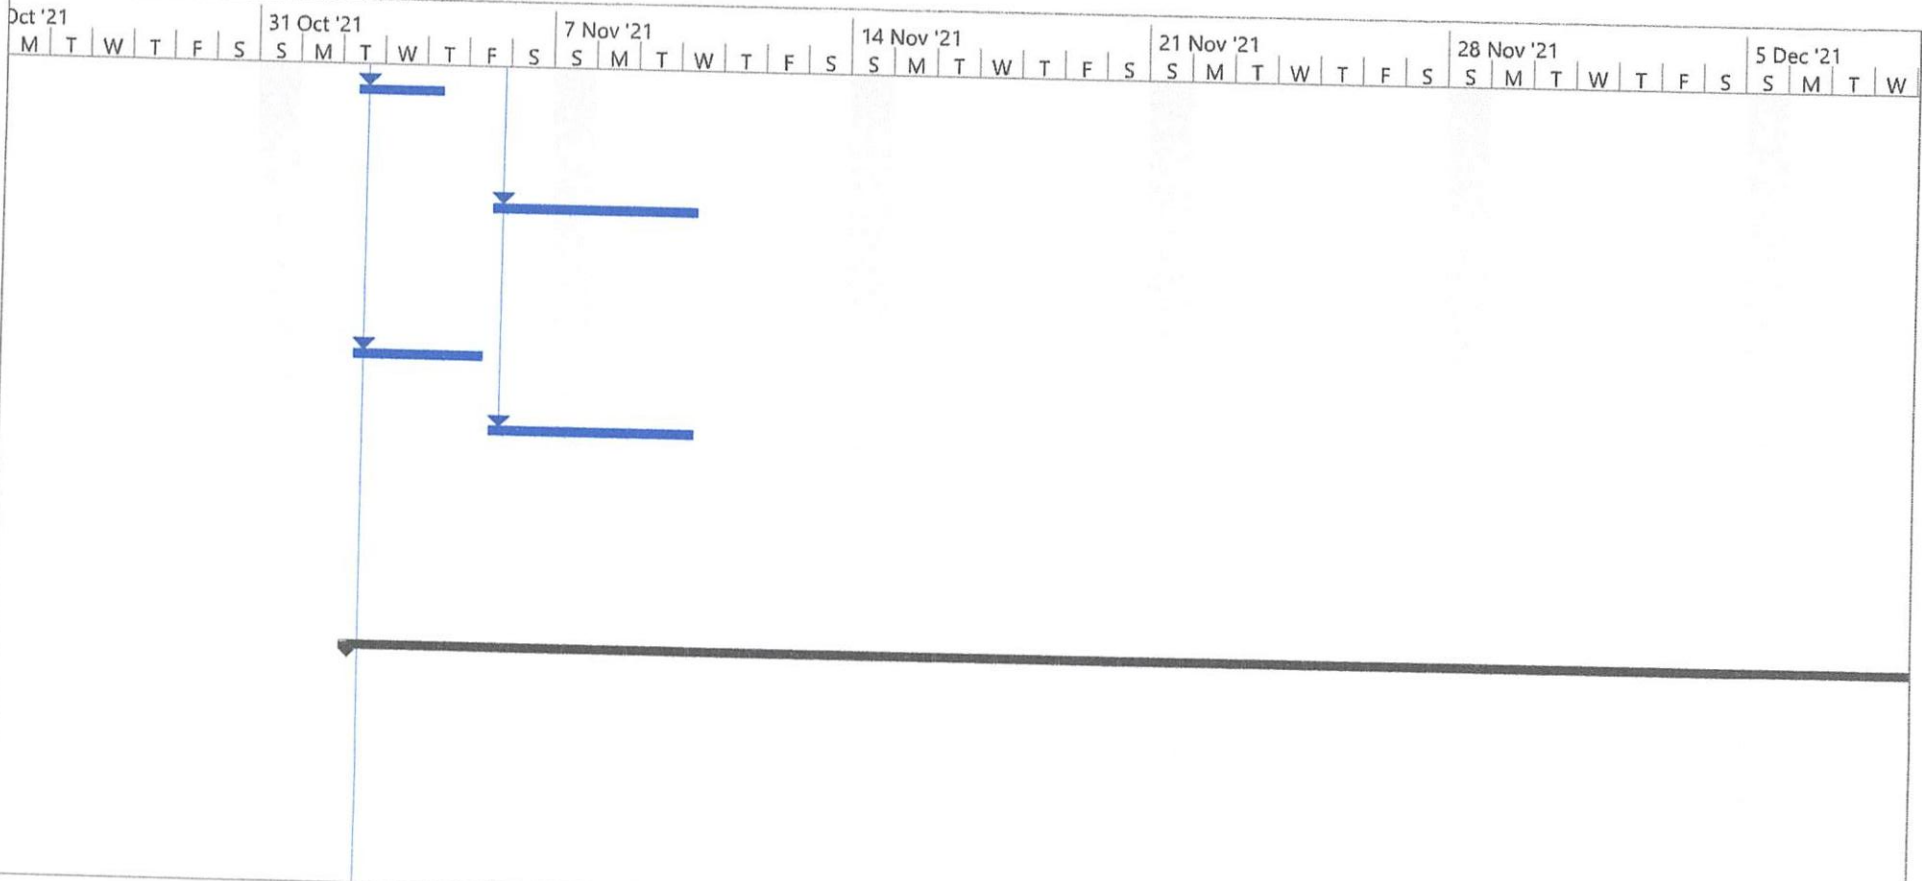


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			


Oct '21 M T W T F S 31 Oct '21 S M T W T F S 7 Nov '21 S M T W T F S 14 Nov '21 S M T W T F S 21 Nov '21 S M T W T F S 28 Nov '21 S M T W T F S 5 Dec '21 S M T W

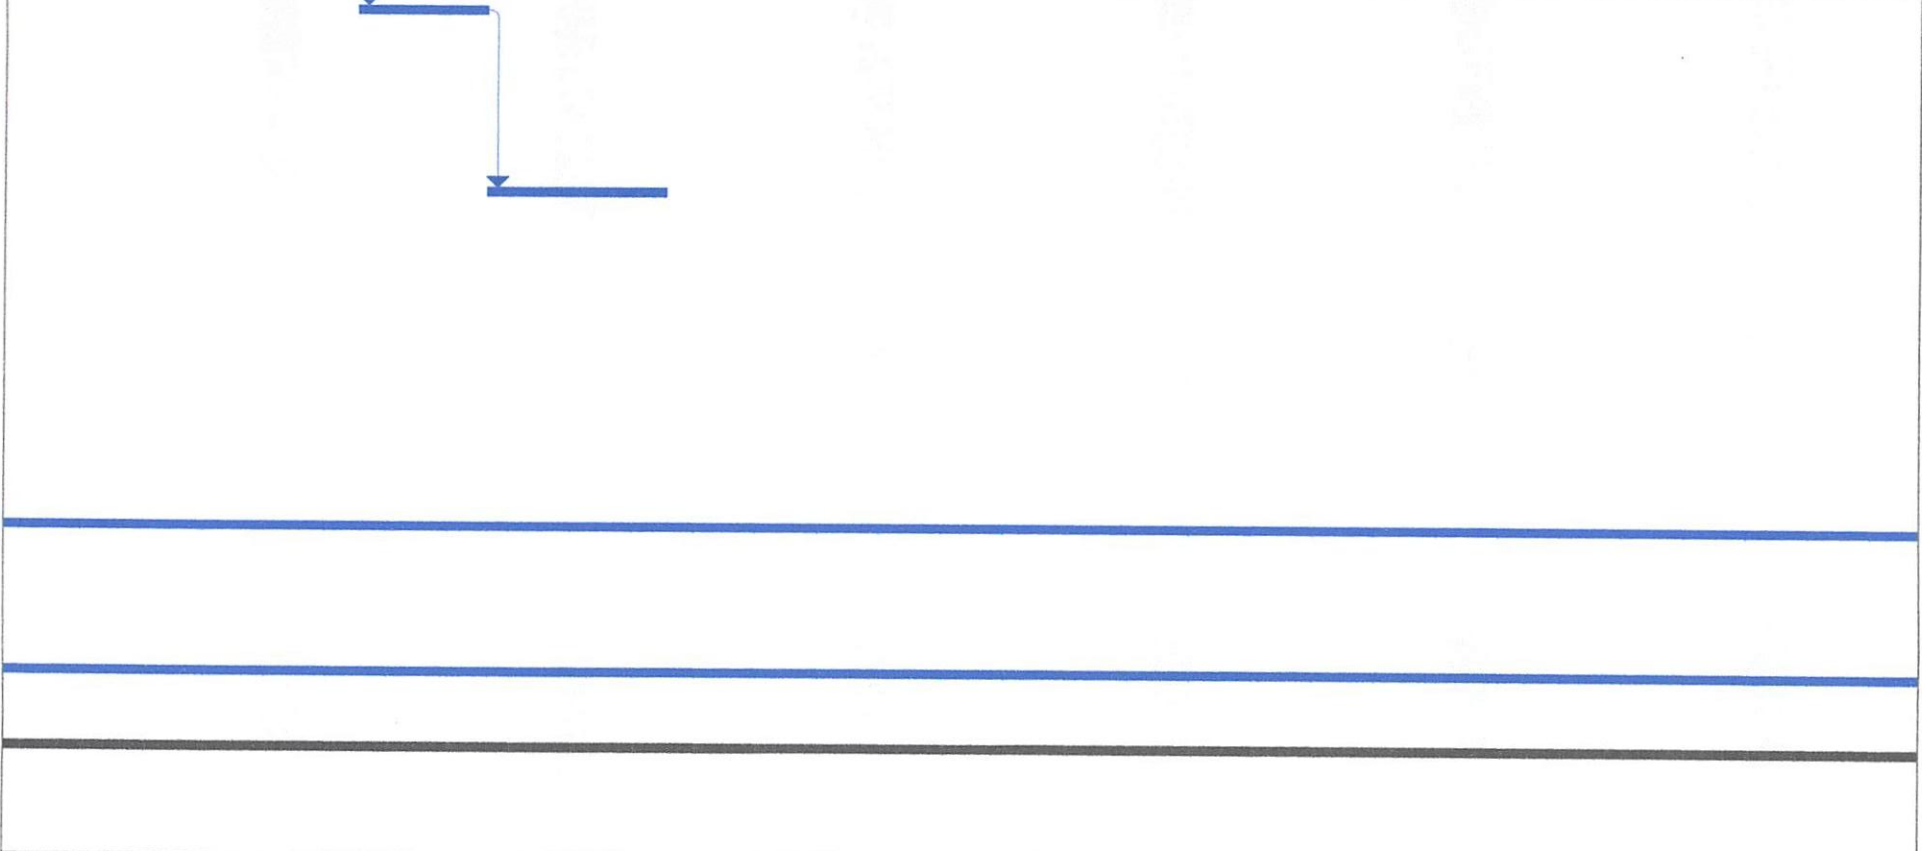


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

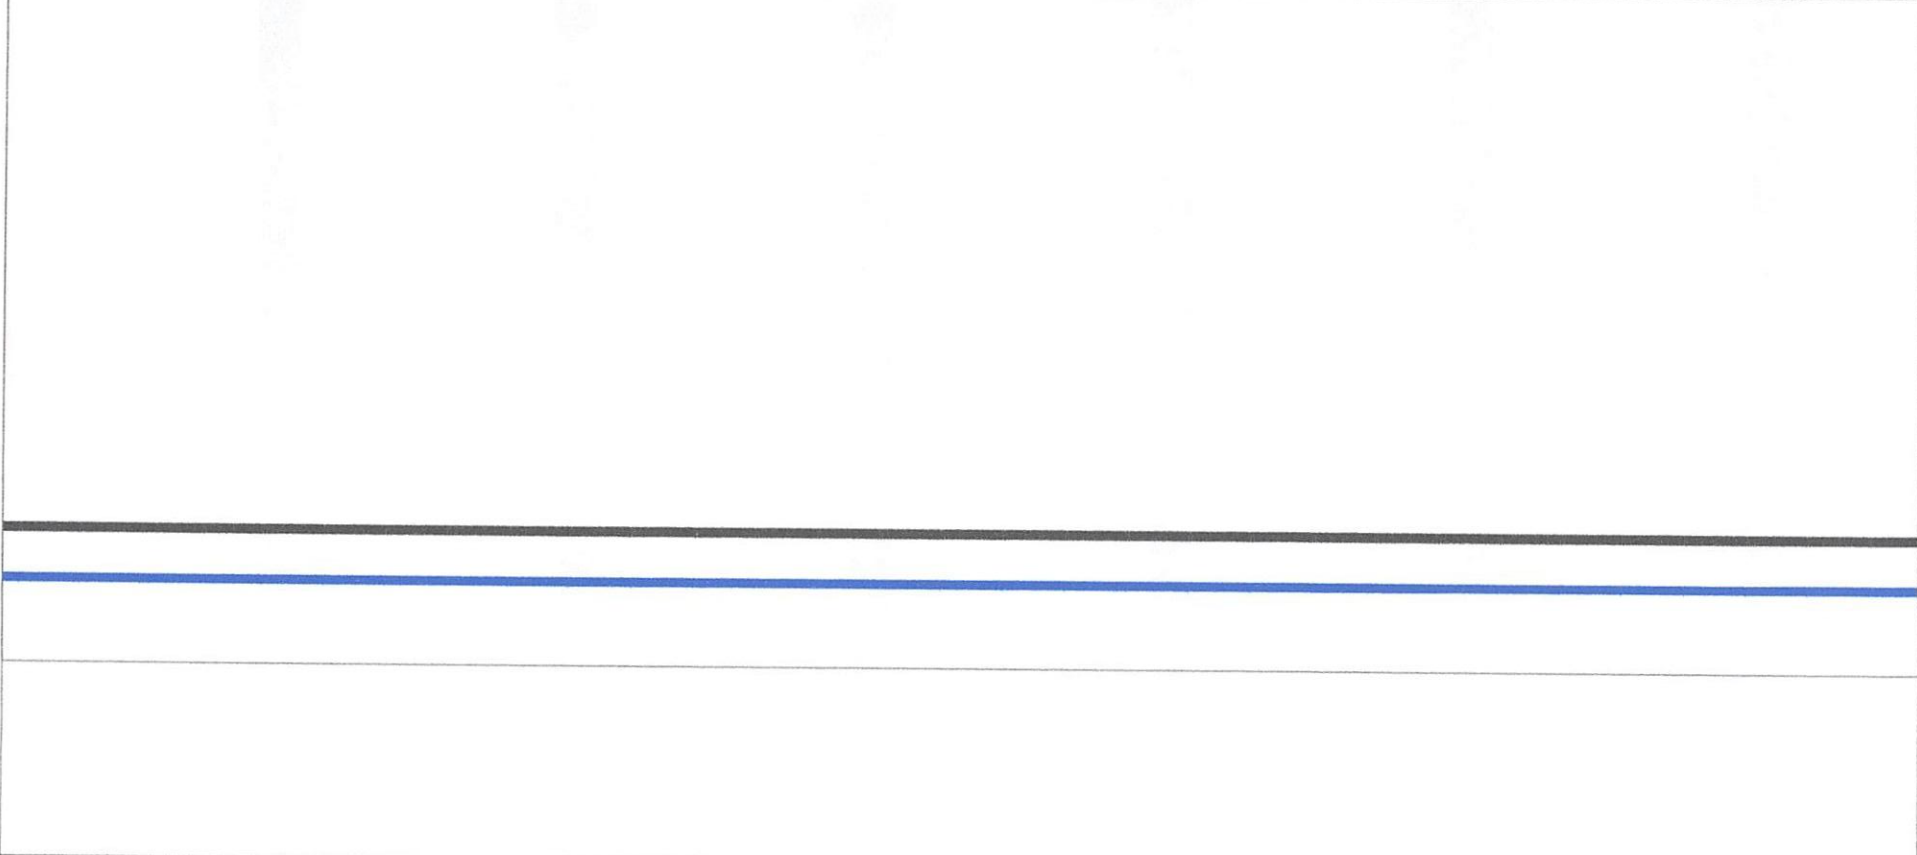


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

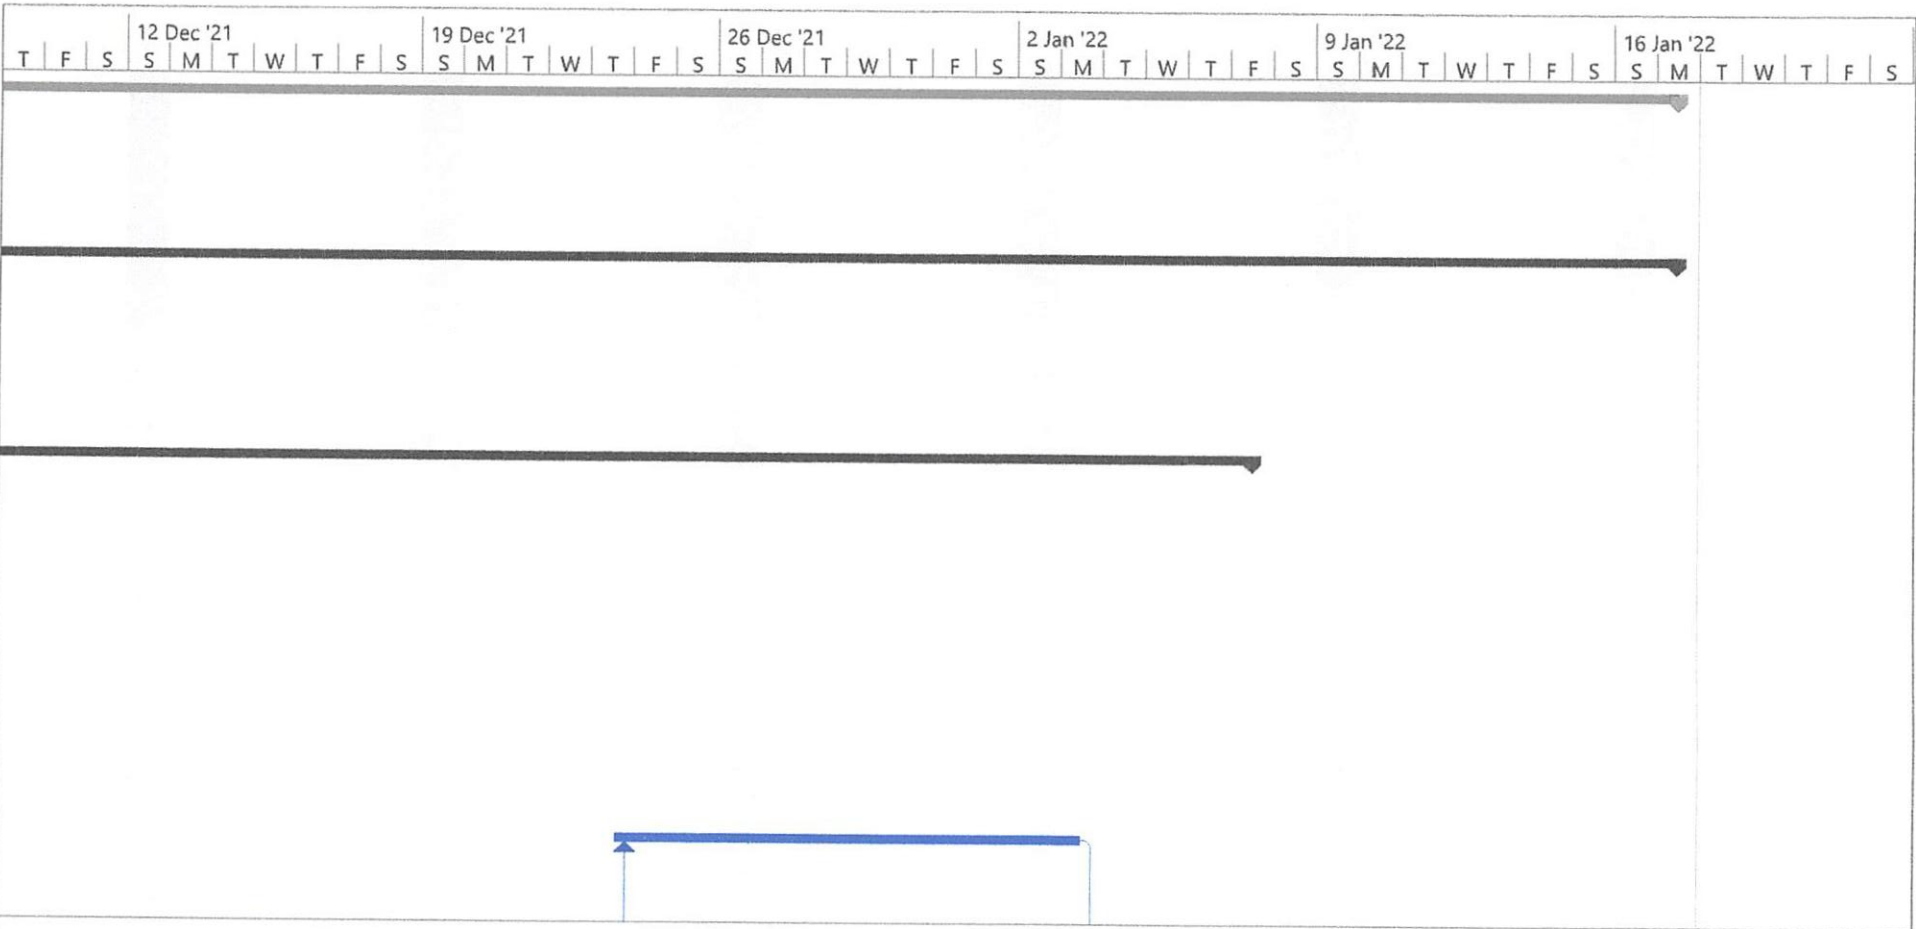


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

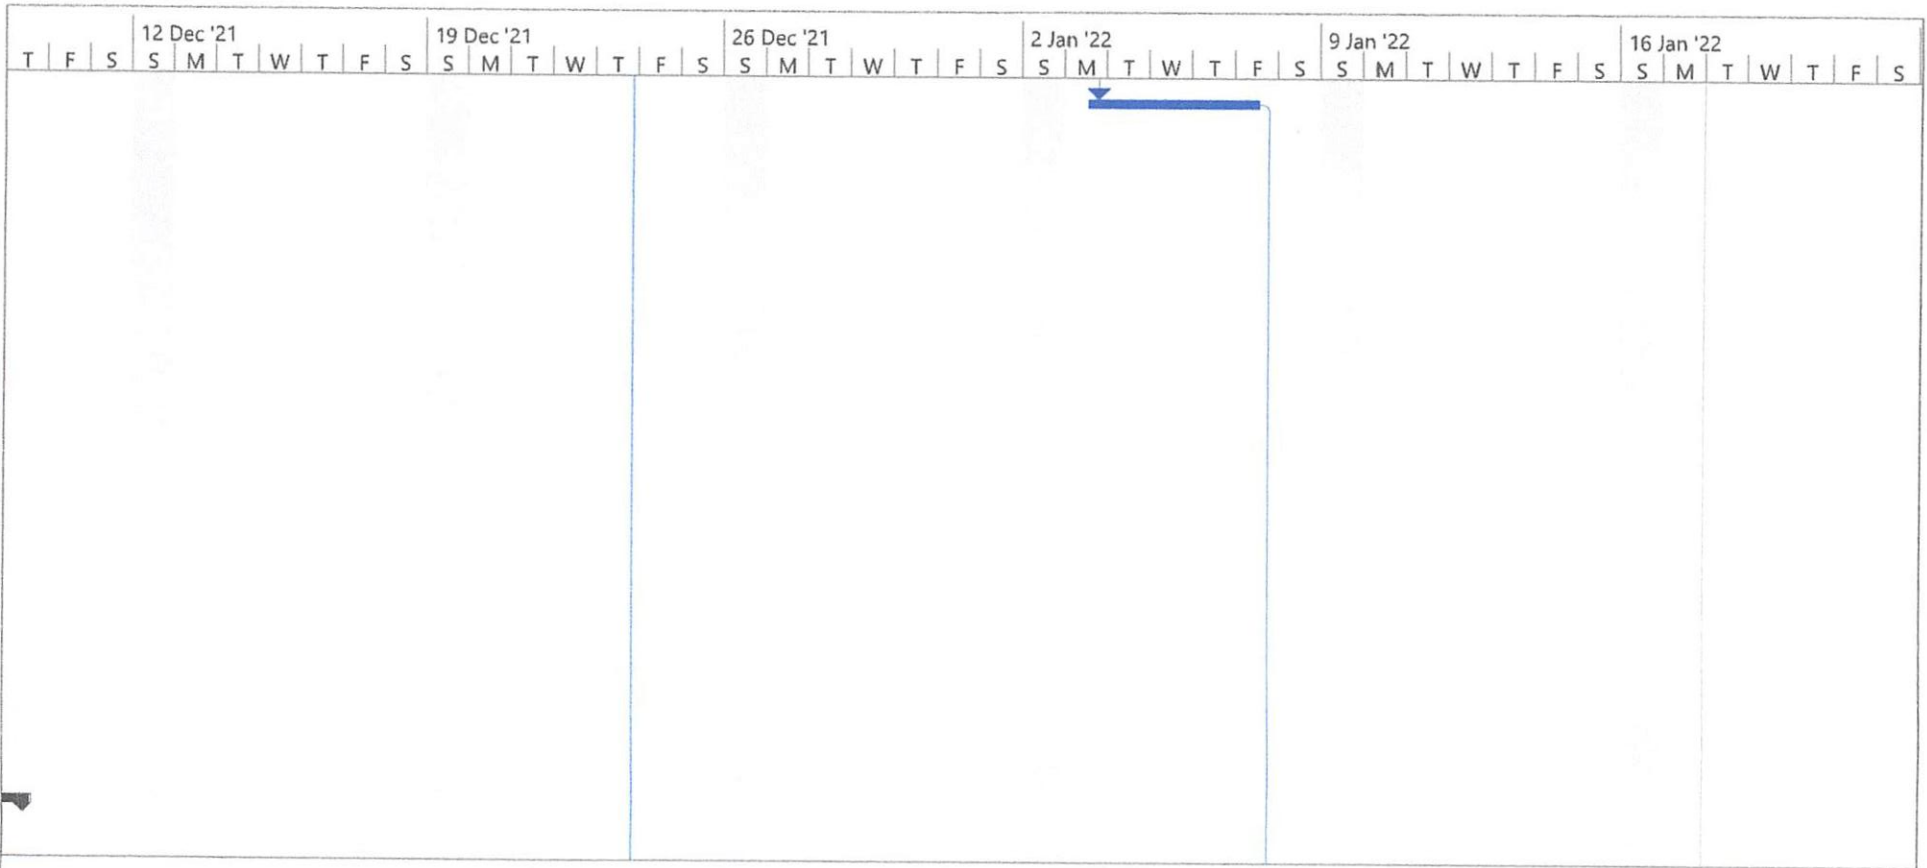


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

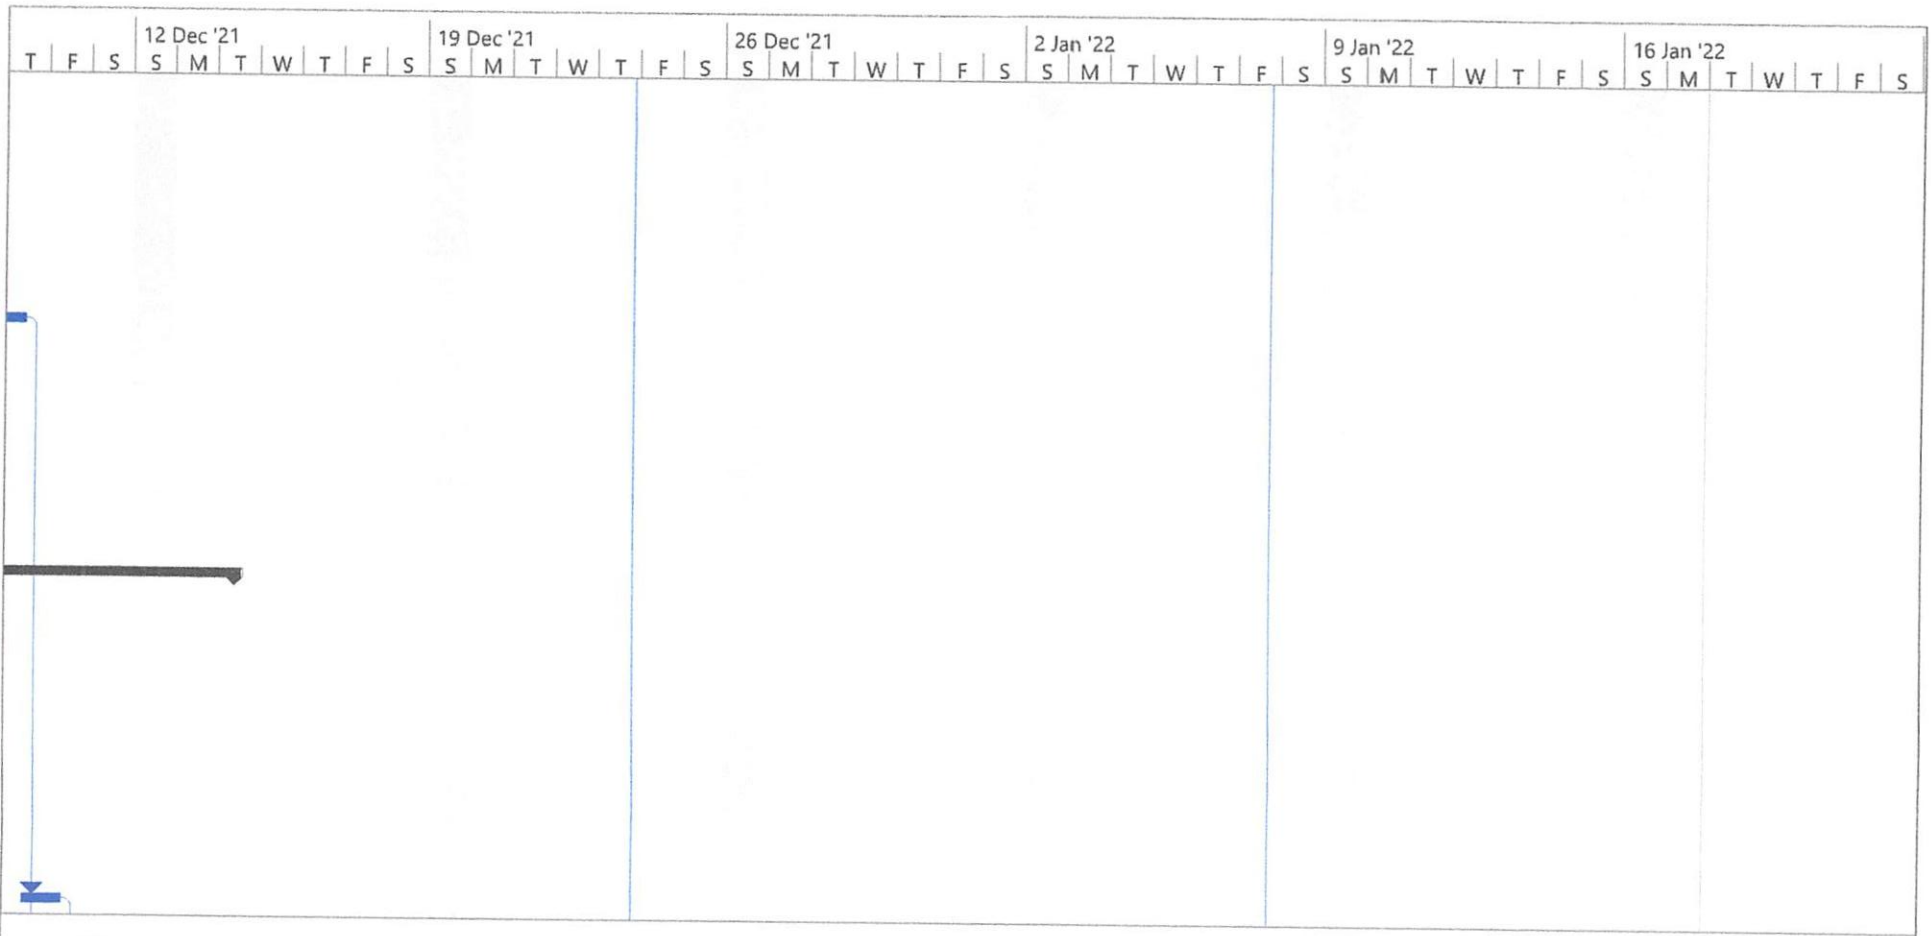


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

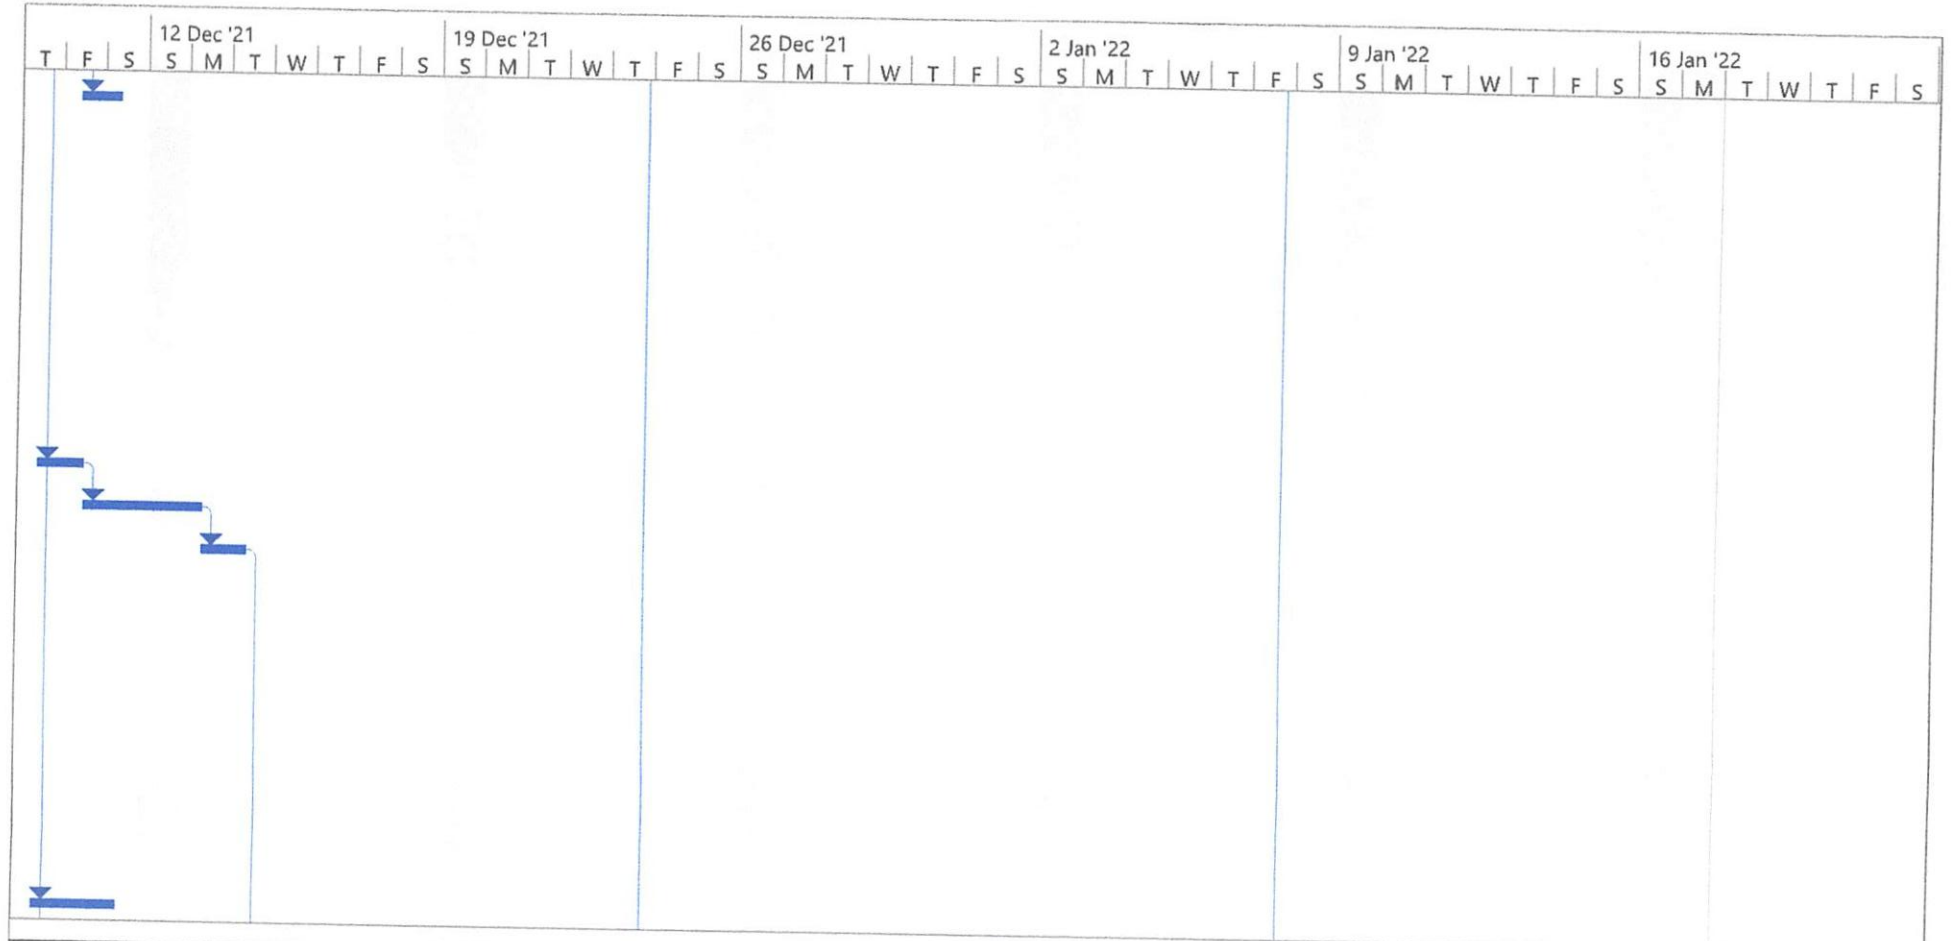


Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

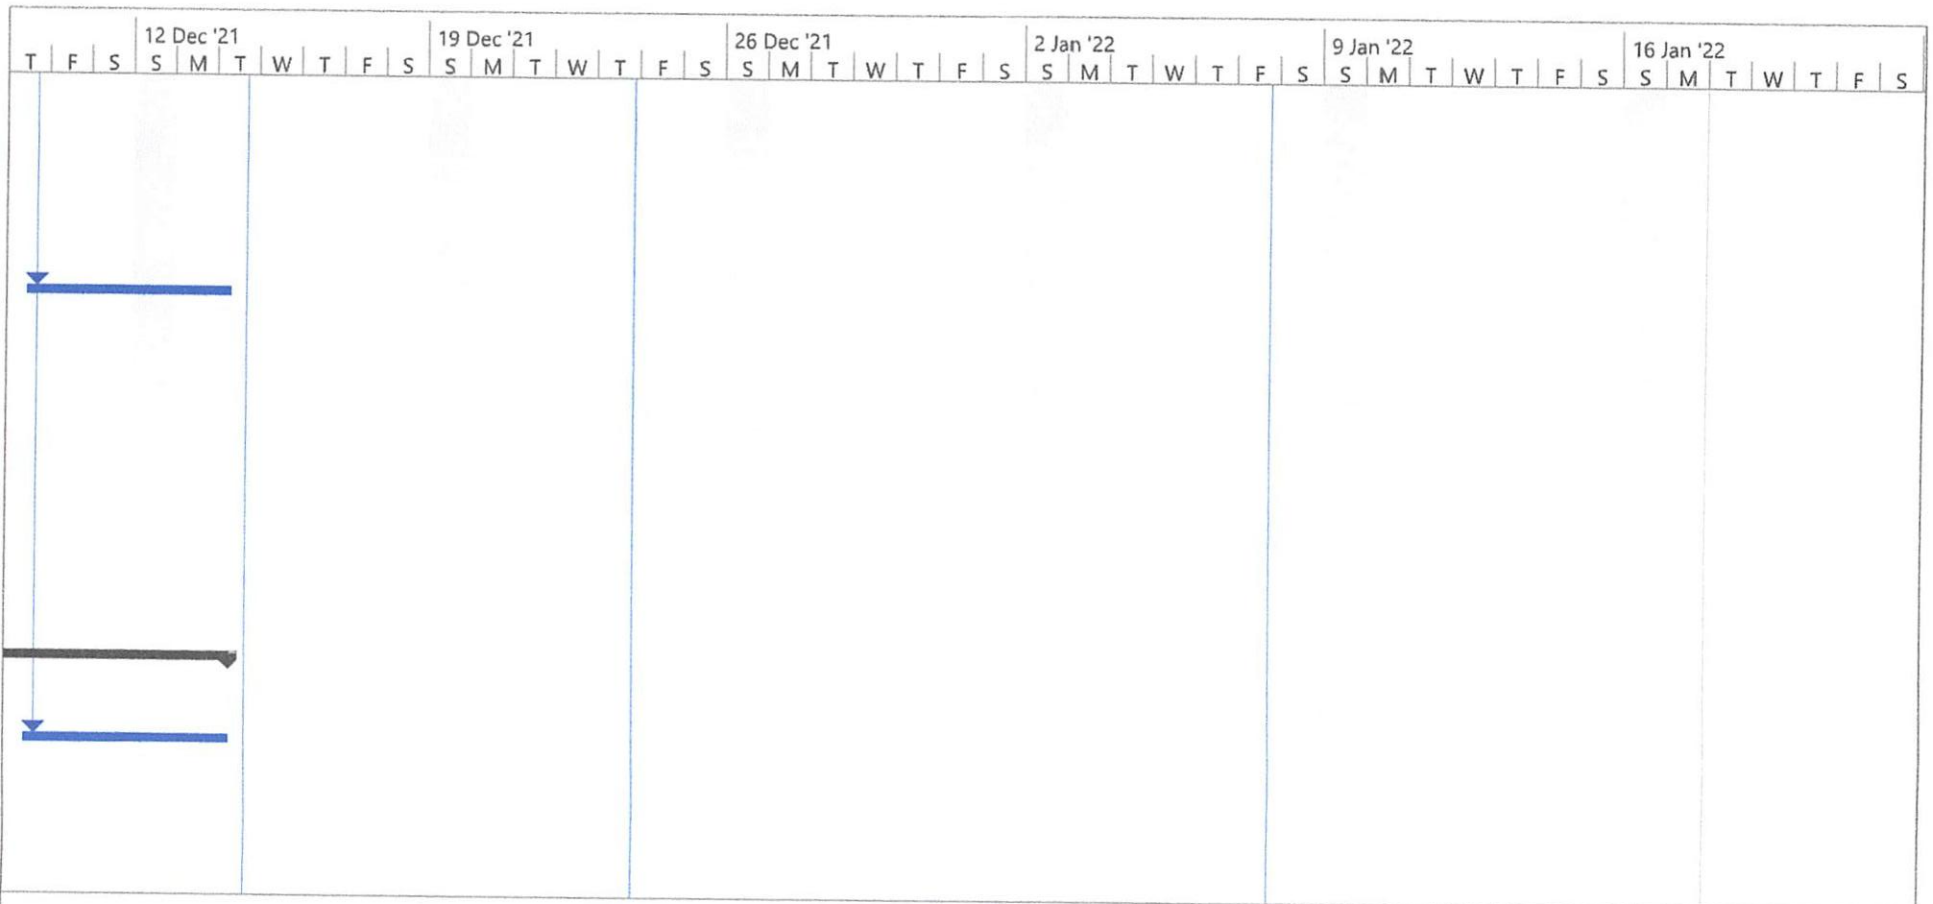

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

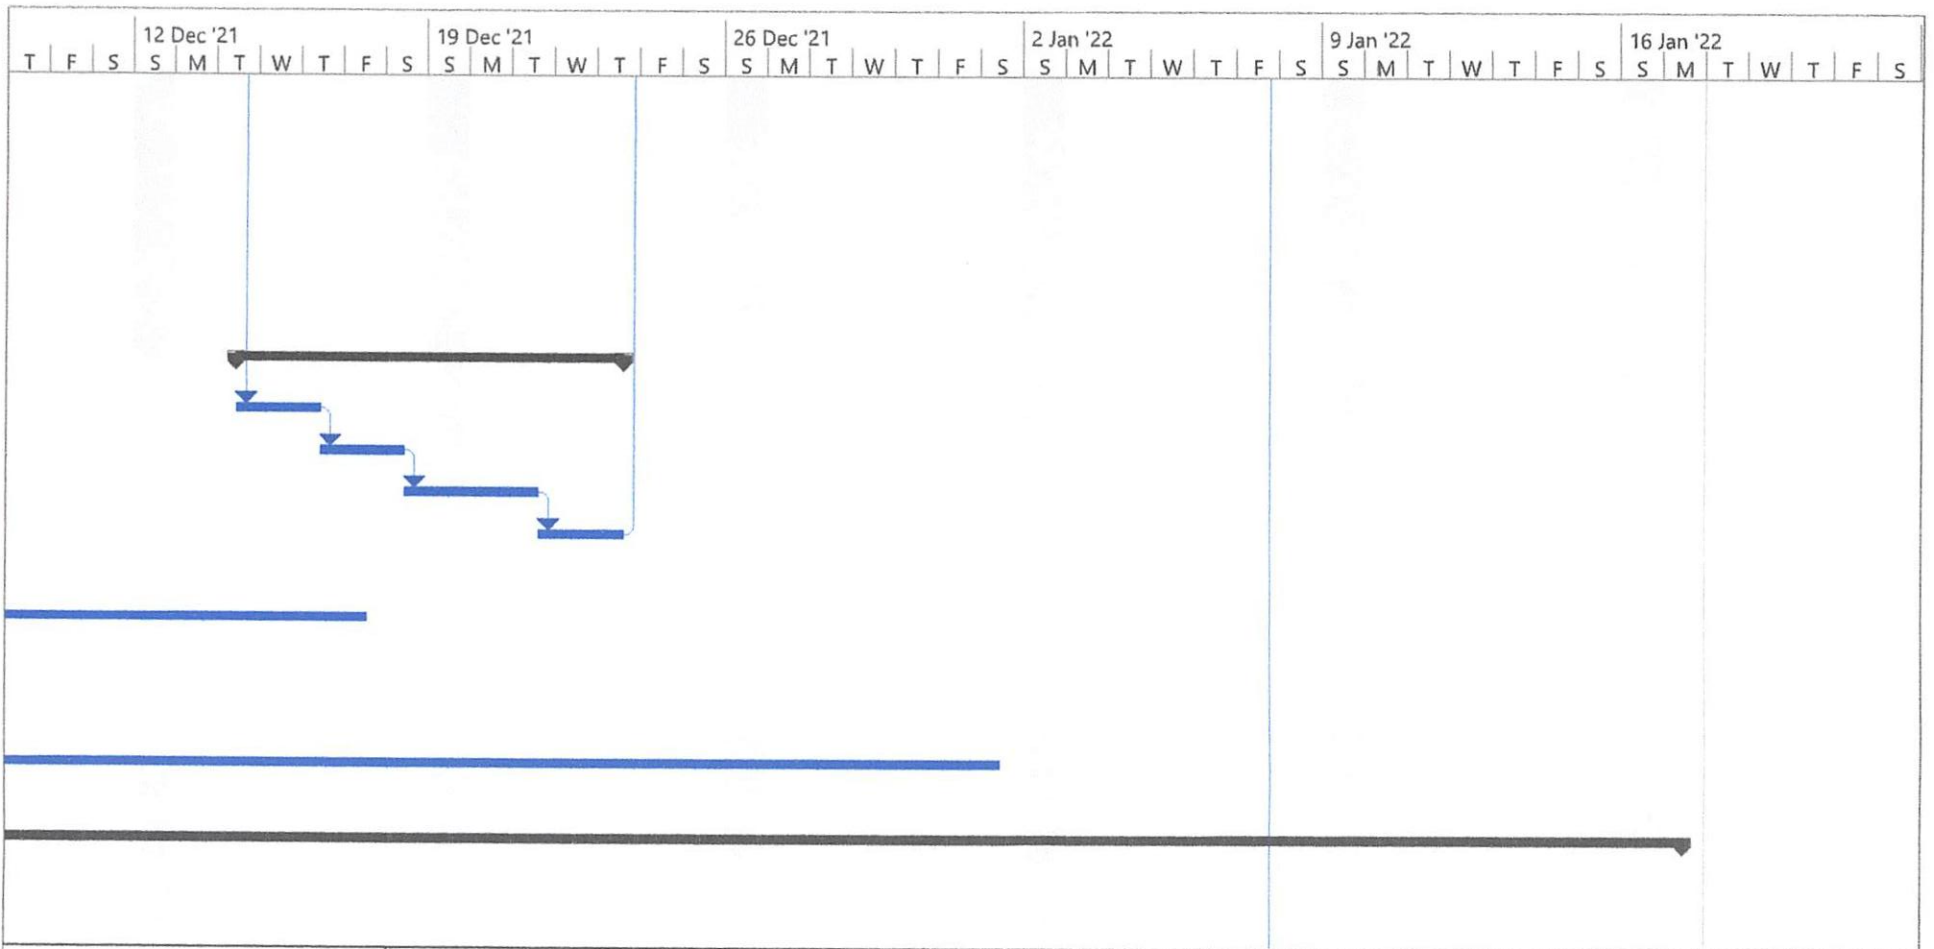

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			

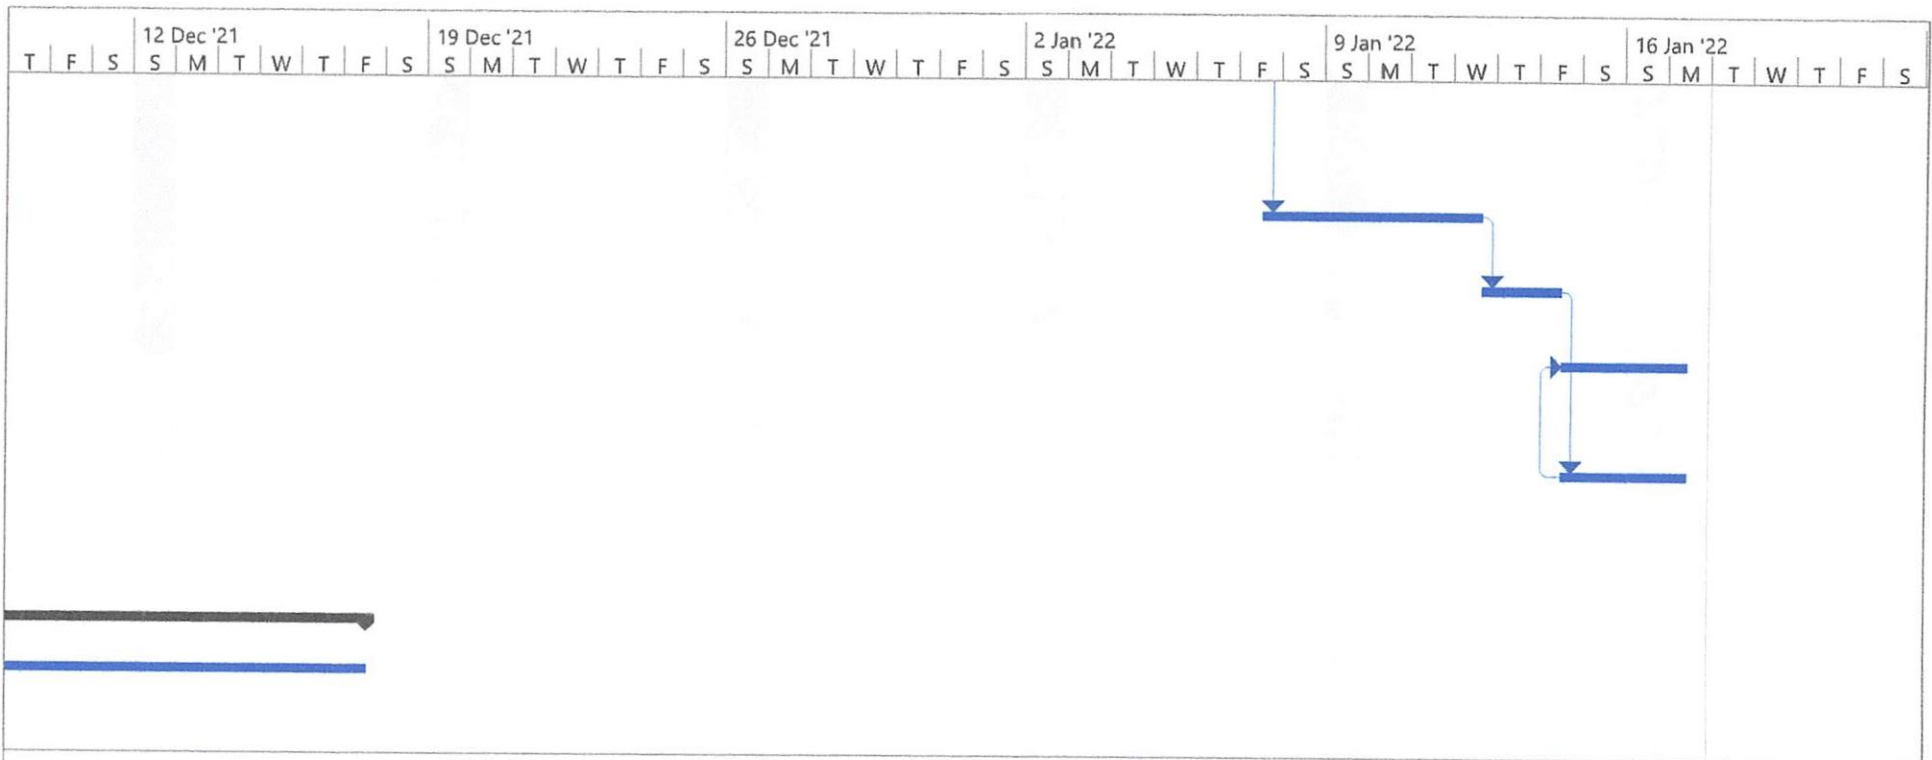

Task		Rolled Up Baseline		Duration-only	
Split		Rolled Up Baseline Milestone		Manual Summary Rollup	
Milestone		Rolled Up Progress		Manual Summary	
Baseline Milestone		Baseline Split		Start-only	
Summary		External Tasks		Finish-only	
Project Summary		External Milestone		Deadline	
Group By Summary		Inactive Task		Baseline	
Rolled Up Task		Inactive Milestone		Progress	
Rolled Up Milestone		Inactive Summary			
Baseline Summary		Manual Task			
